

Project No. 1251-100
Crude Oil Tank Farms Project, Agrood Area 30 (Module-1)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

Sr.	Pre-Commissioning and Commissioning Dossier Index	Applicable (Yes/No)
1	Mechanical Completion Certificate (MCC)	
2	Ready for Startup Certificate (RFSU)	
3	System Punch Lists	
4	System Limits Marked Up P&ID	
5	System Index	
6	Piping Pre-Commissioning	
	6.01) Piping Test Packs	
	6.02) Piping Pre-commissioning Check Lists	
7	Piping Commissioning	
	7.01) Service Test, GLT, CLT and N2 Purging Certificates	
	7.02) Piping Commissioning Check Lists	
Sr.	Pre-Commissioning and Commissioning Dossier Index	Applicable (Yes/No)
8	Mechanical Pre-Commissioning	
	8.01) System Mechanical Index	
	8.02) Equipment Drawings	
	8.03) Equipment Datasheets	
	8.04) Boxing-up Certificates	

	8.05) Grouting Certificates	
	8.06) Pre-Alignment Certificates	
	8.07) Mechanical Pre-Commissioning Checklists	
9	Mechanical Commissioning	
	9.01) Final Alignment Certificates	
	9.02) Motor Solo Run Certificates	
	9.03) Mechanical Run Test (MRT) Certificates	
	9.04) Mechanical Commissioning Checklists	
	9.05) Mechanical Supplier Check Lists & Reports	
10	Instrumentation Pre-Commissioning	
	10.01) System Instrument Index	
	10.02) Instrument Data Sheets	
	10.03) Instrument Cable Schedule	
	10.04) System Instrumentation Wiring Diagram	
	10.05) Hook-up Drawing (Mechanical & Pneumatic)	
	10.06) Instruments Cables Schedule	
	10.07) Instruments Cables Laying Certificates	
	10.08) Instruments Cables Termination Certificates	
	10.09) Instruments Cables Testing Certificates	
	10.10) Instruments Calibration Certificates	
	10.11) Instrument Loop Checks Certificates	
	10.12) Instrumentation Pre-Commissioning Check Lists	
	10.13) Instrumentation Supplier Check Lists & Reports	
11	Instrumentation Commissioning	
	11.01) Instrumentation Function Test Certificates	
	11.02) Instrumentation Supplier Check Lists & Reports	
Sr.	Pre-Commissioning and Commissioning Dossier Index	Applicable (Yes/No)
12	Electrical Pre-Commissioning	
	12.01) System Electrical Index	
	12.02) Electrical Drawings	
	12.03) Motor Datasheets	
	12.04) Electrical Cables Schedule	
	12.05) Electrical Cables Laying Certificates	
	12.06) Electrical Cables Testing Certificates	
	12.07) Electrical Cables Termination Certificates	
	12.08) FAT Reports & Certificates	
	12.09) SAT Reports & Certificates	
	12.10) Electrical Pre-Commissioning Check Lists	
	12.11) Electrical Supplier Check Lists & Reports	

13	Electrical Commissioning	
	13.01) Electrical -Commissioning Check Lists	
	13.02) Electrical Supplier Check Lists & Reports	
14	Red Marked-up Drawings	
	14.01) P&ID	
	14.02) Instrumentation Drawings	
	14.03) Electrical Drawings	



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

1-Mechanical Completion Certificate (MCC)



SYSTEM MECHANICAL COMPLETION CERTIFICATE (MCC)

PROJECT TITLE : CRUDE OIL TANK FARM PROJECT (AGROOD AREA)

PROJECT No : 01251-100




SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

THIS IS TO CERTIFY THAT:

- THE ABOVE SYSTEM HAS BEEN FABRICATED, ERECTED, INSTALLED AND TESTED TO THE REQUIREMENTS OF THE CONTRACT DRAWINGS, SPECIFICATIONS, THE APPLICABLE CODES AND STANDARDS.
- ALL PRE-COMMISSIONING RELEVANT ACTIVITIES, TESTS, INSPECTIONS AND CHECKS HAVE BEEN CARRIED OUT FOR THIS SYSTEM AND FOUND ACCEPTABLE.
- Q/C DOCUMENTATION OF THE ABOVE SYSTEM HAS BEEN AUDITED BY THE CUSTOMER SITE QUALITY CONTROL AND FOUND COMPLETED.
- ALL PUNCH LIST ITEMS CATEGORY (A) IN THIS SUBSYSTEM WERE CLEARED.
- THIS SYSTEM IS MECHANICALLY COMPLETED ON THE DATE AND READY FOR COMMISSIONING (RFC) WITH THE FOLLOWING EXCEPTIONS.

EXCEPTIONS :

COMPANY	PETROJET	ENPPI	PMC
NAME	Sobhy Saleem	Far / Abdulhah Fathy	
TITLE	Qc EST Engineer	Const. Engineer	
SIGNATURE			
DATE	1-8-2021	1-8-2021	



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

2- Ready for Startup Certificate (RFSU)

READY FOR START UP CERTIFICATE

PROJECT TITLE : EGPC CRUDE OIL TANK FARMS PROJECT (AGROOD-30)

PROJECT No. : 1251-100

SYSTEM /AREA /PLANT : Piping Cathodic Protection System



SYSTEM /AREA /PLANT No. : 030-CP-001

THIS IS TO CERTIFY THAT:

- THE MENTIONED SYSTEM /AREA /PLANT IS READY FOR START UP WHERE ALL MECHANICAL WORKS, PRECOMMISSIONING AND COMMISSIONING ACTIVITIES HAVE BEEN SUCCESSFULLY COMPLETED.
- MECHANICAL COMPLETION CERTIFICATE(S) FOR THE MENTIONED SYSTEM / AREA / PLANT HAVE BEEN SIGNED.
- ISSUANCE OF THIS READY FOR START UP CERTIFICATE(S) SHALL NOT RELIEVE CONTRACTOR(S) FROM THEIR OBLIGATIONS TO COMPLETE THE REMAINING SYSTEMS NOR FROM THEIR WARRANTY OBLIGATIONS AND OTHER PROVISIONS OF THE CONTRACT.
- THE FOLLOWING EXCEPTIONS AGREED TO BE CLEARED AFTER START UP AND WILL NOT PREVENT START UP ACTIVITIES.

EXCEPTIONS :

- Some readings which are below the criteria will be investigated and re-checked → Cleared refer to HOS ^{MMH} ~~MMH~~
- Final commissioning forms shall be provided on Saturday (20/11/2021) for approval.

COMPANY	ENPPI	PPC
NAME	Mohamed Mohsen	Mohamed Ibrahim
TITLE	Materials Engineer	Electrical engineer
SIGNATURE		
DATE	18/11/2021	18/11/2021



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID

030-CP-001

System Description

Piping Cathodic Protection System

3- System Punch Lists

PROJECT TITLE : CRUDE OIL TANK FARM PROJECT (AGROOD AREA)

PROJECT NUMBER : 01251-100

DISCIPLINE: Cathodic Protection

SYSTEM NAME: Piping Cathodic Protection System

SYSTEM ID: 030-CP-001

SUB-SYSTEM NAME:

SUB-SYSTEM ID:

NO	DESCRIPTION	CAT	ACTION BY	DISP	CLEARANCE APPROVED BY
1-	All remaining anodes should be finished	A	PTJ	ELC	Ru
2-	All remaining TRS should be finished	A	PTJ	~	Ru
3-	All remaining ASJB should be finished	A	PTJ	~	Ru
4-	All remaining Test Post should be finished	A	PTJ	~	Ru
5-	All remaining ATB, NTB should be finished	A	PTJ	~	Ru
6-	All remaining Vent's Anode (ug) (sulfonation)	A	PTJ	~	Ru
	Anodes should be completed.				Ru
7-	Final married-up to be submitted				Ru

CAT: CATEGORY(A,B,C) ,ACTION BY: (ENPPI,CONST.CONTRACTOR,SUPPLIER.....) , DISP: DISCIPLINE(PIP,MECH,ELECT,INST.....)

COMPANY	PTJ	ENPPI	PMC
NAME	Hostaka ibrahim	Reiner Kuntz	
SIGN.			
DATE	1 / 11 / 2021		



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

4- System Limits Marked Up P&ID

System ID

030-CP-001

System Description

Piping Cathodic Protection System

5- System Index

Enppi

Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID

030-CP-001

System Description

Piping Cathodic Protection System

6- Piping Pre-Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

6.01- Piping Test Packs



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

6.02- Piping Pre-commissioning Check Lists



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

7- Piping Commissioning

System ID	030-CP-001
System Description	Piping Cathodic Protection System

7.01- Service Test, GLT, CLT and N2 Purging Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

7.02- Piping Commissioning Check Lists



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

8- Mechanical pre-Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

8.01- System Mechanical Index



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

8.02- Equipment Drawings



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

8.03- Equipment Datasheets



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

8.04- Boxing-up Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

8.05- Grouting Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

8.06- Pre-Alignment Certificates

System ID	030-CP-001
System Description	Piping Cathodic Protection System

8.07- Mechanical Pre-Commissioning Checklists



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

9- Mechanical Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

9.01- Final Alignment Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

9.02- Motor Solo Run Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

9.03- Mechanical Run Test (MRT) Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

9.04- Mechanical Commissioning Checklists



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

9.05- Mechanical Supplier Check Lists & Reports

System ID

030-CP-001

System Description

Piping Cathodic Protection System

10- Instrumentation Pre-Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

10.01- System Instrument Index



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

10.02- Instrument Data Sheets



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

10.03- Instrument Cable Schedule



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

10.04- System Instrumentation Wiring Diagram

System ID	030-CP-001
System Description	Piping Cathodic Protection System

10.05- Hook-up Drawing (Mechanical & Pneumatic)



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

10.06- Instruments Cables Schedule



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

10.07- Instruments Cables Laying Certificates

Enppi

Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

10.08- Instruments Cables Termination Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

10.09- Instruments Cables Testing Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

10.10- Instruments Calibration Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

10.11- Instrument Loop Checks Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

10.12- Instrumentation Pre-Commissioning Check Lists



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

10.13- Instrumentation Supplier Check Lists & Reports



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

11- Instrumentation Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

11.01) Instrumentation Function Test Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

11.02- Instrumentation Supplier Check Lists & Reports



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

12- Electrical Pre-Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

12.01- System Electrical Index

			Form Type
		185. Description	
		Cathodic Protection	Cathodic Protection
030-CP-001	Piping Cathodic Protection System	Electrical	LV Cable
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist
030-CP-001	Piping Cathodic Protection System	Electrical	Checklist



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



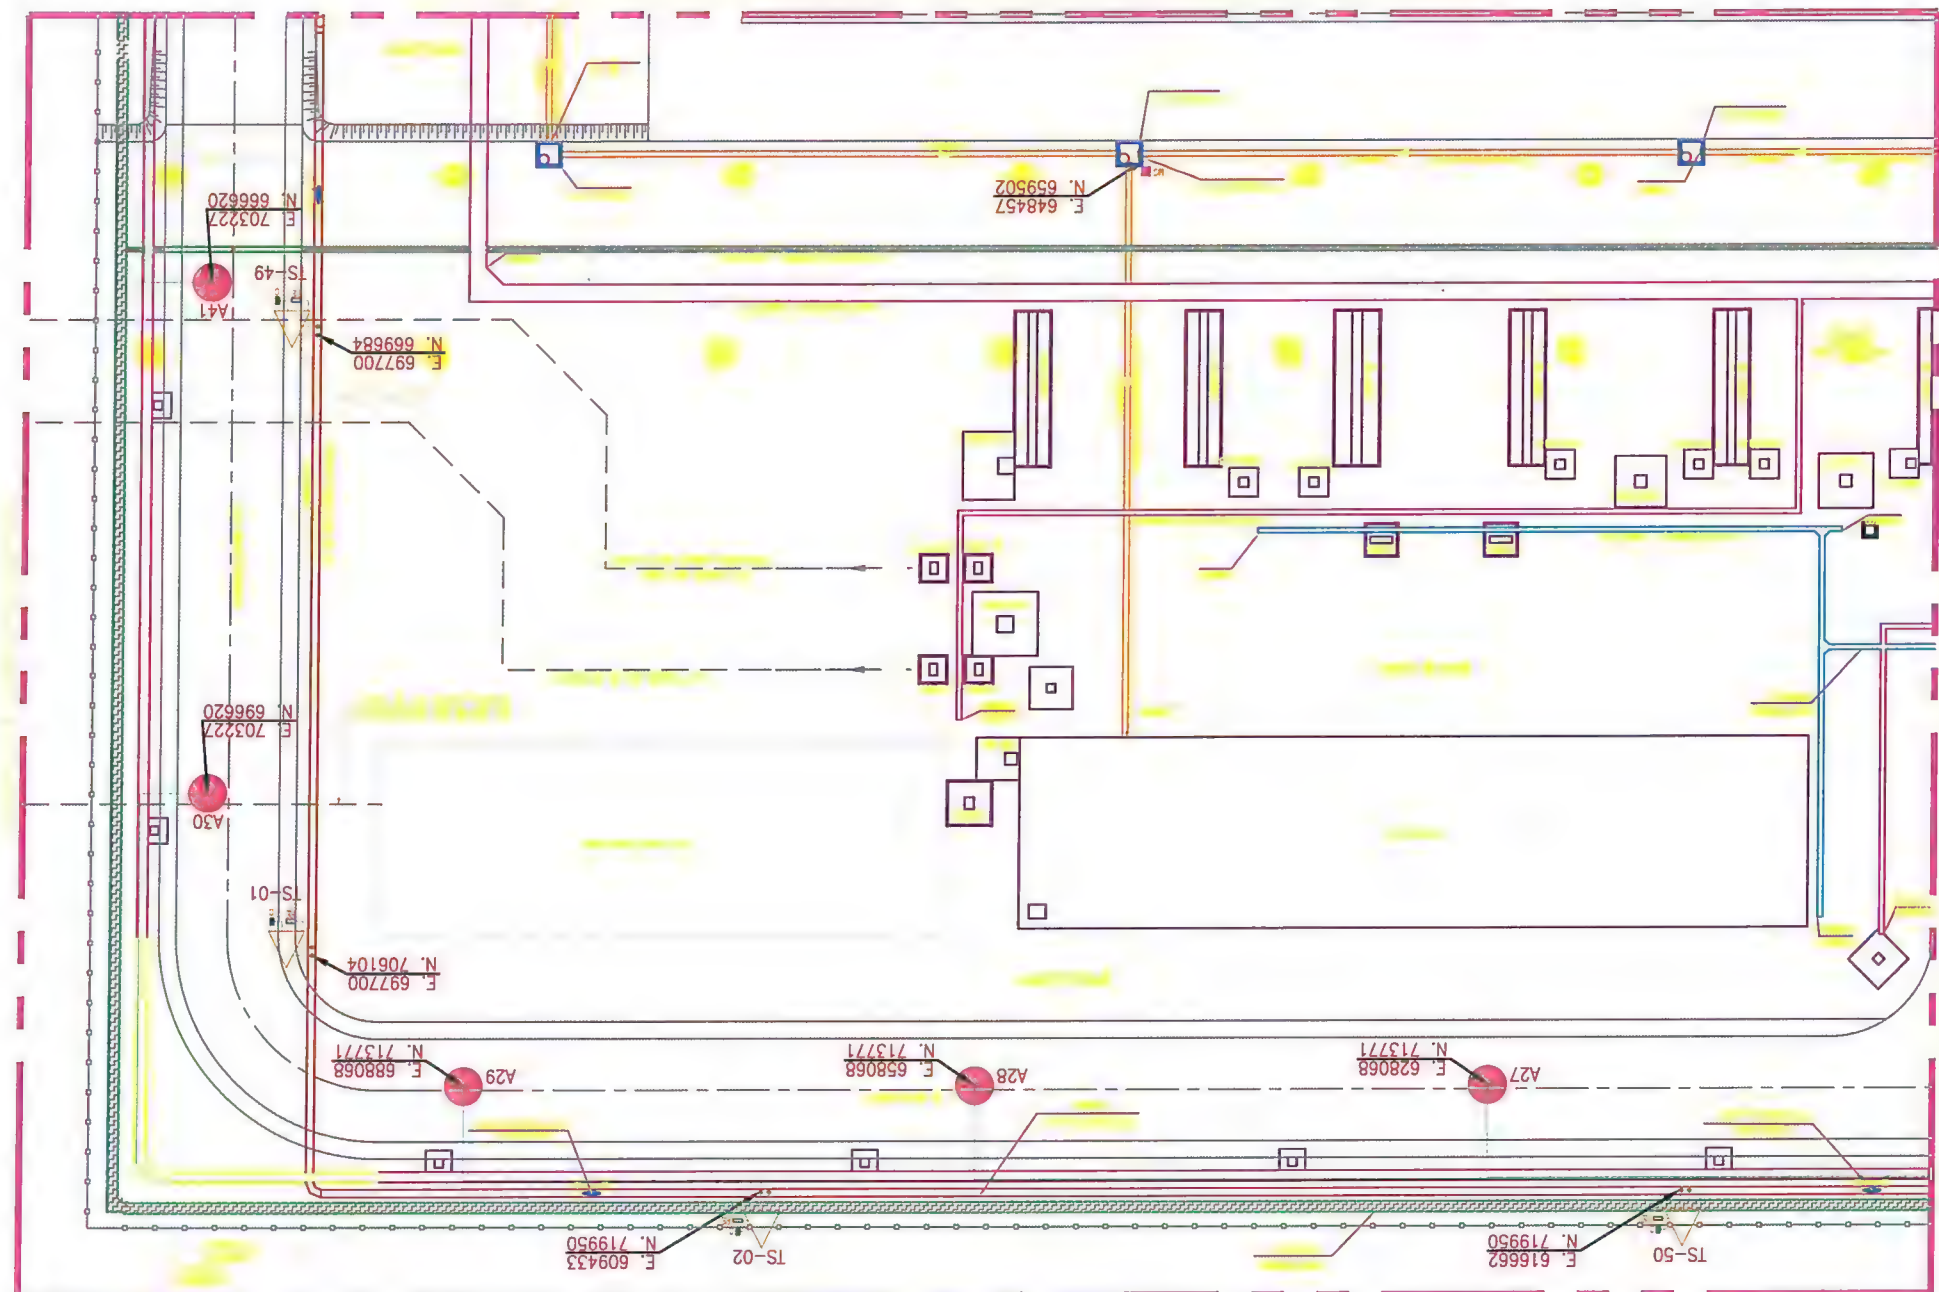
System ID	030-CP-001
System Description	Piping Cathodic Protection System

12.02- Electrical Drawings

[illegible][illegible]

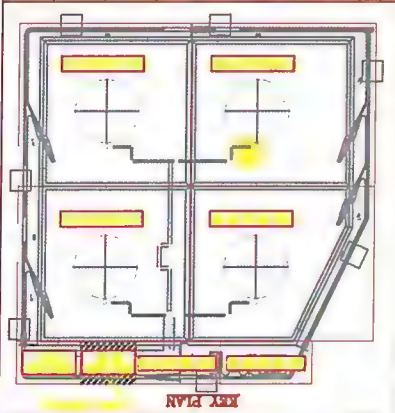
		-	MNO ANODES
		-	TRANSFORMER RECTIFIER
		-	ANODE SPLITTING JUNCTION BOX
		-	NEGATIVE JUNCTION BOX
		-	POSITIVE JUNCTION BOX
		-	TEST STATION WITH RE & COUPON
		-	35mm ² XLPE/PVC POSITIVE FEEDER BLACK CABLE
		-	35mm ² XLPE/PVC NEGATIVE FEEDER BLACK CABLE
		-	16mm ² XLPE/PVC ANODE TAIL BLACK CABLE
		-	16mm ² XLPE/PVC MONITORING BLACK CABLE
		-	10mm ² XLPE/PVC REFERENCE ELECTRODE RED CABLE
		-	10mm ² XLPE/PVC POLARISATION COUPON BLUE CABLE
		-	MAGNESIUM ANODE

LEGEND :

[illegible]

1:150	1251-100-S30-D99-0005	02/08	8
EGPC			
EGPC CRUDE OIL TANK FARM			
AGROOD AREA (MODULE-1) - IN-PLANT			
PIPING LAYOUT - AGROOD-GPC-030			
EGPC PROJECT NO. 1: 1251-100-S30-D99-0005			
EGPC PROJECT NO. 1: 1251-100-S30-D99-0005			

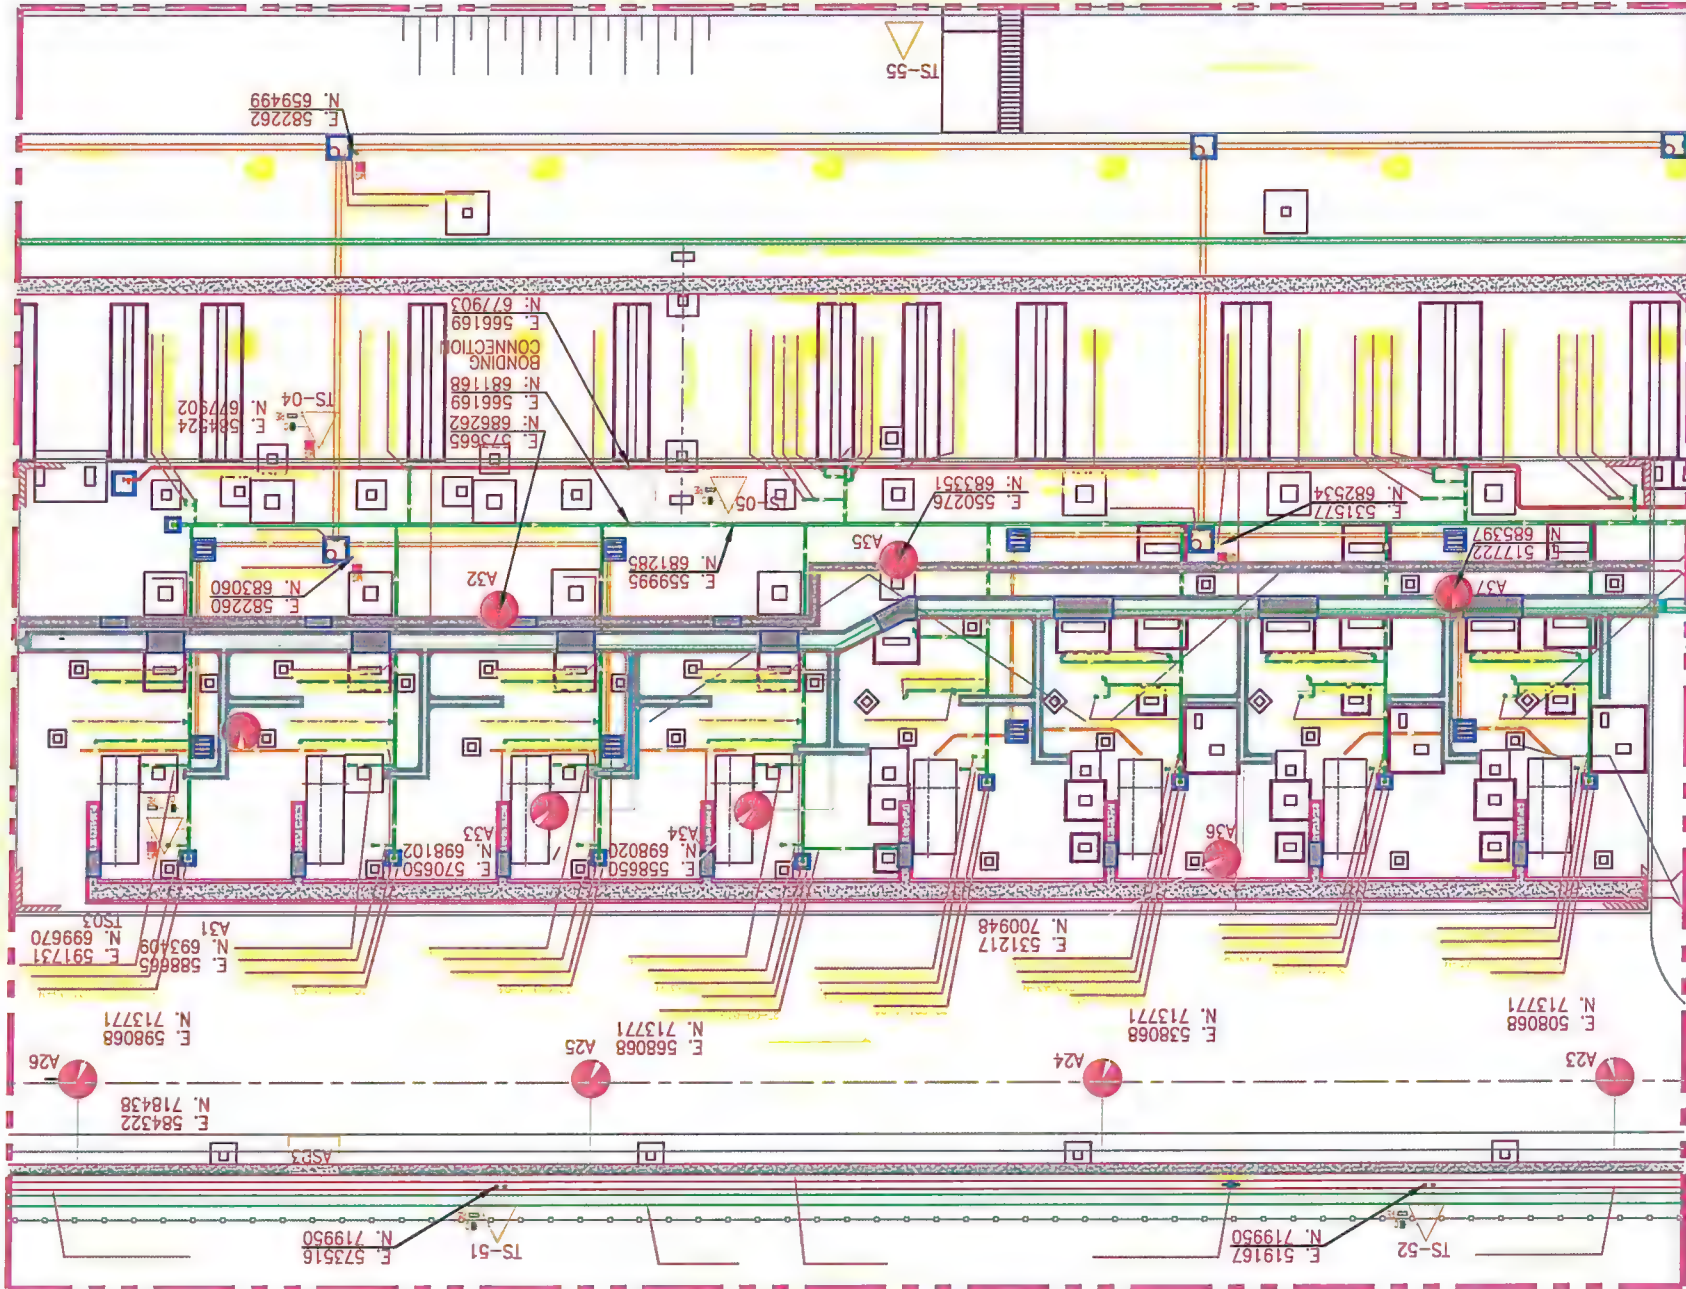
NO.	DESCRIPTION	DATE	BY	CHKD.
1	REVISION			
2	REVISION			
3	REVISION			
4	REVISION			
5	REVISION			
6	REVISION			
7	REVISION			
8	REVISION			



- LEGEND:
- MMO ANODES
 - TRANSFORMER RECTIFIER
 - ANODE SPLITTING JUNCTION BOX
 - NEGATIVE JUNCTION BOX
 - POSITIVE JUNCTION BOX
 - TEST STATION WITH RE & COUPON
 - 35mm² XLPE/PVC POSITIVE FEEDER
 - 35mm² XLPE/PVC NEGATIVE FEEDER
 - BLACK CABLE
 - 16mm² XLPE/PVC ANODE TAIL BLACK CABLE
 - 16mm² XLPE/PVC MONITORING BLACK CABLE
 - 10mm² XLPE/PVC REFERENCE ELECTRODE
 - 10mm² XLPE/PVC POLARISATION COUPON
 - BLUE CABLE
 - MG - MAGNESIUM ANODE

DOCUMENT NUMBER	DESCRIPTION
1251-100-S30-D99-0005	INSTALLATION, COMMISSIONING, OPERATIONS
1251-100-S30-D99-0006	DETAIL DESIGN REPORT AGROOD GPC 030
1251-100-S30-D99-0007	CATHODIC PROTECTION EQUIPMENT DATA SHEETS
1251-100-S30-D99-0008	JUNCTION BOX GENERAL ARRANGEMENT
1251-100-S30-D99-0009	TRANSFORMER RECTIFIER GENERAL ARRANGEMENT
1251-100-S30-D99-0010	ANODE INSTALLATION DRAWING
1251-100-S30-D99-0011	INSTALLATION DETAILS
1251-100-S30-D99-0012	TEST POST AND MONITORING

SUPPLIER DOCUMENT REVIEW	1. Work may proceed.	2. Review and provide a comment on the document.	3. Review and provide a comment on the document.	4. Review and provide a comment on the document.	5. Review and provide a comment on the document.	6. Review and provide a comment on the document.	7. Review and provide a comment on the document.	8. Review and provide a comment on the document.
PROJECT	NEW CRUDE OIL TANK	TITLE	NEW CRUDE OIL TANK	PACKAGE DESCRIPTION	CATHODIC PROTECTION	EQUIPMENT	IDENTIFIER	DOCUMENT NUMBER
REVISION	8	DATE	02/08	1251-100-S30-D99-0005	1251-100-S30-D99-0005	1251-100-S30-D99-0005	1251-100-S30-D99-0005	1251-100-S30-D99-0005



8

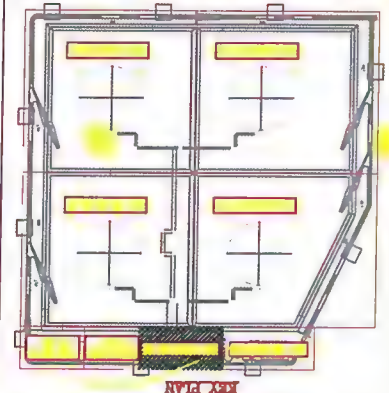
Happy

EGPC CRUDE OIL TANK FARM
AGROD AREA (MODULE-1) - IN-PLANT
PIPING LAYOUT - AGROD-CPC-030

1997-1998 1998-1999 1999-2000 2000-2001 2001-2002 2002-2003 2003-2004 2004-2005 2005-2006 2006-2007 2007-2008 2008-2009 2009-2010 2010-2011 2011-2012 2012-2013 2013-2014 2014-2015 2015-2016 2016-2017 2017-2018 2018-2019 2019-2020 2020-2021 2021-2022 2022-2023 2023-2024 2024-2025 2025-2026 2026-2027 2027-2028 2028-2029 2029-2030 2030-2031 2031-2032 2032-2033 2033-2034 2034-2035 2035-2036 2036-2037 2037-2038 2038-2039 2039-2040 2040-2041 2041-2042 2042-2043 2043-2044 2044-2045 2045-2046 2046-2047 2047-2048 2048-2049 2049-2050 2050-2051 2051-2052 2052-2053 2053-2054 2054-2055 2055-2056 2056-2057 2057-2058 2058-2059 2059-2060 2060-2061 2061-2062 2062-2063 2063-2064 2064-2065 2065-2066 2066-2067 2067-2068 2068-2069 2069-2070 2070-2071 2071-2072 2072-2073 2073-2074 2074-2075 2075-2076 2076-2077 2077-2078 2078-2079 2079-2080 2080-2081 2081-2082 2082-2083 2083-2084 2084-2085 2085-2086 2086-2087 2087-2088 2088-2089 2089-2090 2090-2091 2091-2092 2092-2093 2093-2094 2094-2095 2095-2096 2096-2097 2097-2098 2098-2099 2099-2100 2100-2101 2101-2102 2102-2103 2103-2104 2104-2105 2105-2106 2106-2107 2107-2108 2108-2109 2109-2110 2110-2111 2111-2112 2112-2113 2113-2114 2114-2115 2115-2116 2116-2117 2117-2118 2118-2119 2119-2120 2120-2121 2121-2122 2122-2123 2123-2124 2124-2125 2125-2126 2126-2127 2127-2128 2128-2129 2129-2130 2130-2131 2131-2132 2132-2133 2133-2134 2134-2135 2135-2136 2136-2137 2137-2138 2138-2139 2139-2140 2140-2141 2141-2142 2142-2143 2143-2144 2144-2145 2145-2146 2146-2147 2147-2148 2148-2149 2149-2150 2150-2151 2151-2152 2152-2153 2153-2154 2154-2155 2155-2156 2156-2157 2157-2158 2158-2159 2159-2160 2160-2161 2161-2162 2162-2163 2163-2164 2164-2165 2165-2166 2166-2167 2167-2168 2168-2169 2169-2170 2170-2171 2171-2172 2172-2173 2173-2174 2174-2175 2175-2176 2176-2177 2177-2178 2178-2179 2179-2180 2180-2181 2181-2182 2182-2183 2183-2184 2184-2185 2185-2186 2186-2187 2187-2188 2188-2189 2189-2190 2190-2191 2191-2192 2192-2193 2193-2194 2194-2195 2195-2196 2196-2197 2197-2198 2198-2199 2199-2200 2200-2201 2201-2202 2202-2203 2203-2204 2204-2205 2205-2206 2206-2207 2207-2208 2208-2209 2209-2210 2210-2211 2211-2212 2212-2213 2213-2214 2214-2215 2215-2216 2216-2217 2217-2218 2218-2219 2219-2220 2220-2221 2221-2222 2222-2223 2223-2224 2224-2225 2225-2226 2226-2227 2227-2228 2228-2229 2229-2230 2230-2231 2231-2232 2232-2233 2233-2234 2234-2235 2235-2236 2236-2237 2237-2238 2238-2239 2239-2240 2240-2241 2241-2242 2242-2243 2243-2244 2244-2245 2245-2246 2246-2247 2247-2248 2248-2249 2249-2250 2250-2251 2251-2252 2252-2253 2253-2254 2254-2255 2255-2256 2256-2257 2257-2258 2258-2259 2259-2260 2260-2261 2261-2262 2262-2263 2263-2264 2264-2265 2265-2266 2266-2267 2267-2268 2268-2269 2269-2270 2270-2271 2271-2272 2272-2273 2273-2274 2274-2275 2275-2276 2276-2277 2277-2278 2278-2279 2279-2280 2280-2281 2281-2282 2282-2283 2283-2284 2284-2285 2285-2286 2286-2287 2287-2288 2288-228



EGPC

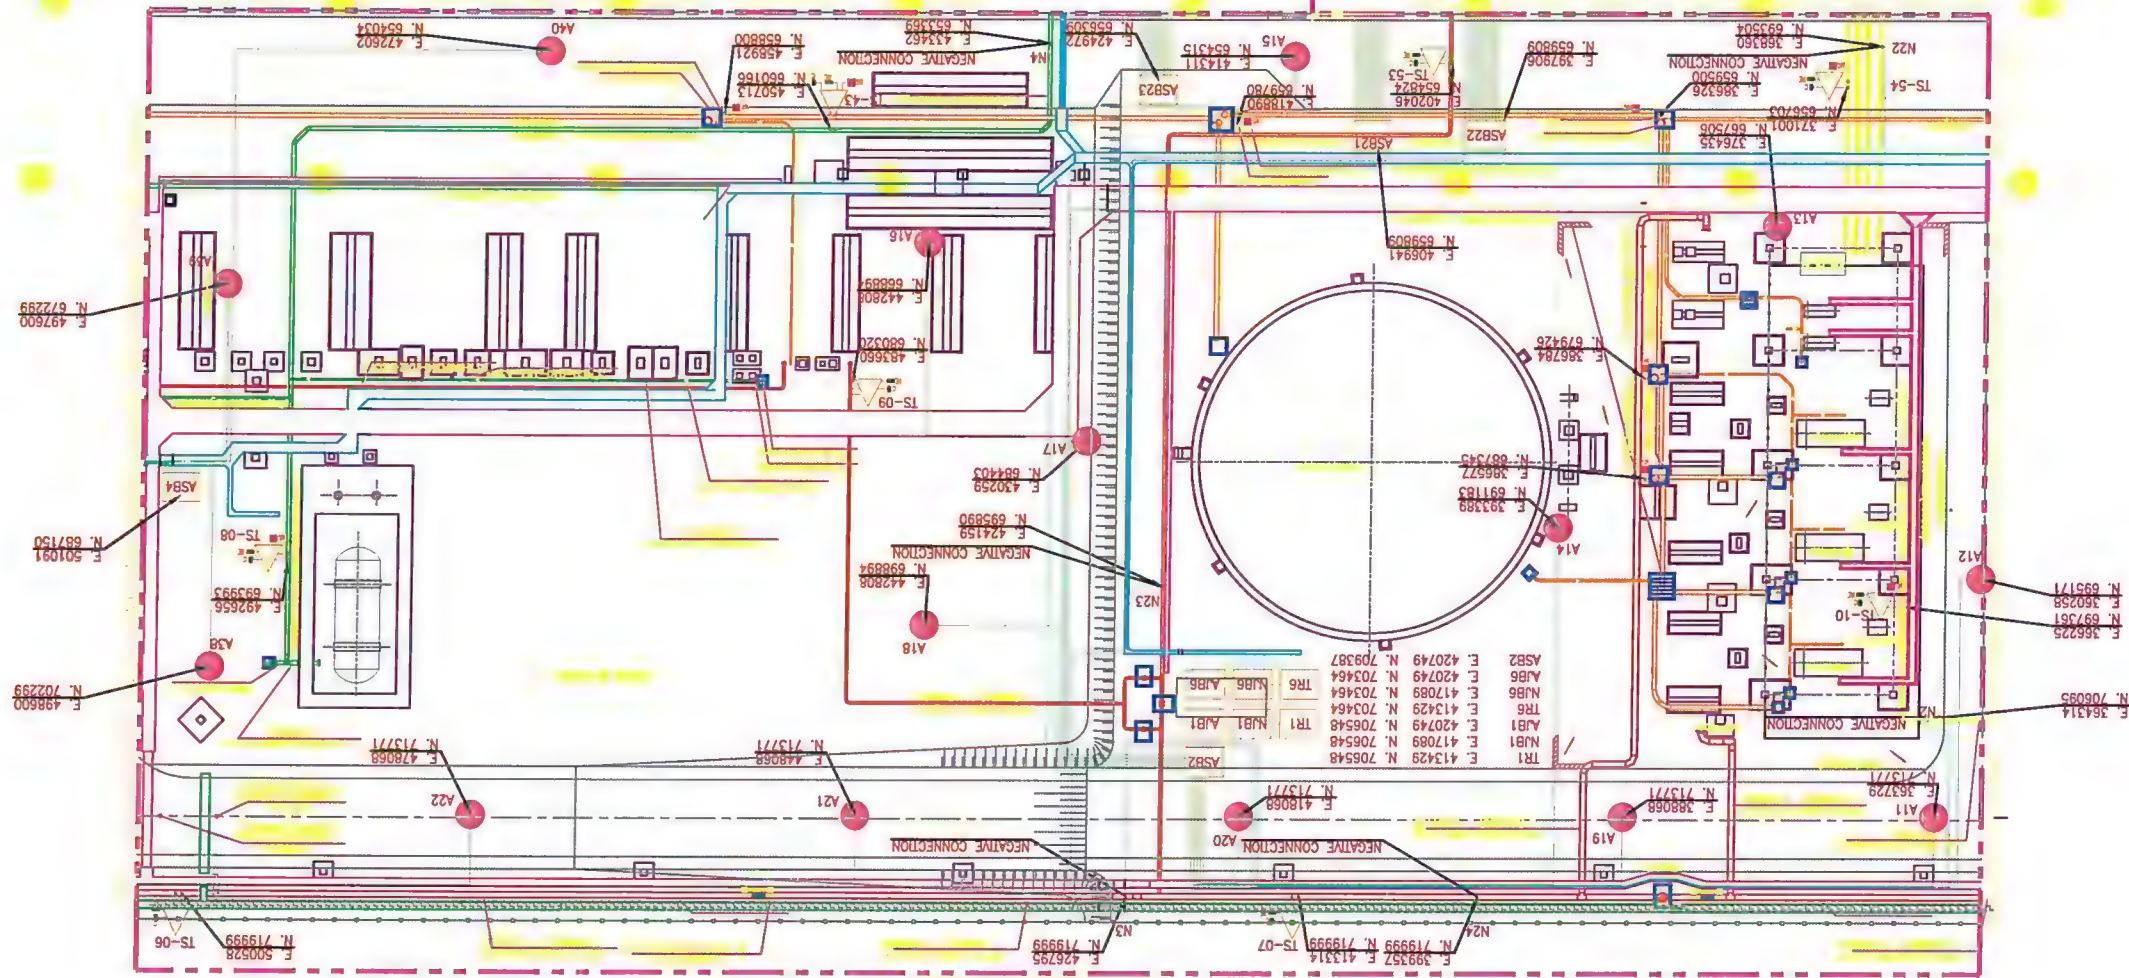
[illegible]

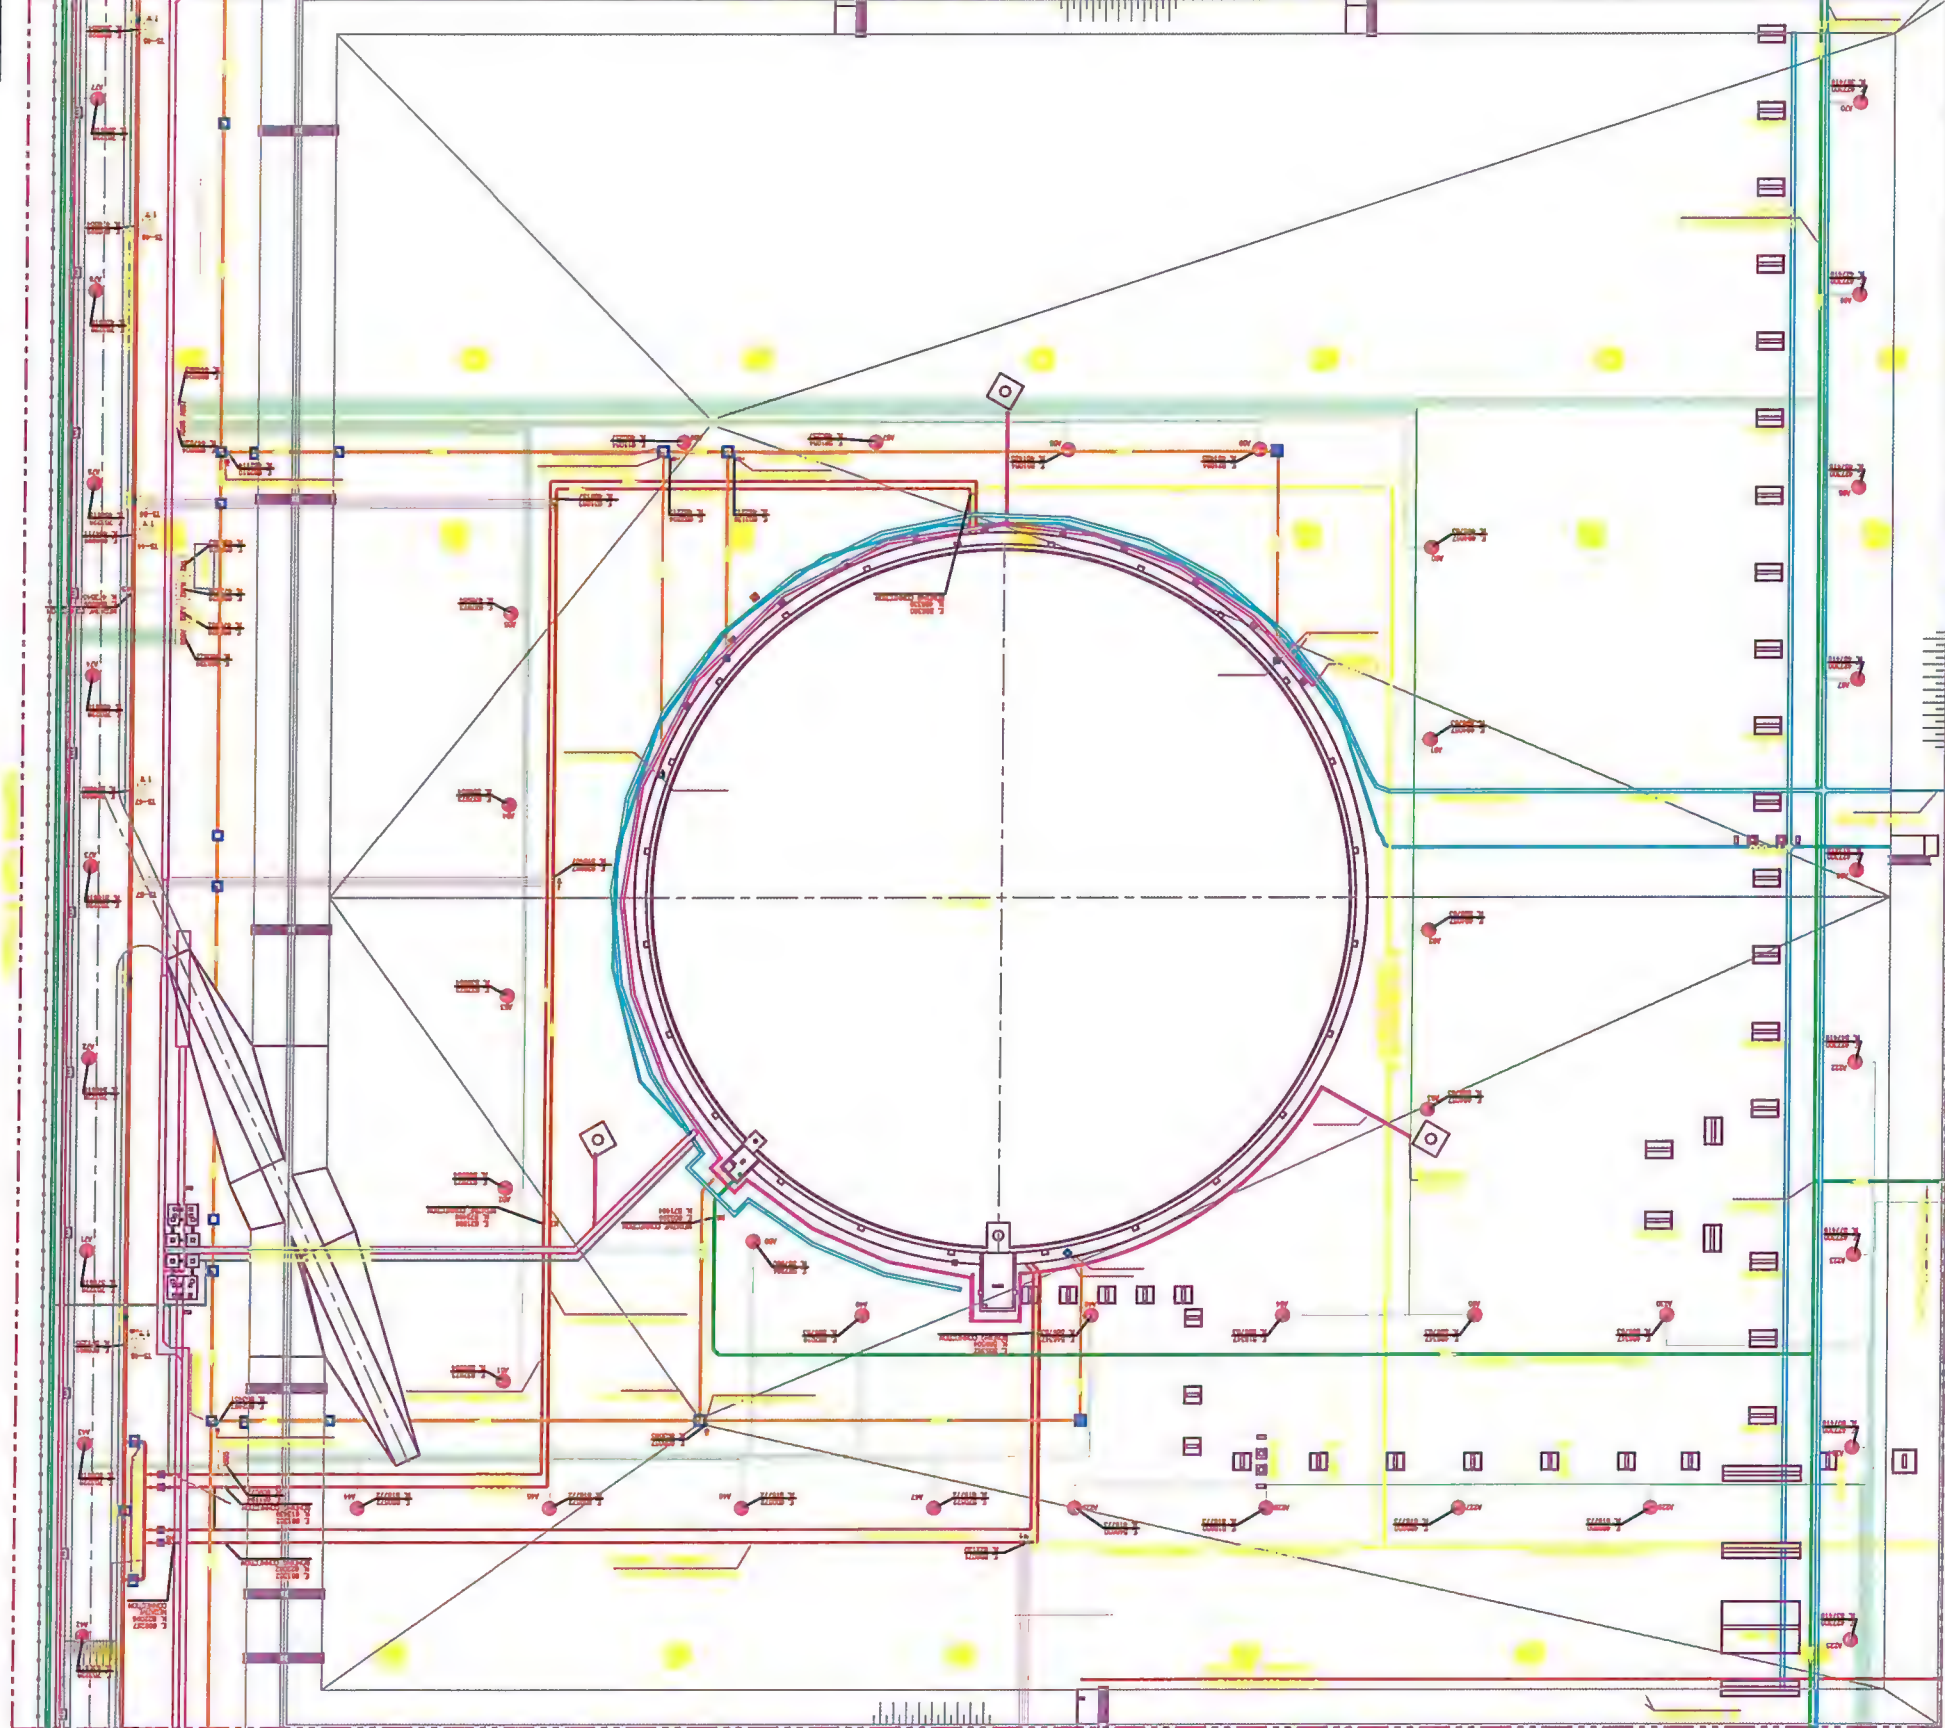
- | | | |
|-----------|--|---|
| | | MAGNESIUM ANODE |
| — — — — — | | BLUE CABLE |
| | | 10mm ² XLPE/PVC POLARISATION COUPON |
| — — — — — | | RED CABLE |
| | | 10mm ² XLPE/PVC REFERENCE ELECTRODE |
| — — — — — | | 16mm ² XLPE/PVC MONITORING BLACK CABLE |
| | | 16mm ² XLPE/PVC ANODE TAIL BLACK CABLE |
| — — — — — | | BLACK CABLE |
| | | 35mm ² XLPE/PVC NEGATIVE FEEDER |
| — — — — — | | BLACK CABLE |
| | | 35mm ² XLPE/PVC POSITIVE FEEDER |
| — — — — — | | TEST STATION WITH RE & COUPON |
| | | POSITIVE JUNCTION BOX |
| — — — — — | | NEGATIVE JUNCTION BOX |
| | | ANODE SPLITTING JUNCTION BOX |
| — — — — — | | TRANSFORMER RECTIFIER |
| | | MMO ANODES |
- LEGEND :

LEGEND

[illegible]

DOCUMENT NUMBER	DESCRIPTION	REFERENCES
1251-100-330-098-098-0024	TEST POST AND PERFORMANCE ELECTRONIC RECORDS DETAILS	
1251-100-330-098-098-0024	ARMED INSPECTION DRAWING	
1251-100-330-001-001-0001	TRANSMISSIONS RECTIFIER GENERAL APPROVED	
1251-100-330-001-001-0001	JUNCTION BOX GENERAL APPROVED	
1251-100-330-408-000-0000	CATHODE PROTECTION EQUIPMENT DATA SHEET	
1251-100-330-003-003-0000	DETAIL DESIGN REPORT KAYAKS AND DOG	
1251-100-330-098-098-0000	INSTALLATION, COMMISSIONING, OPERATIONS	
	MANUAL, DRAWING	

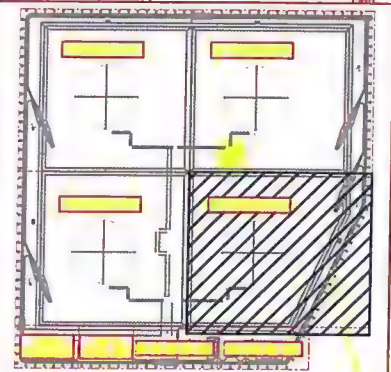




SIGNATURE		DATE
NAME		
PROJECT		NEW CRUDE OIL TANK
PACKAGE DESCRIPTION		CATHODIC PROTECTION
DRAWING		
DOCUMENT NUMBER	000	SHEET 0 OF 0
REVISION		
1251-100-S30-000-0000	06/08	8
1251-100-S30-000-0005		
1251-100-S30-000-0005		



NO.	DESCRIPTION	DATE	BY	CHKD.	APPD.
1	ISSUED FOR REVIEW				
2	ISSUED FOR REVIEW				
3	ISSUED FOR REVIEW				
4	ISSUED FOR REVIEW				
5	ISSUED FOR REVIEW				
6	ISSUED FOR REVIEW				
7	ISSUED FOR REVIEW				
8	ISSUED FOR REVIEW				

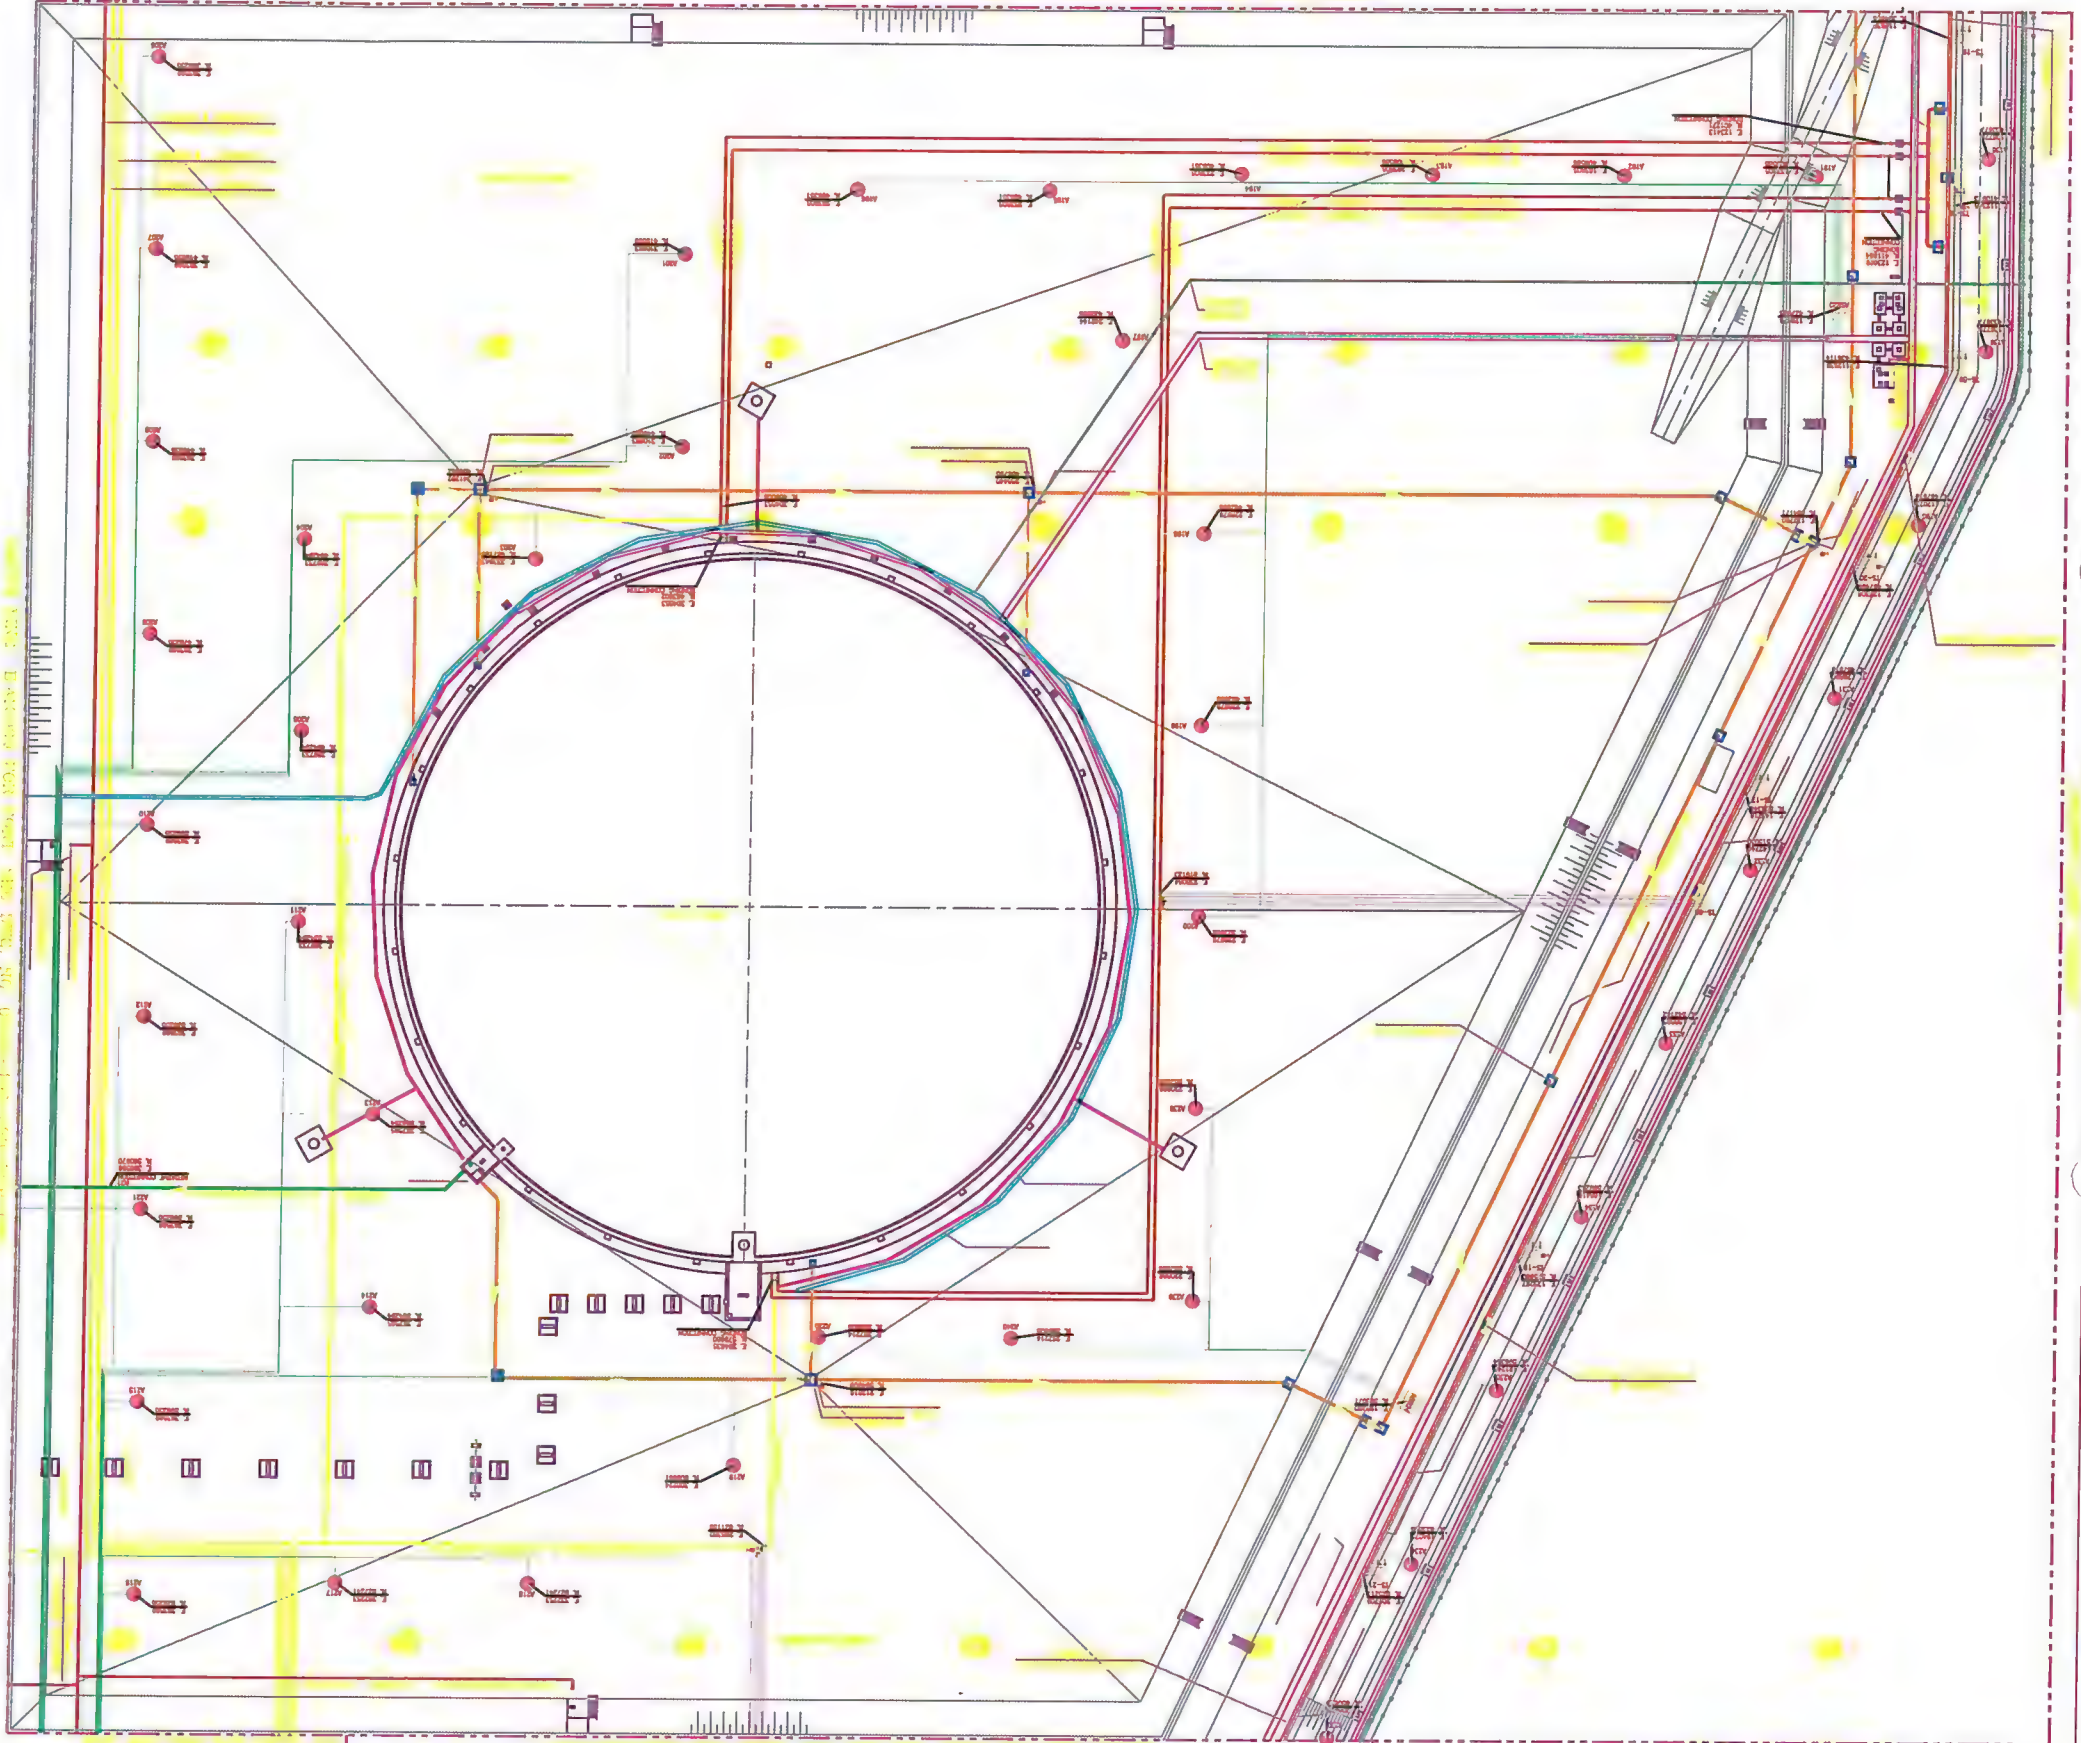



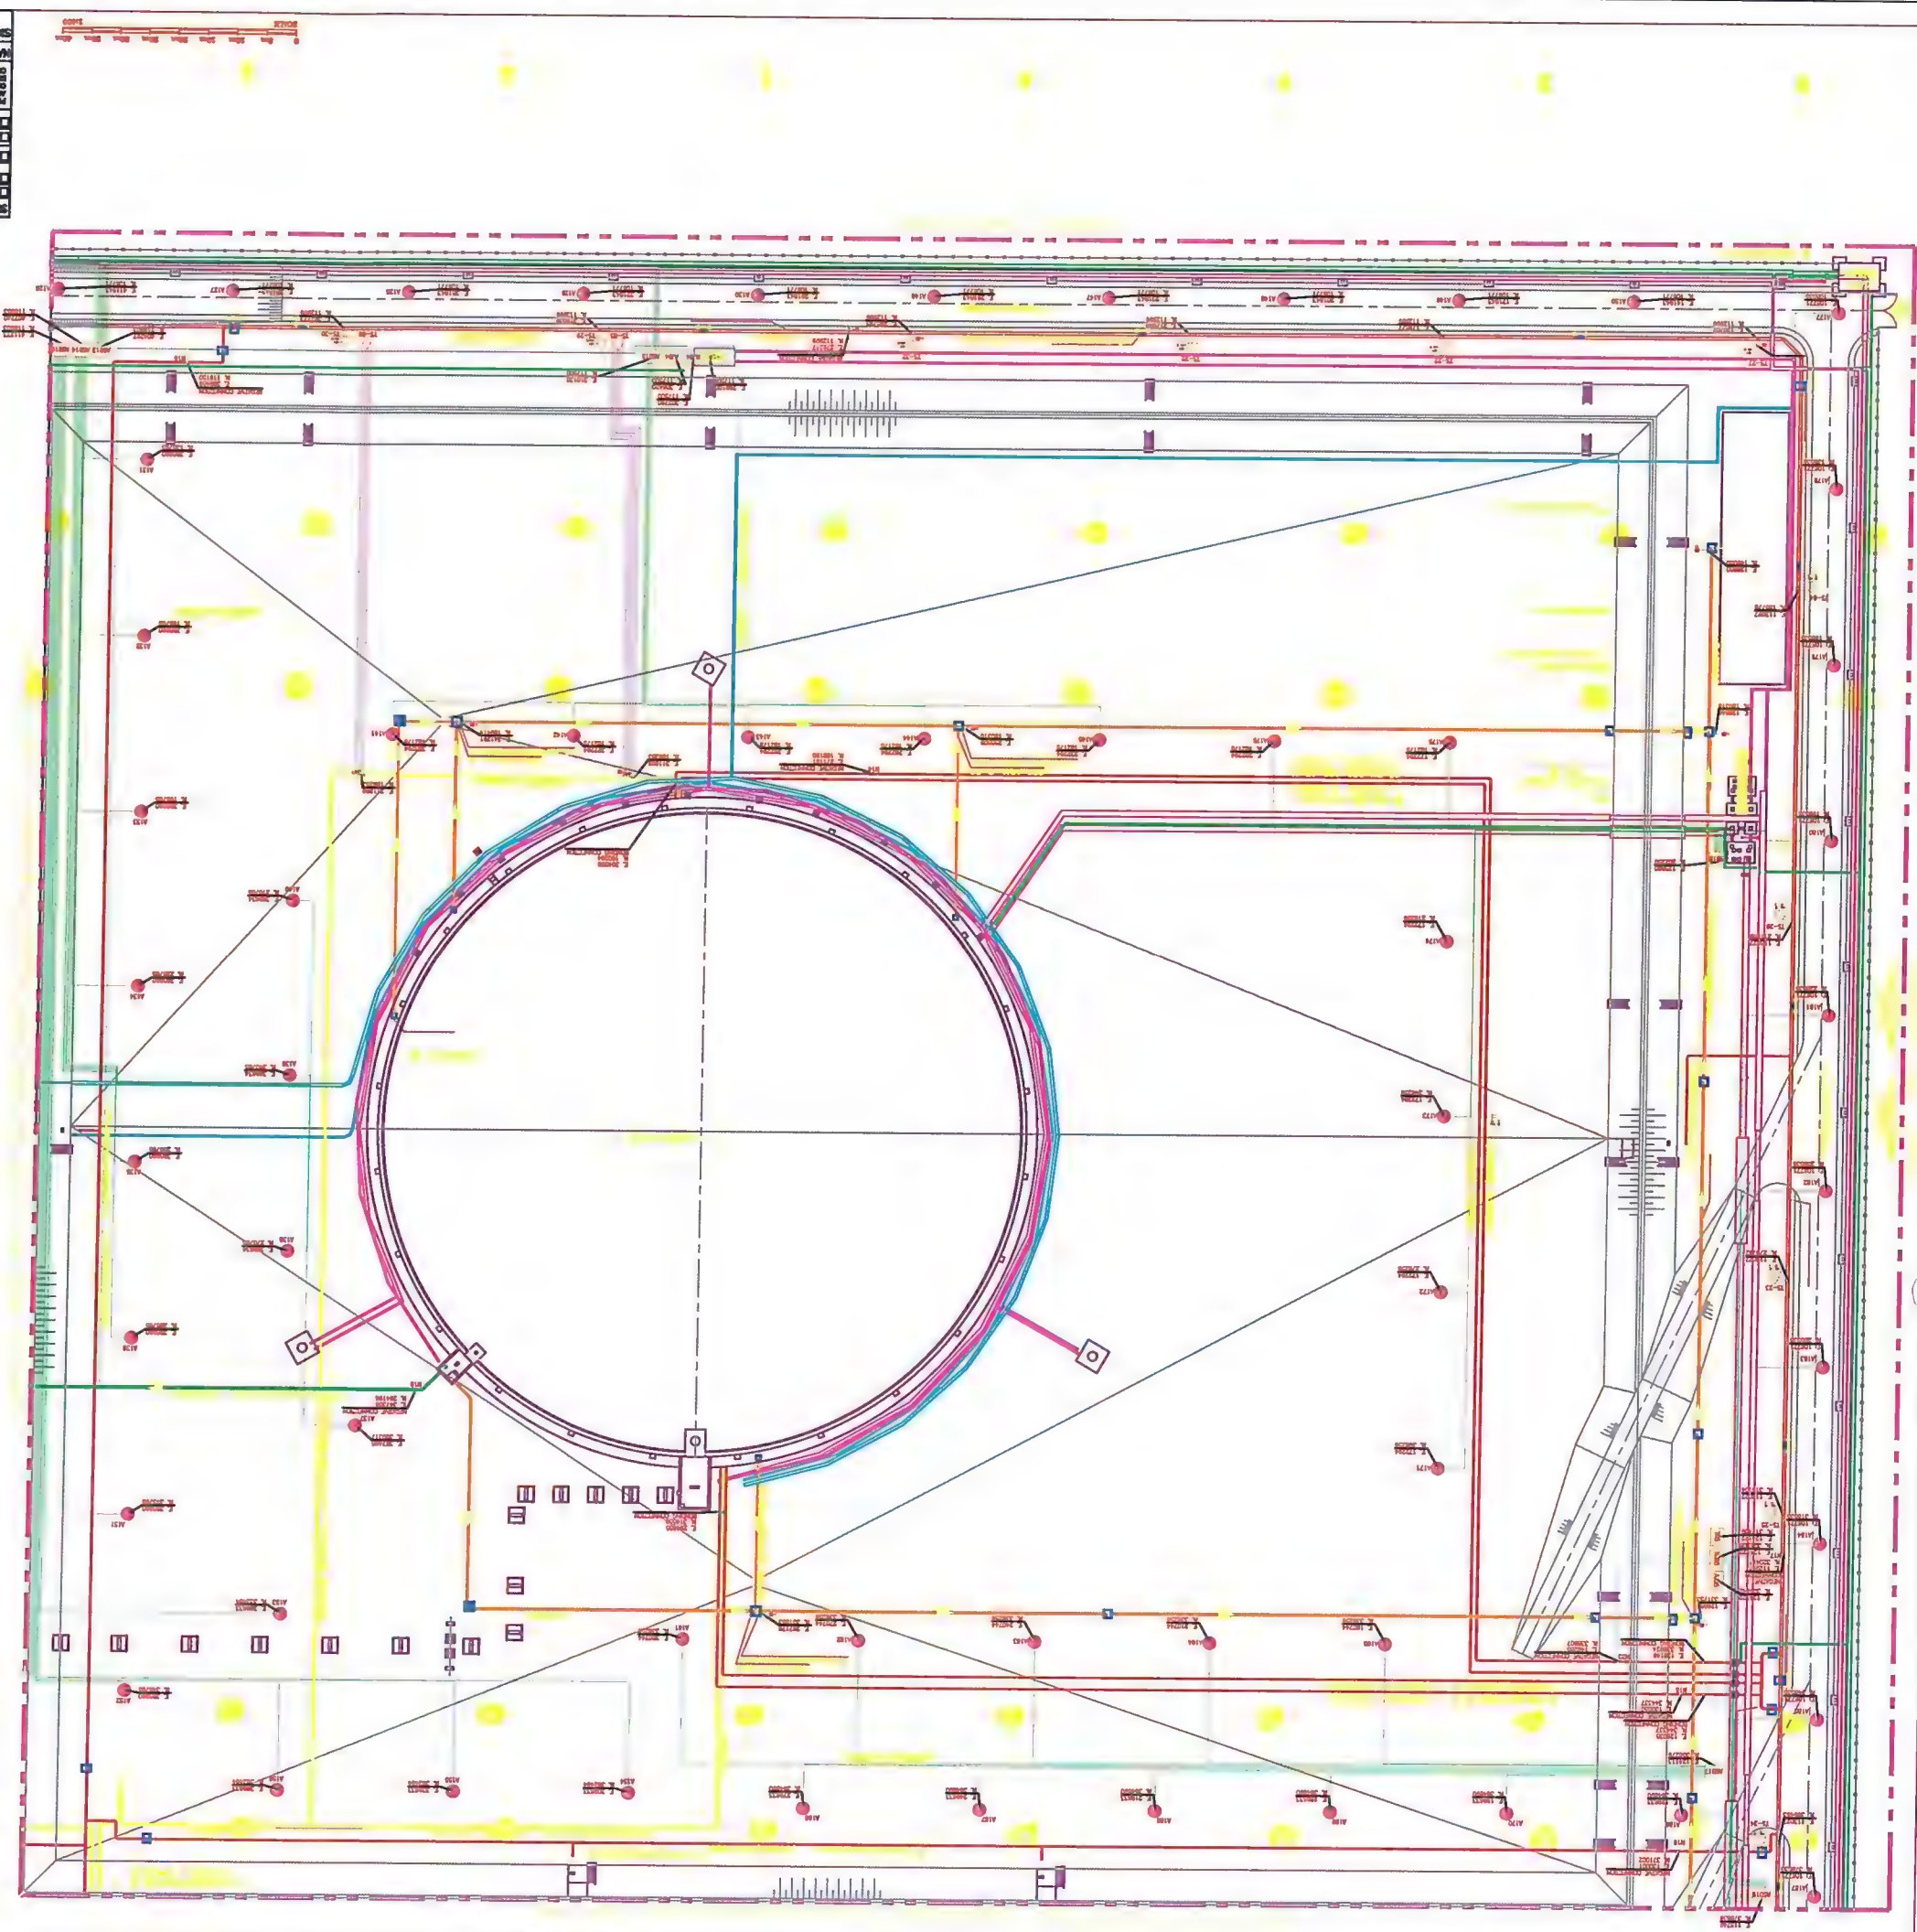
KEY PLAN

- LEGEND :
- MMO ANODES
 - TR TRANSFORMER RECTIFIER
 - AS ANODE SPLITTING JUNCTION BOX
 - NB NEGATIVE JUNCTION BOX
 - PO POSITIVE JUNCTION BOX
 - TEST STATION WITH RE & COUPON
 - 35mm² XLPE/PVC POSITIVE FEEDER BLACK CABLE
 - 35mm² XLPE/PVC NEGATIVE FEEDER BLACK CABLE
 - 16mm² XLPE/PVC ANODE TAIL BLACK CABLE
 - 16mm² XLPE/PVC MONITORING BLACK CABLE
 - 10mm² XLPE/PVC REFERENCE ELECTRODE RED CABLE
 - 10mm² XLPE/PVC POLARISATION COUPON BLUE CABLE
 - MG - MAGNESIUM ANODE

LEGEND

NO.	DESCRIPTION
1	THIS DRAWING HAS BEEN ISSUED FOR CATHODIC PROTECTION EQUIPMENT
2	FOR ANY OTHER WORKS PLEASE REFER TO THE DRAWING NO. (1251-100-S30-000-0000)
3	DATE (1251-100-S30-000-0000) TO (0000)
4	DATE (1251-100-S30-000-0000) TO (0000)
5	DATE (1251-100-S30-000-0000) TO (0000)
6	DATE (1251-100-S30-000-0000) TO (0000)
7	DATE (1251-100-S30-000-0000) TO (0000)
8	DATE (1251-100-S30-000-0000) TO (0000)
9	DATE (1251-100-S30-000-0000) TO (0000)
10	DATE (1251-100-S30-000-0000) TO (0000)
11	DATE (1251-100-S30-000-0000) TO (0000)
12	DATE (1251-100-S30-000-0000) TO (0000)
13	DATE (1251-100-S30-000-0000) TO (0000)
14	DATE (1251-100-S30-000-0000) TO (0000)
15	DATE (1251-100-S30-000-0000) TO (0000)
16	DATE (1251-100-S30-000-0000) TO (0000)
17	DATE (1251-100-S30-000-0000) TO (0000)
18	DATE (1251-100-S30-000-0000) TO (0000)
19	DATE (1251-100-S30-000-0000) TO (0000)
20	DATE (1251-100-S30-000-0000) TO (0000)
21	DATE (1251-100-S30-000-0000) TO (0000)
22	DATE (1251-100-S30-000-0000) TO (0000)
23	DATE (1251-100-S30-000-0000) TO (0000)
24	DATE (1251-100-S30-000-0000) TO (0000)
25	DATE (1251-100-S30-000-0000) TO (0000)
26	DATE (1251-100-S30-000-0000) TO (0000)
27	DATE (1251-100-S30-000-0000) TO (0000)
28	DATE (1251-100-S30-000-0000) TO (0000)
29	DATE (1251-100-S30-000-0000) TO (0000)
30	DATE (1251-100-S30-000-0000) TO (0000)
31	DATE (1251-100-S30-000-0000) TO (0000)
32	DATE (1251-100-S30-000-0000) TO (0000)
33	DATE (1251-100-S30-000-0000) TO (0000)
34	DATE (1251-100-S30-000-0000) TO (0000)
35	DATE (1251-100-S30-000-0000) TO (0000)
36	DATE (1251-100-S30-000-0000) TO (0000)
37	DATE (1251-100-S30-000-0000) TO (0000)
38	DATE (1251-100-S30-000-0000) TO (0000)
39	DATE (1251-100-S30-000-0000) TO (0000)
40	DATE (1251-100-S30-000-0000) TO (0000)
41	DATE (1251-100-S30-000-0000) TO (0000)
42	DATE (1251-100-S30-000-0000) TO (0000)
43	DATE (1251-100-S30-000-0000) TO (0000)
44	DATE (1251-100-S30-000-0000) TO (0000)
45	DATE (1251-100-S30-000-0000) TO (0000)
46	DATE (1251-100-S30-000-0000) TO (0000)
47	DATE (1251-100-S30-000-0000) TO (0000)
48	DATE (1251-100-S30-000-0000) TO (0000)
49	DATE (1251-100-S30-000-0000) TO (0000)
50	DATE (1251-100-S30-000-0000) TO (0000)
51	DATE (1251-100-S30-000-0000) TO (0000)
52	DATE (1251-100-S30-000-0000) TO (0000)
53	DATE (1251-100-S30-000-0000) TO (0000)
54	DATE (1251-100-S30-000-0000) TO (0000)
55	DATE (1251-100-S30-000-0000) TO (0000)
56	DATE (1251-100-S30-000-0000) TO (0000)
57	DATE (1251-100-S30-000-0000) TO (0000)
58	DATE (1251-100-S30-000-0000) TO (0000)
59	DATE (1251-100-S30-000-0000) TO (0000)
60	DATE (1251-100-S30-000-0000) TO (0000)
61	DATE (1251-100-S30-000-0000) TO (0000)
62	DATE (1251-100-S30-000-0000) TO (0000)
63	DATE (1251-100-S30-000-0000) TO (0000)
64	DATE (1251-100-S30-000-0000) TO (0000)
65	DATE (1251-100-S30-000-0000) TO (0000)
66	DATE (1251-100-S30-000-0000) TO (0000)
67	DATE (1251-100-S30-000-0000) TO (0000)
68	DATE (1251-100-S30-000-0000) TO (0000)
69	DATE (1251-100-S30-000-0000) TO (0000)
70	DATE (1251-100-S30-000-0000) TO (0000)
71	DATE (1251-100-S30-000-0000) TO (0000)
72	DATE (1251-100-S30-000-0000) TO (0000)
73	DATE (1251-100-S30-000-0000) TO (0000)
74	DATE (1251-100-S30-000-0000) TO (0000)
75	DATE (1251-100-S30-000-0000) TO (0000)
76	DATE (1251-100-S30-000-0000) TO (0000)
77	DATE (1251-100-S30-000-0000) TO (0000)
78	DATE (1251-100-S30-000-0000) TO (0000)
79	DATE (1251-100-S30-000-0000) TO (0000)
80	DATE (1251-100-S30-000-0000) TO (0000)
81	DATE (1251-100-S30-000-0000) TO (0000)
82	DATE (1251-100-S30-000-0000) TO (0000)
83	DATE (1251-100-S30-000-0000) TO (0000)
84	DATE (1251-100-S30-000-0000) TO (0000)
85	DATE (1251-100-S30-000-0000) TO (0000)
86	DATE (1251-100-S30-000-0000) TO (0000)
87	DATE (1251-100-S30-000-0000) TO (0000)
88	DATE (1251-100-S30-000-0000) TO (0000)
89	DATE (1251-100-S30-000-0000) TO (0000)
90	DATE (1251-100-S30-000-0000) TO (0000)
91	DATE (1251-100-S30-000-0000) TO (0000)
92	DATE (1251-100-S30-000-0000) TO (0000)
93	DATE (1251-100-S30-000-0000) TO (0000)
94	DATE (1251-100-S30-000-0000) TO (0000)
95	DATE (1251-100-S30-000-0000) TO (0000)
96	DATE (1251-100-S30-000-0000) TO (0000)
97	DATE (1251-100-S30-000-0000) TO (0000)
98	DATE (1251-100-S30-000-0000) TO (0000)
99	DATE (1251-100-S30-000-0000) TO (0000)
100	DATE (1251-100-S30-000-0000) TO (0000)





400V AC 50Hz 3 PH. SUPPLY

50V 50A TRANSFORMER RECTIFIER

AGO30-TR-003

35mm² XLPE/PVC CABLE

AGO30-AJB-003

35mm² XLPE/PVC CABLE

35mm² XLPE/PVC CABLE

AGO30-NJB-003

AGO30-ASB-009

AGO30-ASB-010

AGO30-ASB-011

AGO30-ASB-012

35mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

6"-FW-030-056-A3-N
10"-CD-030-011-A3-N
6"-FW-030-096-A3-N
6"-FW-030-099-A3-N

MMO ANODE 81
MMO ANODE 82
MMO ANODE 83
MMO ANODE 84
MMO ANODE 85
MMO ANODE 86
MMO ANODE 87
MMO ANODE 88
MMO ANODE 89
MMO ANODE 90

MMO ANODE 91
MMO ANODE 92
MMO ANODE 93
MMO ANODE 94
MMO ANODE 95
MMO ANODE 96
MMO ANODE 97
MMO ANODE 98
MMO ANODE 99
MMO ANODE 100

MMO ANODE 101
MMO ANODE 102
MMO ANODE 103
MMO ANODE 104
MMO ANODE 105
MMO ANODE 106
MMO ANODE 107
MMO ANODE 108
MMO ANODE 109
MMO ANODE 110

MMO ANODE 111
MMO ANODE 112
MMO ANODE 113
MMO ANODE 114
MMO ANODE 115
MMO ANODE 116
MMO ANODE 117
MMO ANODE 118
MMO ANODE 119
MMO ANODE 120

REFERENCES

1251-100-S30-D99-0005
IN-PLANT PIPING LAYOUT
AGROOD-GPC-030

1251-100-S30-D99-0015
EQUIPMENT LAYOUT
AGROOD-GPC-030

1251-100-S30-E05-0005
CABLE SCHEDULE
AGROOD-GPC-030

SUPPLIER DOCUMENT REVIEW

- ☐ 1. Work may proceed.
- ☐ 2. Revise and resubmit in accordance with comments, work may proceed subject to incorporation of changes indicated
- ☐ 3. Revise and resubmit.(major comments)work may not proceed
- ☐ 4. Rejected.(reason to be specified on the document).
- ☐ 5. Hold for a specific reason(to be specified on the document).

PERMISSION TO PROCEED DOES NOT CONSTITUTE
ACCEPTANCE OR APPROVAL OF DESIGN DETAILS,
CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS
DEVELOPED OR SELECTED BY SUPPLIER FROM FULL
COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.

NAME

SIGNATURE

DATE:

PROJECT
TITLE

PACKAGE
DESCRIPTION

EQUIPMANT
TAG

CODE
IDENTIFIER

DOCUMENT NUMBER

NEW CRUDE OIL TANK
FARM PROJECT

CATHODIC PROTECTION

E10

SHEET 3 OF 7

REVISION

1

1	ISSUED FOR APPROVAL	N/A	PB	DC	14/01/21
0	ISSUED FOR REVIEW	N/A	PB	DC	23/10/20
No.	DESCRIPTION	DCR No.	BY	CHECK	DATE

corrpro[®]
An Aegion™ Company

Adam Street, Bowesfield Lane,
Stockton-on-Tees, Cleveland TS18 3HQ.
Tel: (01642) 614106. Fax: 614100 Telex: 587388

Information shown on this drawing is
confidential and must not be copied
or conveyed to third parties without
the express permission of Corpro
Companies Europe Ltd.
Certain items shown on this drawing are
subject to worldwide patent applications.

ENPPI		NEW CRUDE OIL TANK FARM PROJECT	
SINGLE LINE DIAGRAM AGROOD-GPC-030			
Drawn PB	Date 23/10/2020	Checked DC	Date 23/10/2020
Scale NTS	DRG. No. 34501020-DWG-030		Issue No. 1

400V AC 50Hz 3 PH. SUPPLY

50V 50A TRANSFORMER RECTIFIER

AG030-TR-004

35mm² XLPE/PVC CABLE

AG030-AJB-004

35mm² XLPE/PVC CABLE

35mm² XLPE/PVC CABLE

AG030-NJB-004

AG030-ASB-013

AG030-ASB-014

AG030-ASB-015

AG030-ASB-016

35mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

18"-FW-030-045-A3-N
6"-FW-030-102-A3-N
10"-CD-030-010-A3-N
8"-FW-030-086-A3-N

MMO ANODE 121
MMO ANODE 122
MMO ANODE 123
MMO ANODE 124
MMO ANODE 125
MMO ANODE 126
MMO ANODE 127
MMO ANODE 128
MMO ANODE 129
MMO ANODE 130

MMO ANODE 131
MMO ANODE 132
MMO ANODE 133
MMO ANODE 134
MMO ANODE 135
MMO ANODE 136
MMO ANODE 137
MMO ANODE 138
MMO ANODE 139
MMO ANODE 140

MMO ANODE 141
MMO ANODE 142
MMO ANODE 143
MMO ANODE 144
MMO ANODE 145
MMO ANODE 146
MMO ANODE 147
MMO ANODE 148
MMO ANODE 149
MMO ANODE 150

MMO ANODE 151
MMO ANODE 152
MMO ANODE 153
MMO ANODE 154
MMO ANODE 155
MMO ANODE 156
MMO ANODE 157
MMO ANODE 158
MMO ANODE 159
MMO ANODE 160

REFERENCES

1251-100-S30-D99-0005
IN-PLANT PIPING LAYOUT
AGROOD-GPC-030

1251-100-S30-D99-0015
EQUIPMENT LAYOUT
AGROOD-GPC-030

1251-100-S30-E05-0005
CABLE SCHEDULE
AGROOD-GPC-030

SUPPLIER DOUMENT REVIEW

- ☐ 1. Work may proceed.
- ☐ 2. Revise and resubmit in accordance with comments,work may proceed subject to incorporation of changes indicated
- ☐ 3. Revise and resubmit.(major comments)work may not proceed
- ☐ 4. Rejected.(reason to be specified on the document).
- ☐ 5. Hold for a specific reason(to be specified on the document).

PERMISSION TO PROCEED DOES NOT CONSTITUTE
ACCEPTANCE OR APPROVAL OF DESIGN DETAILS,
CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS
DEVELOPED OR SELECTED BY SUPPLIER FROM FULL
COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.

NAME

SIGNATURE

DATE:

PROJECT
TITLE

NEW CRUDE OIL TANK
FARM PROJECT

PACKAGE
DESCRIPTION

CATHODIC PROTECTION

EQUIPMANT
TAG

CODE
IDENTIFIER

E10

SHEET 4 OF 7

DOCUMENT NUMBER

1251-100-S30-E10-0005

REVISION

1

No.	DESCRIPTION	DCR No.	BY	CHECK	DATE
1	ISSUED FOR APPROVAL	N/A	PB	DC	14/01/21
0	ISSUED FOR REVIEW	N/A	PB	DC	23/10/20

corrpro[®]
An Aegion™ Company

Adam Street,Bowesfield Lane,
Stockton-on-Tees,Cleveland TS18 3HQ.
Tel: (01642) 614106. Fax: 614100 Telex: 587388

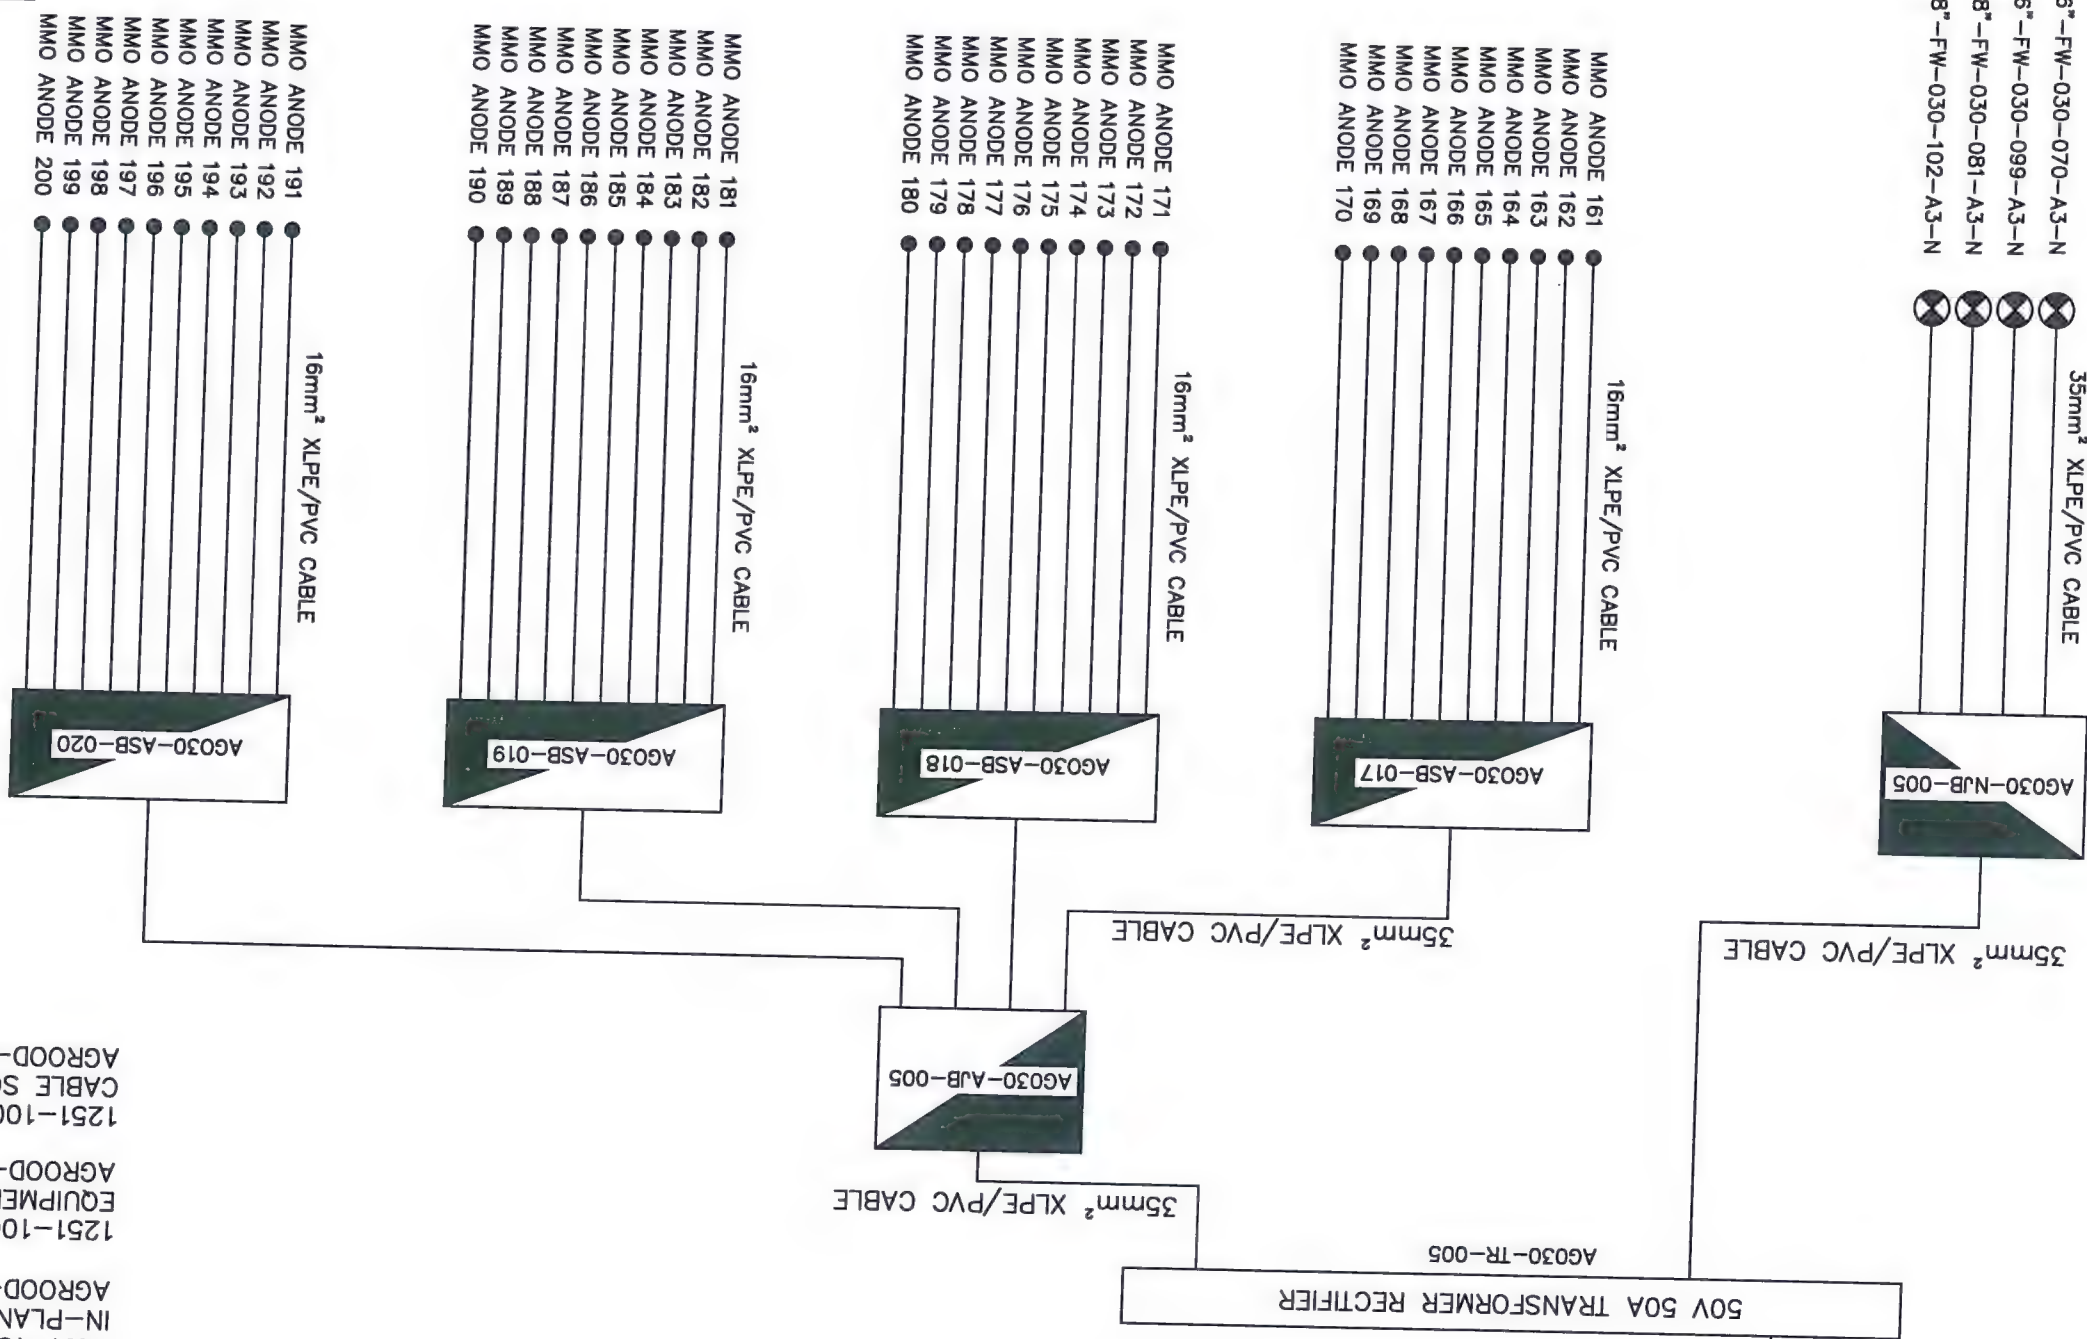
Information shown on this drawing is
confidential and must not be copied
or conveyed to third parties without
the express permission of Corpro
Companies Europe Ltd.
Certain items shown on this drawing are
subject to worldwide patent applications.

ENPPI NEW CRUDE OIL TANK FARM PROJECT

SINGLE LINE DIAGRAM
AGROOD-GPC-030

Drawn	Date	Checked	Date
PB	23/10/2020	DC	23/10/2020
Scale	DRG. No.	Issue No.	
NTS	34501020-DWG-030	1	

REFERENCES
1251-100-S30-D99-0005
IN-PLANT PIPING LAYOUT
AGROOD-GPC-030
1251-100-S30-D99-0015
EQUIPMENT LAYOUT
AGROOD-GPC-030
1251-100-S30-E05-0005
CABLE SCHEDULE
AGROOD-GPC-030



SIGNATURE		DATE:		1251-100-S30-E10-0005		Scale		NTS		34501020-DWG-030		Issue No.		1	
NAME		DOCUMENT NUMBER		REVISION		Drawn		PB		Date		23/10/2020		23/10/2020	
PERMISSION TO PROCEED DOES NOT CONSTITUTE ACCEPTANCE OR APPROVAL OF DESIGN DETAILS, CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS DEVELOPED OR SELECTED BY SUPPLIER FROM FULL COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.		CODE IDENTIFIER		E10		SHEET		5 OF 7		AGROOD-GPC-030		SINGLE LINE DIAGRAM		ENPPI	
1. Work may proceed.		2. Revise and resubmit in accordance with comments, work of changes indicated		3. Revise and resubmit (major comments) work may not proceed		4. Rejected (reason to be specified on the document).		5. Hold for a specific reason (to be specified on the document).		EQUIPMENT TAG		CATHODIC PROTECTION		FARM PROJECT	
PROJECT TITLE		PACKAGE DESCRIPTION		TAG		CODE IDENTIFIER		E10		SHEET		5 OF 7		REVISION	
PROJECT		NEW CRUDE OIL TANK		FARM PROJECT		CATHODIC PROTECTION		TAG		CODE IDENTIFIER		E10		SHEET	
14/01/21		PB		DC		23/10/20		DC		23/10/2020		Date		23/10/2020	
1		PB		DC		23/10/20		DC		23/10/2020		Date		23/10/2020	
1		PB		DC		23/10/20		DC		23/10/2020		Date		23/10/2020	

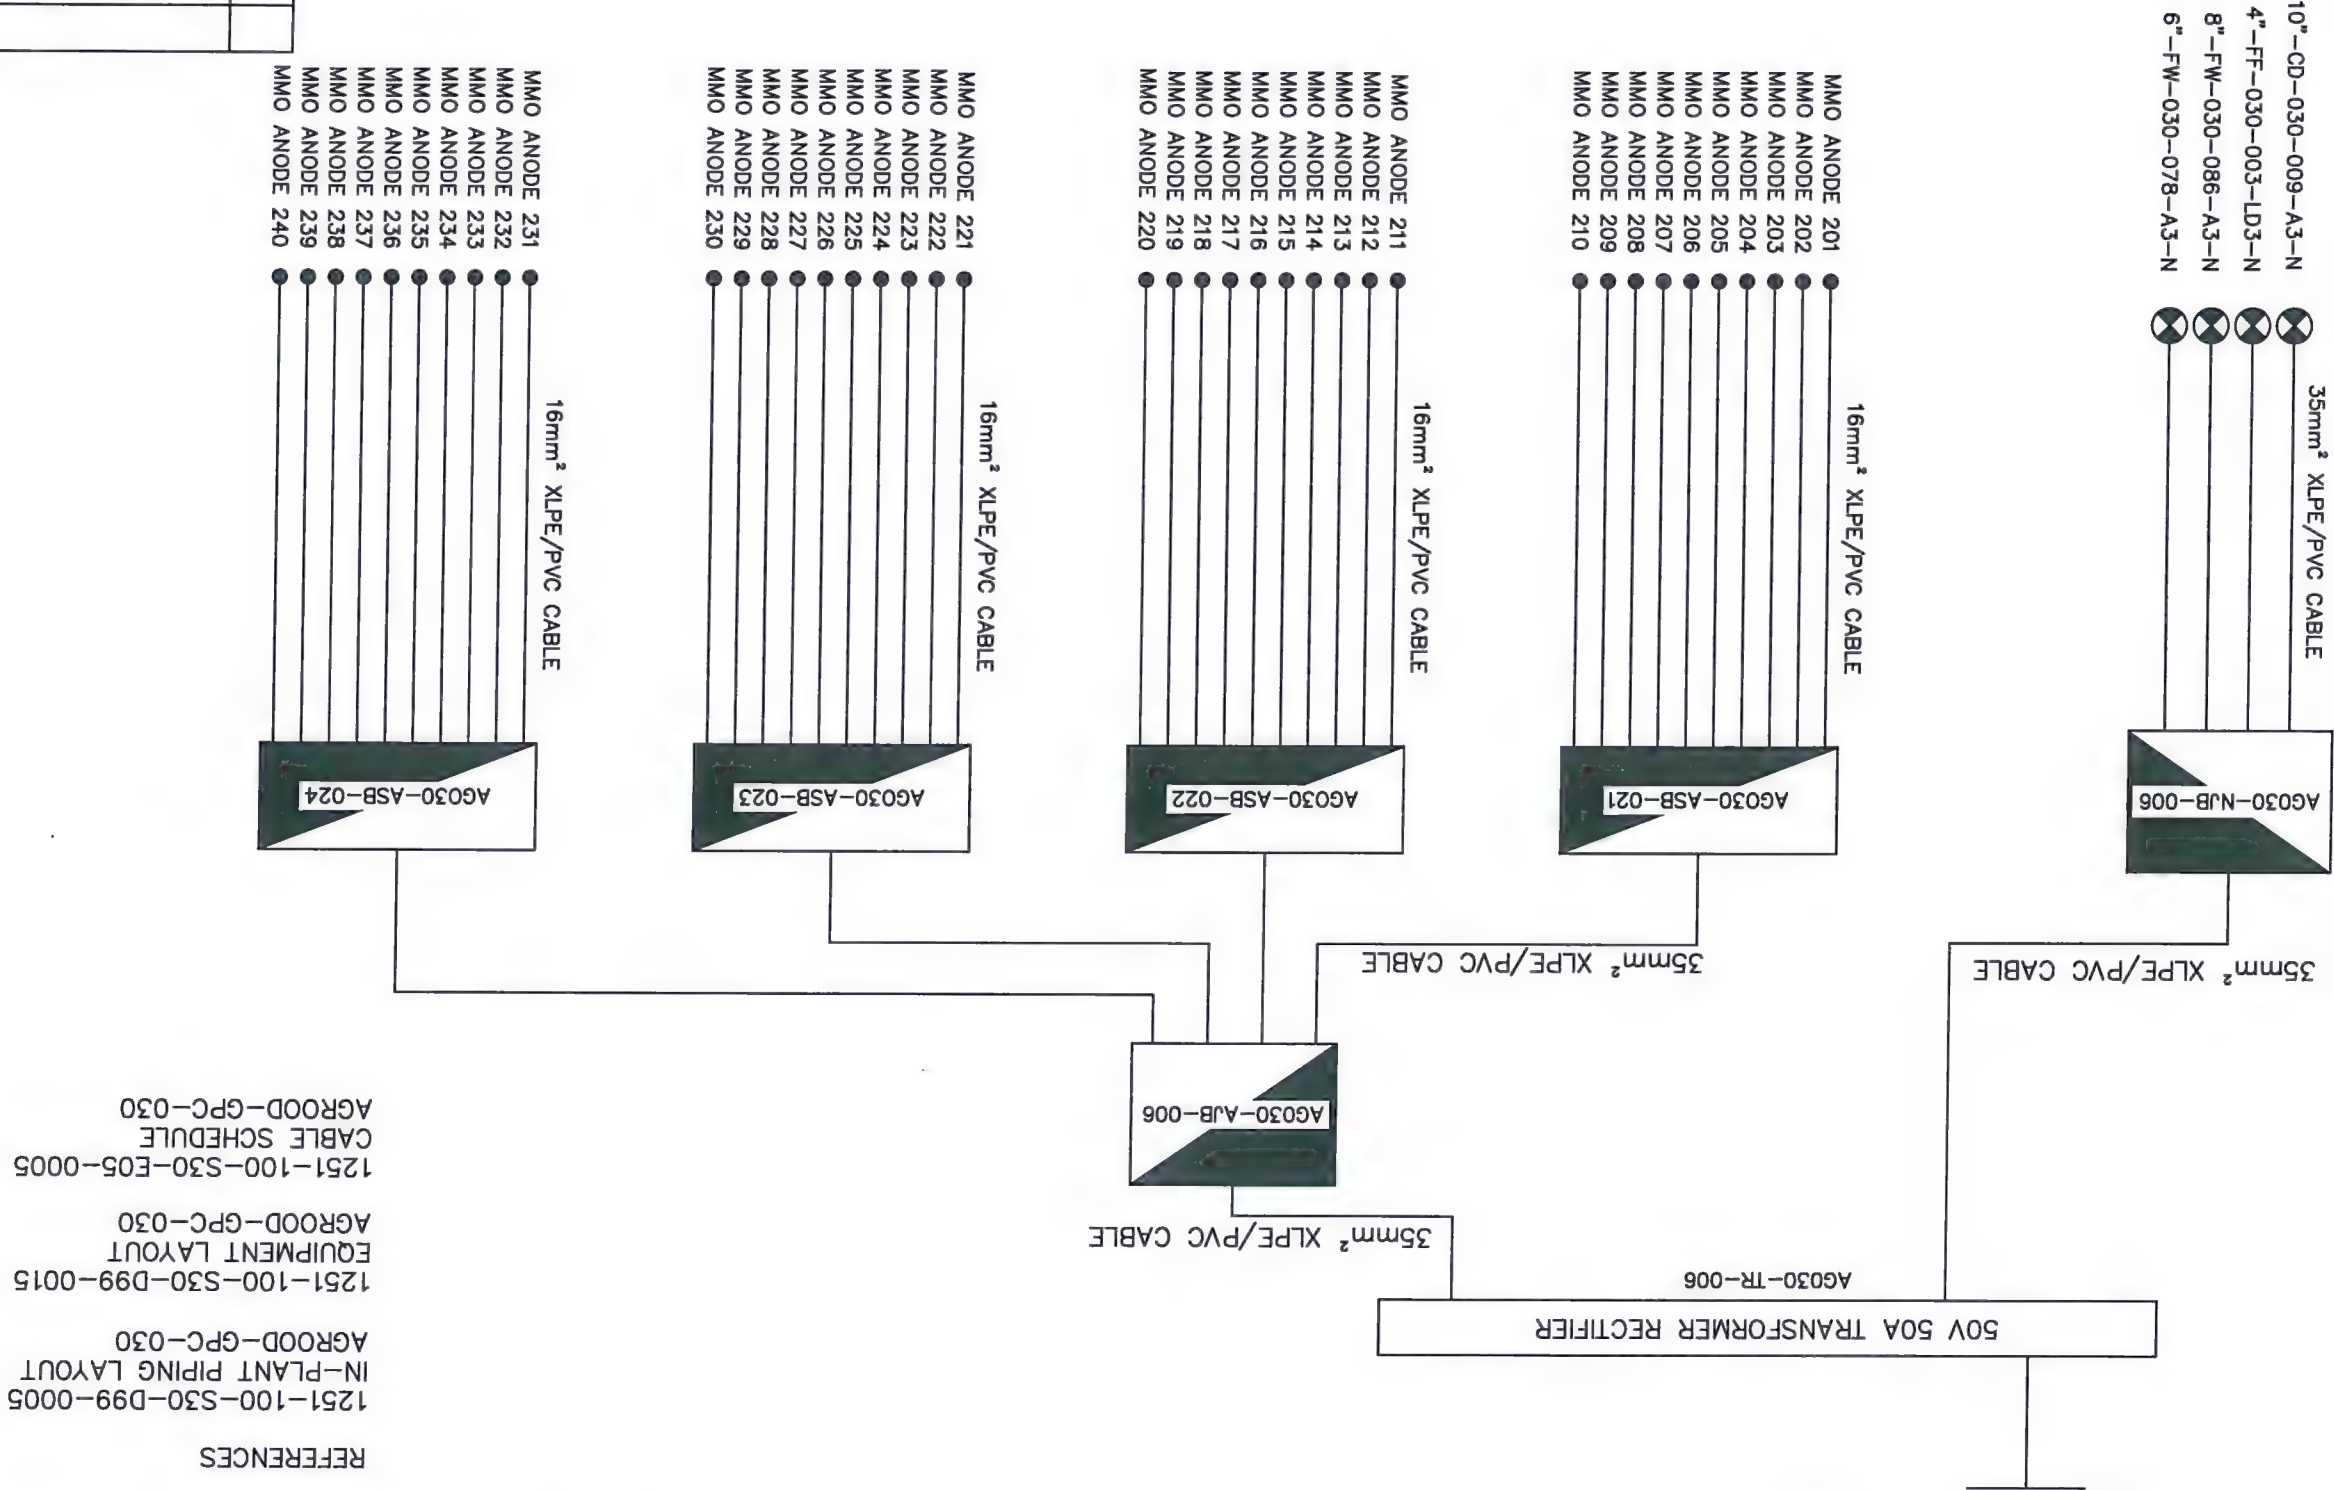
Information shown on this drawing is confidential and must not be copied or conveyed to third parties without the express permission of Compro Companies Europe Ltd.

Certain items shown on this drawing are subject to worldwide patent applications.

Adam Street, Bowesfield Lane, Stockton-on-Tees, Cleveland TS18 3HQ. Tel: (01642) 614106. Fax: 614100. Telex: 587388

compro An Aegion™ Company

400V AC 50Hz 3 PH. SUPPLY

[illegible]

6"-FW-030-096-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-101-A3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-095-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FF-030-004-LD3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-094-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-102-A3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-005-LD3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FF-030-004-LD3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-093-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-102-A3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-005-LD3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-101-A3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-093-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-100-A3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-094-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FF-030-003-LD3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-107-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-099-A3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-007-LD3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FF-030-003-LD3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-106-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-099-A3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-107-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-100-A3-N	35mm ² XLPE/PVC BONDING CABLE
8"-FW-030-108-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-114-A3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-008-LD3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FF-030-002-LD3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-109-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-115-A3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-008-LD3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FF-030-002-A3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-109-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-112-A3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-108-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FF-030-001-LD3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-118-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-112-A3-N	35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-153-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-113-A3-N	35mm ² XLPE/PVC BONDING CABLE
2"-WP-030-011-LD3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-113-A3-N	35mm ² XLPE/PVC BONDING CABLE
8"-SW-030-01	35mm ² XLPE/PVC BONDING CABLE	6"-FF-030-001-LD3-N	35mm ² XLPE/PVC BONDING CABLE
8"-SW-030-01	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-095-A3-N	35mm ² XLPE/PVC BONDING CABLE
8"-SW-030-02	35mm ² XLPE/PVC BONDING CABLE	6"-FF-030-006-LD3-N	35mm ² XLPE/PVC BONDING CABLE
6"-CD-030-215-A3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FW-030-096-A3-N	35mm ² XLPE/PVC BONDING CABLE
4"-FW-030-142-LD3-N	35mm ² XLPE/PVC BONDING CABLE	6"-FF-030-006-LD3-N	35mm ² XLPE/PVC BONDING CABLE

REFERENCES

1251-100-S30-D99-0005
IN-PLANT PIPING LAYOUT
AGROOD-GPC-030

1251-100-S30-D99-0015
EQUIPMENT LAYOUT
AGROOD-GPC-030

1251-100-S30-E05-0005
CABLE SCHEDULE
AGROOD-GPC-030

SIGNATURE		DATE:	
NAME		DOCUMENT NUMBER	
PERMISSION TO PROCEED DOES NOT CONSTITUTE ACCEPTANCE OR APPROVAL OF DESIGN DETAILS, CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS DEVELOPED OR SELECTED BY SUPPLIER FROM FULL COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.		REVISION	
<input type="checkbox"/> 1. Work may proceed. <input type="checkbox"/> 2. Revise and resubmit in accordance with comments,work of changes indicated <input type="checkbox"/> 3. Revise and resubmit.(major comments)work may not proceed <input type="checkbox"/> 4. Rejected.(reason to be specified on the document). <input type="checkbox"/> 5. Hold for a specific reason(to be specified on the document).		CODE IDENTIFIER	SHEET 7 OF 7
EQUIPAMENT TAG		E10	
PACKAGE DESCRIPTION		CATHODIC PROTECTION	
PROJECT TITLE		FARM PROJECT	
SUPPLIER DOCUMENT REVIEW		NEW CRUDE OIL TANK	
1251-100-S30-E10-0005		1	

Scale	NTS	DRG. No.	34501020-DWG-030
Drawn	PB	Date	23/10/2020
		Checked	DC
		Date	23/10/2020
		Issue No.	1

ENPPI

SINGLE LINE DIAGRAM

AGROOD-GPC-030

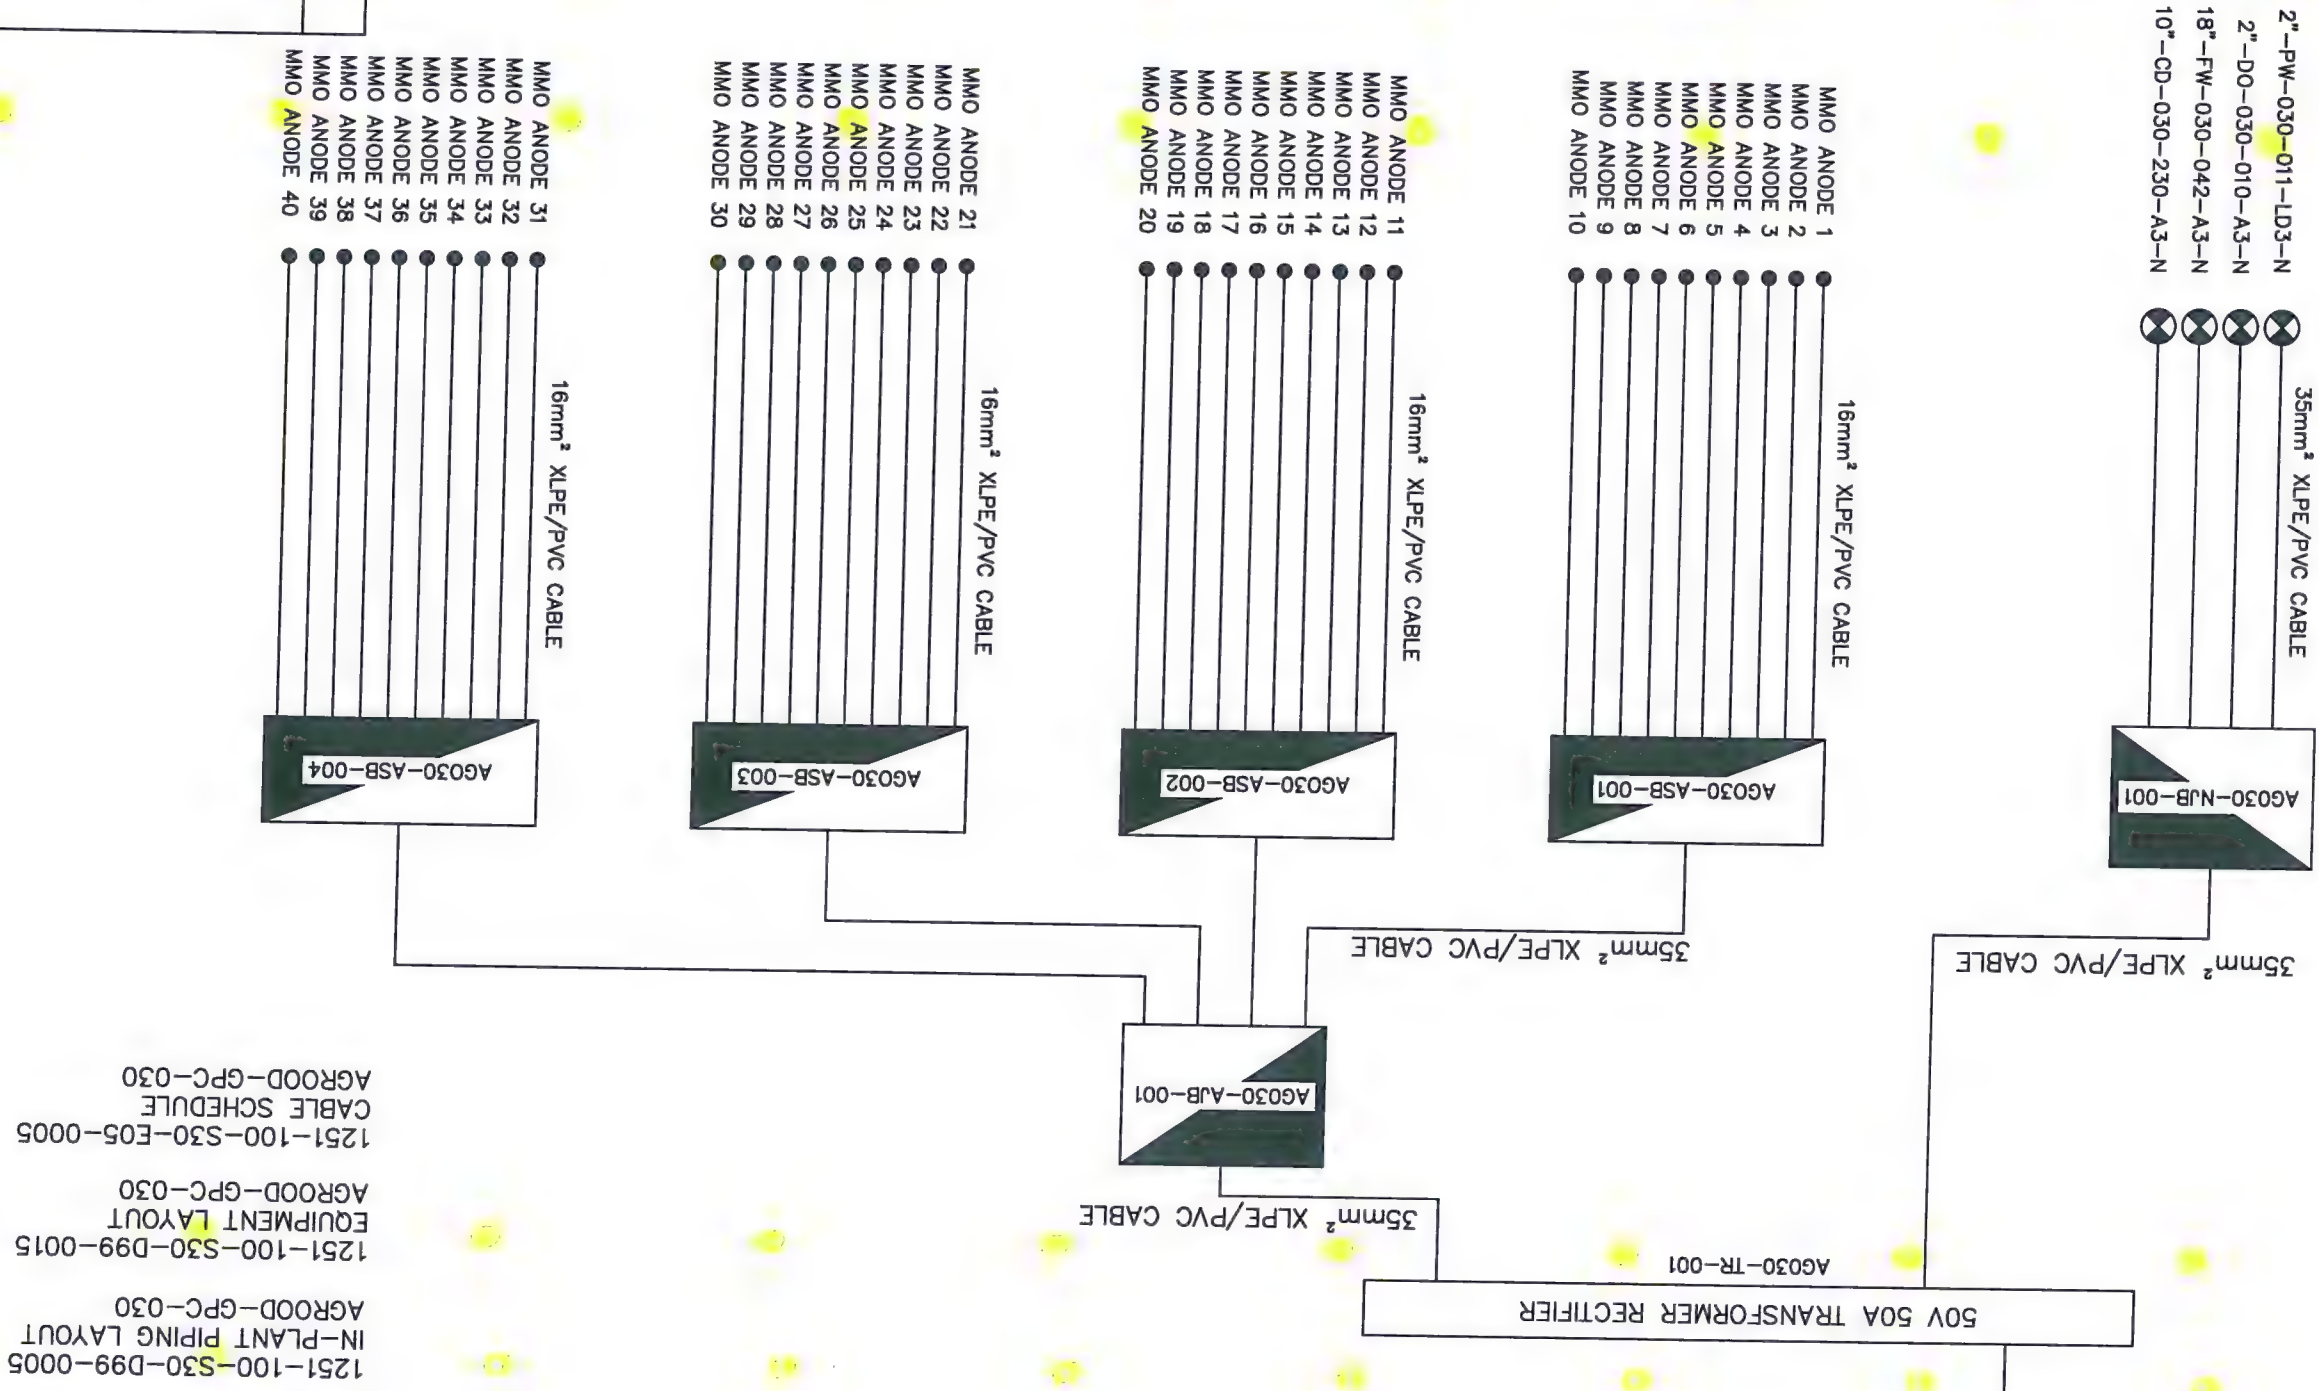
NEW CRUDE OIL TANK FARM PROJECT

Adam Street,Bowesfield Lane,
Stockton-on-Tees,Cleveland TS18 3HQ.
Tel: (01642) 614106. Fax: 614100 Telex: 587388
Companies Europe Ltd.
Information shown on this drawing is
confidential and must not be copied
or conveyed to third parties without
the express permission of Compro

compro
An Aegion™ Company

No.	DESCRIPTION	DCR No.	BY	CHECK	DATE
0	ISSUED FOR REVIEW	N/A	PB	DC	23/10/20
1	ISSUED FOR APPROVAL	N/A	PB	DC	14/01/21

400V AC 50Hz 3 PH. SUPPLY

[illegible]

400V AC 50Hz 3 PH. SUPPLY

50V 50A TRANSFORMER RECTIFIER

AG030-TR-002

35mm² XLPE/PVC CABLE

AG030-AJB-002

35mm² XLPE/PVC CABLE

AG030-NJB-002

35mm² XLPE/PVC CABLE

AG030-ASB-005

AG030-ASB-006

AG030-ASB-007

AG030-ASB-008

REFERENCES

1251-100-S30-D99-0005
IN-PLANT PIPING LAYOUT
AGROOD-GPC-030

1251-100-S30-D99-0015
EQUIPMENT LAYOUT
AGROOD-GPC-030

1251-100-S30-E05-0005
CABLE SCHEDULE
AGROOD-GPC-030

35mm² XLPE/PVC CABLE

6"-FW-030-054-A3-N
10"-CD-030-002-A3-N
6"-FW-030-109-A3-N
6"-FW-030-106-A3-N

16mm² XLPE/PVC CABLE

MMO ANODE 41
MMO ANODE 42
MMO ANODE 43
MMO ANODE 44
MMO ANODE 45
MMO ANODE 46
MMO ANODE 47
MMO ANODE 48
MMO ANODE 49
MMO ANODE 50

16mm² XLPE/PVC CABLE

MMO ANODE 51
MMO ANODE 52
MMO ANODE 53
MMO ANODE 54
MMO ANODE 55
MMO ANODE 56
MMO ANODE 57
MMO ANODE 58
MMO ANODE 59
MMO ANODE 60

16mm² XLPE/PVC CABLE

MMO ANODE 61
MMO ANODE 62
MMO ANODE 63
MMO ANODE 64
MMO ANODE 65
MMO ANODE 66
MMO ANODE 67
MMO ANODE 68
MMO ANODE 69
MMO ANODE 70

16mm² XLPE/PVC CABLE

MMO ANODE 71
MMO ANODE 72
MMO ANODE 73
MMO ANODE 74
MMO ANODE 75
MMO ANODE 76
MMO ANODE 77
MMO ANODE 78
MMO ANODE 79
MMO ANODE 80

SUPPLIER DOUMENT REVIEW

- ☐ 1. Work may proceed.
- ☐ 2. Revise and resubmit in accordance with comments,work may proceed subject to incorporation of changes indicated
- ☐ 3. Revise and resubmit.(major comments)work may not proceed
- ☐ 4. Rejected.(reason to be specified on the document).
- ☐ 5. Hold for a specific reason(to be specified on the document).

PERMISSION TO PROCEED DOES NOT CONSTITUTE ACCEPTANCE OR APPROVAL OF DESIGN DETAILS, CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS DEVELOPED OR SELECTED BY SUPPLIER FROM FULL COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.

NAME

SIGNATURE

DATE:

PROJECT
TITLE

NEW CRUDE OIL TANK
FARM PROJECT

PACKAGE
DESCRIPTION

CATHODIC PROTECTION

EQUIPMANT
TAG

CODE
IDENTIFIER

E10

SHEET 2 OF 7

DOCUMENT NUMBER

1251-100-S30-E10-0005

REVISION

1

1	ISSUED FOR APPROVAL	N/A	PB	DC	14/01/21
0	ISSUED FOR REVIEW	N/A	PB	DC	23/10/20

No.	DESCRIPTION	DCR No.	BY	CHECK	DATE
-----	-------------	---------	----	-------	------

Corpro
An Aegion™ Company

Adam Street,Bowesfield Lane,
Stockton-on-Tees,Cleveland TS18 3HQ.
Tel: (01642) 614106. Fax: 614100 Telex: 587388

Information shown on this drawing is confidential and must not be copied or conveyed to third parties without the express permission of Corpro Companies Europe Ltd.
Certain items shown on this drawing are subject to worldwide patent applications.

ENPPI	NEW CRUDE OIL TANK FARM PROJECT
-------	---------------------------------

SINGLE LINE DIAGRAM
AGROOD-GPC-030

Drawn	PB	Date	23/10/2020	Checked	DC	Date	23/10/2020
Scale	NTS	DRG. No.	24501000	Issue No.			

400V AC 50Hz 3 PH. SUPPLY

50V 50A TRANSFORMER RECTIFIER

AG030-TR-003

35mm² XLPE/PVC CABLE

AG030-AJB-003

35mm² XLPE/PVC CABLE

35mm² XLPE/PVC CABLE

AG030-NJB-003

AG030-ASB-009

AG030-ASB-010

AG030-ASB-011

AG030-ASB-012

35mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

6"-FW-030-056-A3-N
10"-CD-030-011-A3-N
6"-FW-030-096-A3-N
6"-FW-030-099-A3-N

MMO ANODE 81
MMO ANODE 82
MMO ANODE 83
MMO ANODE 84
MMO ANODE 85
MMO ANODE 86
MMO ANODE 87
MMO ANODE 88
MMO ANODE 89
MMO ANODE 90

MMO ANODE 91
MMO ANODE 92
MMO ANODE 93
MMO ANODE 94
MMO ANODE 95
MMO ANODE 96
MMO ANODE 97
MMO ANODE 98
MMO ANODE 99
MMO ANODE 100

MMO ANODE 101
MMO ANODE 102
MMO ANODE 103
MMO ANODE 104
MMO ANODE 105
MMO ANODE 106
MMO ANODE 107
MMO ANODE 108
MMO ANODE 109
MMO ANODE 110

MMO ANODE 111
MMO ANODE 112
MMO ANODE 113
MMO ANODE 114
MMO ANODE 115
MMO ANODE 116
MMO ANODE 117
MMO ANODE 118
MMO ANODE 119
MMO ANODE 120

REFERENCES

1251-100-S30-D99-0005
IN-PLANT PIPING LAYOUT
AGROOD-GPC-030

1251-100-S30-D99-0015
EQUIPMENT LAYOUT
AGROOD-GPC-030

1251-100-S30-E05-0005
CABLE SCHEDULE
AGROOD-GPC-030

SUPPLIER DOUMENT REVIEW

- ☐ 1. Work may proceed.
- ☐ 2. Revise and resubmit in accordance with comments,work may proceed subject to incorporation of changes indicated
- ☐ 3. Revise and resubmit.(major comments)work may not proceed
- ☐ 4. Rejected.(reason to be specified on the document).
- ☐ 5. Hold for a specific reason(to be specified on the document).

PERMISSION TO PROCEED DOES NOT CONSTITUTE ACCEPTANCE OR APPROVAL OF DESIGN DETAILS, CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS DEVELOPED OR SELECTED BY SUPPLIER FROM FULL COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.

NAME

SIGNATURE

DATE:

PROJECT
TITLE

NEW CRUDE OIL TANK
FARM PROJECT

PACKAGE
DESCRIPTION

CATHODIC PROTECTION

EQUIPMANT
TAG

CODE
IDENTIFIER

E10

SHEET 3 OF 7

DOCUMENT NUMBER

1251-100-S30-E10-0005

REVISION

1

1	ISSUED FOR APPROVAL	N/A	PB	DC	14/01/21
0	ISSUED FOR REVIEW	N/A	PB	DC	23/10/20

No.	DESCRIPTION	DCR No.	BY	CHECK	DATE
-----	-------------	---------	----	-------	------

Corpro
An Aegion™ Company

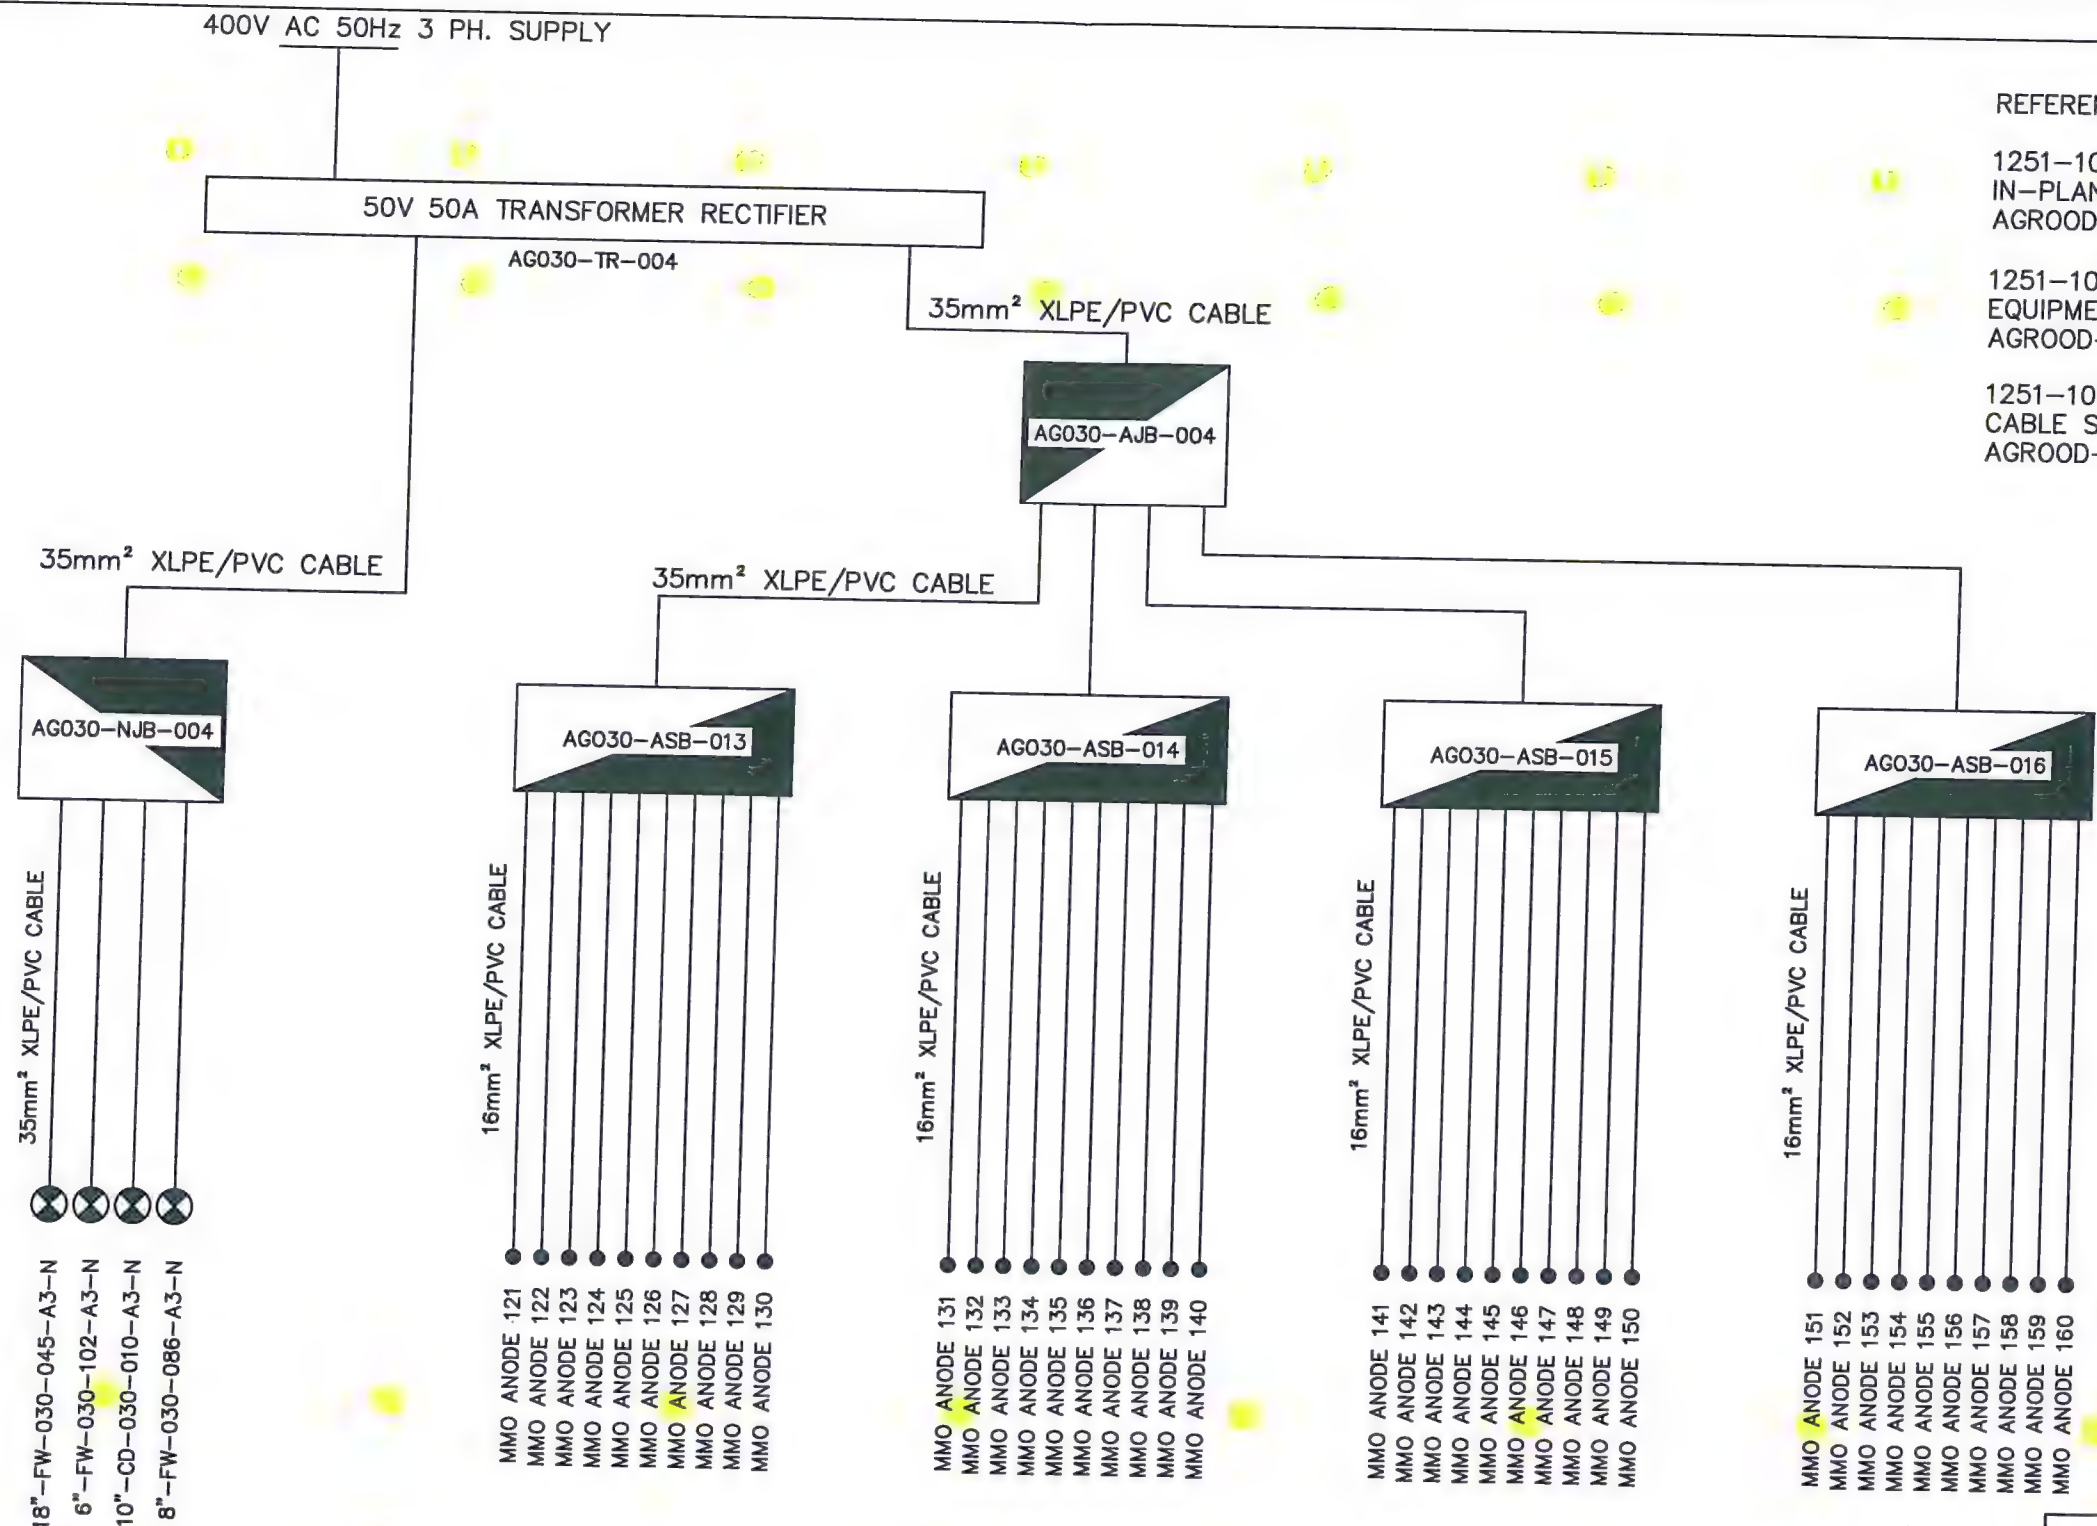
Adam Street,Bowesfield Lane,
Stockton-on-Tees,Cleveland TS18 3HQ.
Tel: (01642) 614106. Fax: 614100 Telex: 587388

Information shown on this drawing is confidential and must not be copied or conveyed to third parties without the express permission of Corpro Companies Europe Ltd. Certain items shown on this drawing are subject to worldwide patent applications.

ENPPI	NEW CRUDE OIL TANK FARM PROJECT
-------	---------------------------------

SINGLE LINE DIAGRAM
AGROOD-GPC-030

Drawn	PB	Date	23/10/2020	Checked	DC	Date	23/10/2020
Scale	NTS	DRG. No.	24501000	Issue No.			



REFERENCES

1251-100-S30-D99-0005
IN-PLANT PIPING LAYOUT
AGROOD-GPC-030

1251-100-S30-D99-0015
EQUIPMENT LAYOUT
AGROOD-GPC-030

1251-100-S30-E05-0005
CABLE SCHEDULE
AGROOD-GPC-030

SUPPLIER DOCUMENT REVIEW		PROJECT TITLE		NEW CRUDE OIL TANK FARM PROJECT	
<input type="checkbox"/> 1. Work may proceed.		PACKAGE DESCRIPTION		CATHODIC PROTECTION	
<input type="checkbox"/> 2. Revise and resubmit in accordance with comments, work may proceed subject to incorporation of changes indicated		EQUIPMENT TAG			
<input type="checkbox"/> 3. Revise and resubmit.(major comments)work may not proceed		CODE IDENTIFIER		E10 SHEET 4 OF 7	
<input type="checkbox"/> 4. Rejected.(reason to be specified on the document).		DOCUMENT NUMBER		1251-100-S30-E10-0005	
<input type="checkbox"/> 5. Hold for a specific reason(to be specified on the document).		REVISION		1	
PERMISSION TO PROCEED DOES NOT CONSTITUTE ACCEPTANCE OR APPROVAL OF DESIGN DETAILS, CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS DEVELOPED OR SELECTED BY SUPPLIER FROM FULL COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.					
NAME					
SIGNATURE		DATE:			

1	ISSUED FOR APPROVAL	N/A	PB	DC	14/01/21
0	ISSUED FOR REVIEW	N/A	PB	DC	23/10/20
No.	DESCRIPTION	DCR No.	BY	CHECK	DATE
Corpro An Aegion™ Company Adam Street, Bowesfield Lane, Stockton-on-Tees, Cleveland TS18 3HQ. Tel: (01642) 614106. Fax: 614100 Telex: 587388					
Information shown on this drawing is confidential and must not be copied or conveyed to third parties without the express permission of Corpro Companies Europe Ltd. Certain items shown on this drawing are subject to worldwide patent applications.					
ENPPI		NEW CRUDE OIL TANK FARM PROJECT			
SINGLE LINE DIAGRAM AGROOD-GPC-030					
Drawn	PB	Date	23/10/2020	Checked	DC
Scale	NTS	DRG. No.	34501020-DWG-030	Issue No.	1

400V AC 50Hz 3 PH. SUPPLY

50V 50A TRANSFORMER RECTIFIER

AG030-TR-005

35mm² XLPE/PVC CABLE

AG030-AJB-005

35mm² XLPE/PVC CABLE

35mm² XLPE/PVC CABLE

AG030-NJB-005

AG030-ASB-017

AG030-ASB-018

AG030-ASB-019

AG030-ASB-020

35mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

16mm² XLPE/PVC CABLE

6"-FW-030-070-A3-N
6"-FW-030-099-A3-N
8"-FW-030-081-A3-N
8"-FW-030-102-A3-N

MMO ANODE 161
MMO ANODE 162
MMO ANODE 163
MMO ANODE 164
MMO ANODE 165
MMO ANODE 166
MMO ANODE 167
MMO ANODE 168
MMO ANODE 169
MMO ANODE 170

MMO ANODE 171
MMO ANODE 172
MMO ANODE 173
MMO ANODE 174
MMO ANODE 175
MMO ANODE 176
MMO ANODE 177
MMO ANODE 178
MMO ANODE 179
MMO ANODE 180

MMO ANODE 181
MMO ANODE 182
MMO ANODE 183
MMO ANODE 184
MMO ANODE 185
MMO ANODE 186
MMO ANODE 187
MMO ANODE 188
MMO ANODE 189
MMO ANODE 190

MMO ANODE 191
MMO ANODE 192
MMO ANODE 193
MMO ANODE 194
MMO ANODE 195
MMO ANODE 196
MMO ANODE 197
MMO ANODE 198
MMO ANODE 199
MMO ANODE 200

REFERENCES

1251-100-S30-D99-0005
IN-PLANT PIPING LAYOUT
AGROOD-GPC-030

1251-100-S30-D99-0015
EQUIPMENT LAYOUT
AGROOD-GPC-030

1251-100-S30-E05-0005
CABLE SCHEDULE
AGROOD-GPC-030

SUPPLIER DOUMENT REVIEW		PROJECT TITLE	NEW CRUDE OIL TANK FARM PROJECT	
<input type="checkbox"/> 1. Work may proceed.		PACKAGE DESCRIPTION	CATHODIC PROTECTION	
<input type="checkbox"/> 2. Revise and resubmit in accordance with comments,work may proceed subject to incorporation of changes indicated		EQUIPMANT TAG		
<input type="checkbox"/> 3. Revise and resubmit.(major comments)work may not proceed		CODE IDENTIFIER	E10	SHEET 5 OF 7
<input type="checkbox"/> 4. Rejected.(reason to be specified on the document).		NAME	DOCUMENT NUMBER	REVISION
<input type="checkbox"/> 5. Hold for a specific reason(to be specified on the document).		SIGNATURE	DATE:	
PERMISSION TO PROCEED DOES NOT CONSTITUTE ACCEPTANCE OR APPROVAL OF DESIGN DETAILS, CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS DEVELOPED OR SELECTED BY SUPPLIER FROM FULL COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.		1251-100-S30-E10-0005 1		

1	ISSUED FOR APPROVAL	N/A	PB	DC	14/01/21
0	ISSUED FOR REVIEW	N/A	PB	DC	23/10/20
No.	DESCRIPTION	DCR No.	BY	CHECK	DATE
corrpro An Aegion™ Company					
Adam Street,Bowesfield Lane, Stockton-on-Tees,Cleveland TS18 3HQ. Tel: (01642) 614106. Fax: 614100 Telex: 587388					
Information shown on this drawing is confidential and must not be copied or conveyed to third parties without the express permission of Corpro Companies Europe Ltd. Certain items shown on this drawing are subject to worldwide patent applications.					
ENPPI		NEW CRUDE OIL TANK FARM PROJECT			
SINGLE LINE DIAGRAM AGROOD-GPC-030					
Drawn	PB	Date	23/10/2020	Checked	DC
Scale	NTS	DRG. No.	34501020-DWG-030	Issue No.	1

400V AC 50Hz 3 PH. SUPPLY

50V 50A TRANSFORMER RECTIFIER

AG030-TR-006

35mm² XLPE/PVC CABLE

AG030-AJB-006

35mm² XLPE/PVC CABLE

AG030-NJB-006

35mm² XLPE/PVC CABLE

AG030-ASB-021

AG030-ASB-022

AG030-ASB-023

AG030-ASB-024

35mm² XLPE/PVC CABLE



10"-CD-030-009-A3-N
4"-FF-030-003-LD3-N
8"-FW-030-086-A3-N
6"-FW-030-078-A3-N

16mm² XLPE/PVC CABLE

MMO ANODE 201
MMO ANODE 202
MMO ANODE 203
MMO ANODE 204
MMO ANODE 205
MMO ANODE 206
MMO ANODE 207
MMO ANODE 208
MMO ANODE 209
MMO ANODE 210

16mm² XLPE/PVC CABLE

MMO ANODE 211
MMO ANODE 212
MMO ANODE 213
MMO ANODE 214
MMO ANODE 215
MMO ANODE 216
MMO ANODE 217
MMO ANODE 218
MMO ANODE 219
MMO ANODE 220

16mm² XLPE/PVC CABLE

MMO ANODE 221
MMO ANODE 222
MMO ANODE 223
MMO ANODE 224
MMO ANODE 225
MMO ANODE 226
MMO ANODE 227
MMO ANODE 228
MMO ANODE 229
MMO ANODE 230

16mm² XLPE/PVC CABLE

MMO ANODE 231
MMO ANODE 232
MMO ANODE 233
MMO ANODE 234
MMO ANODE 235
MMO ANODE 236
MMO ANODE 237
MMO ANODE 238
MMO ANODE 239
MMO ANODE 240

REFERENCES

1251-100-S30-D99-0005
IN-PLANT PIPING LAYOUT
AGROOD-GPC-030

1251-100-S30-D99-0015
EQUIPMENT LAYOUT
AGROOD-GPC-030

1251-100-S30-E05-0005
CABLE SCHEDULE
AGROOD-GPC-030

SUPPLIER DOUMENT REVIEW		PROJECT TITLE		NEW CRUDE OIL TANK FARM PROJECT	
<input type="checkbox"/> 1. Work may proceed.		PACKAGE DESCRIPTION		CATHODIC PROTECTION	
<input type="checkbox"/> 2. Revise and resubmit in accordance with comments,work may proceed subject to incorporation of changes indicated		EQUIPMANT TAG			
<input type="checkbox"/> 3. Revise and resubmit.(major comments)work may not proceed		CODE IDENTIFIER		E10 SHEET 6 OF 7	
<input type="checkbox"/> 4. Rejected.(reason to be specified on the document).		DOCUMENT NUMBER		1251-100-S30-E10-0005	
<input type="checkbox"/> 5. Hold for a specific reason(to be specified on the document).		REVISION		1	
PERMISSION TO PROCEED DOES NOT CONSTITUTE ACCEPTANCE OR APPROVAL OF DESIGN DETAILS, CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS DEVELOPED OR SELECTED BY SUPPLIER FROM FULL COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.					
NAME					
SIGNATURE		DATE:			

1	ISSUED FOR APPROVAL	N/A	PB	DC	14/01/21
0	ISSUED FOR REVIEW	N/A	PB	DC	23/10/20
No.	DESCRIPTION	DCR No.	BY	CHECK	DATE

Corrpro
An Aegion™ Company





























Adam Street, Bowesfield Lane,
Stockton-on-Tees, Cleveland TS18 3HQ.
Tel: (01642) 614106. Fax: 614100 Telex: 587388





























Information shown on this drawing is confidential and must not be copied or conveyed to third parties without the express permission of Corrpro Companies Europe Ltd.
Certain items shown on this drawing are subject to worldwide patent applications.

ENPPI NEW CRUDE OIL TANK FARM PROJECT

SINGLE LINE DIAGRAM
AGROOD-GPC-030

Drawn	PB	Date	23/10/2020	Checked	DC	Date	23/10/2020
Scale	NTS	DRG. No.	34501020-DWC-030	Issue No.	1		

6" -FW-030-096-A3-N		35mm ² XLPE/PVC BONDING CABLE
6" -FW-030-095-A3-N		
6" -FW-030-094-A3-N		35mm ² XLPE/PVC BONDING CABLE
8" -FF-030-005-LD3-N		
6" -FW-030-093-A3-N		35mm ² XLPE/PVC BONDING CABLE
8" -FF-030-005-LD3-N		
6" -FW-030-093-A3-N		35mm ² XLPE/PVC BONDING CABLE
6" -FW-030-094-A3-N		
6" -FW-030-107-A3-N		35mm ² XLPE/PVC BONDING CABLE
6" -FF-030-007-LD3-N		
6" -FW-030-106-A3-N		35mm ² XLPE/PVC BONDING CABLE
6" -FF-030-007-LD3-N		
6" -FW-030-106-A3-N		35mm ² XLPE/PVC BONDING CABLE
6" -FW-030-107-A3-N		
8" -FW-030-108-A3-N		35mm ² XLPE/PVC BONDING CABLE
6" -FF-030-008-LD3-N		
6" -FW-030-109-A3-N		35mm ² XLPE/PVC BONDING CABLE
6" -FF-030-008-LD3-N		
6" -FW-030-109-A3-N		35mm ² XLPE/PVC BONDING CABLE
6" -FW-030-108-A3-N		
6" -FW-030-118-A3-N		35mm ² XLPE/PVC BONDING CABLE
6" -FW-030-153-A3-N		
2" -WP-030-011-LD3-N		35mm ² XLPE/PVC BONDING CABLE
8" -SW-030-01		
8" -SW-030-01		35mm ² XLPE/PVC BONDING CABLE
8" -SW-030-02		
6" -CD-030-215-A3-N		35mm ² XLPE/PVC BONDING CABLE
4" -FW-030-142-LD3-N		

6"-FW-030-101-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-004-LD3-N		
6"-FW-030-102-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-004-LD3-N		
6"-FW-030-102-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-101-A3-N		
6"-FW-030-100-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-003-LD3-N		
6"-FW-030-099-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-003-LD3-N		
6"-FW-030-099-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-100-A3-N		
6"-FW-030-114-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-002-LD3-N		
6"-FW-030-114-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-115-A3-N		
6"-FW-030-115-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-002-A3-N		
6"-FW-030-112-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-001-LD3-N		
6"-FW-030-112-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FW-030-113-A3-N		
6"-FW-030-113-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-001-LD3-N		
6"-FW-030-095-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-006-LD3-N		
6"-FW-030-096-A3-N		35mm ² XLPE/PVC BONDING CABLE
6"-FF-030-006-LD3-N		

REFERENCES


1251-100-S30-D99-0005
IN-PLANT PIPING LAYOUT
AGROOD-GPC-030

1251-100-S30-D99-0015
EQUIPMENT LAYOUT
AGROOD-GPC-030

1251-100-S30-E05-0005
CABLE SCHEDULE
AGROOD-GPC-030

SUPPLIER DOCUMENT REVIEW		PROJECT TITLE	NEW CRUDE OIL TANK FARM PROJECT	
<input type="checkbox"/> 1. Work may proceed.	PERMISSION TO PROCEED DOES NOT CONSTITUTE ACCEPTANCE OR APPROVAL OF DESIGN-DETAILS, CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS DEVELOPED OR SELECTED BY SUPPLIER FROM FULL COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.	PACKAGE DESCRIPTION	CATHODIC PROTECTION	
<input type="checkbox"/> 2. Revise and resubmit in accordance with comments, work may proceed subject to incorporation of changes indicated		EQUIPMENT TAG		
<input type="checkbox"/> 3. Revise and resubmit.(major comments)work may not proceed		CODE IDENTIFIER	E10	SHEET 7 OF 7
<input type="checkbox"/> 4. Rejected.(reason to be specified on the document).				
<input type="checkbox"/> 5. Hold for a specific reason(to be specified on the document).				
NAME		DOCUMENT NUMBER		REVISION
SIGNATURE	DATE:	1251-100-S30-E10-0005		1

1	ISSUED FOR APPROVAL	N/A	PB	DC	14/01/21
0	ISSUED FOR REVIEW	N/A	PB	DC	23/10/20
No.	DESCRIPTION	DCR No.	BY	CHECK	DATE

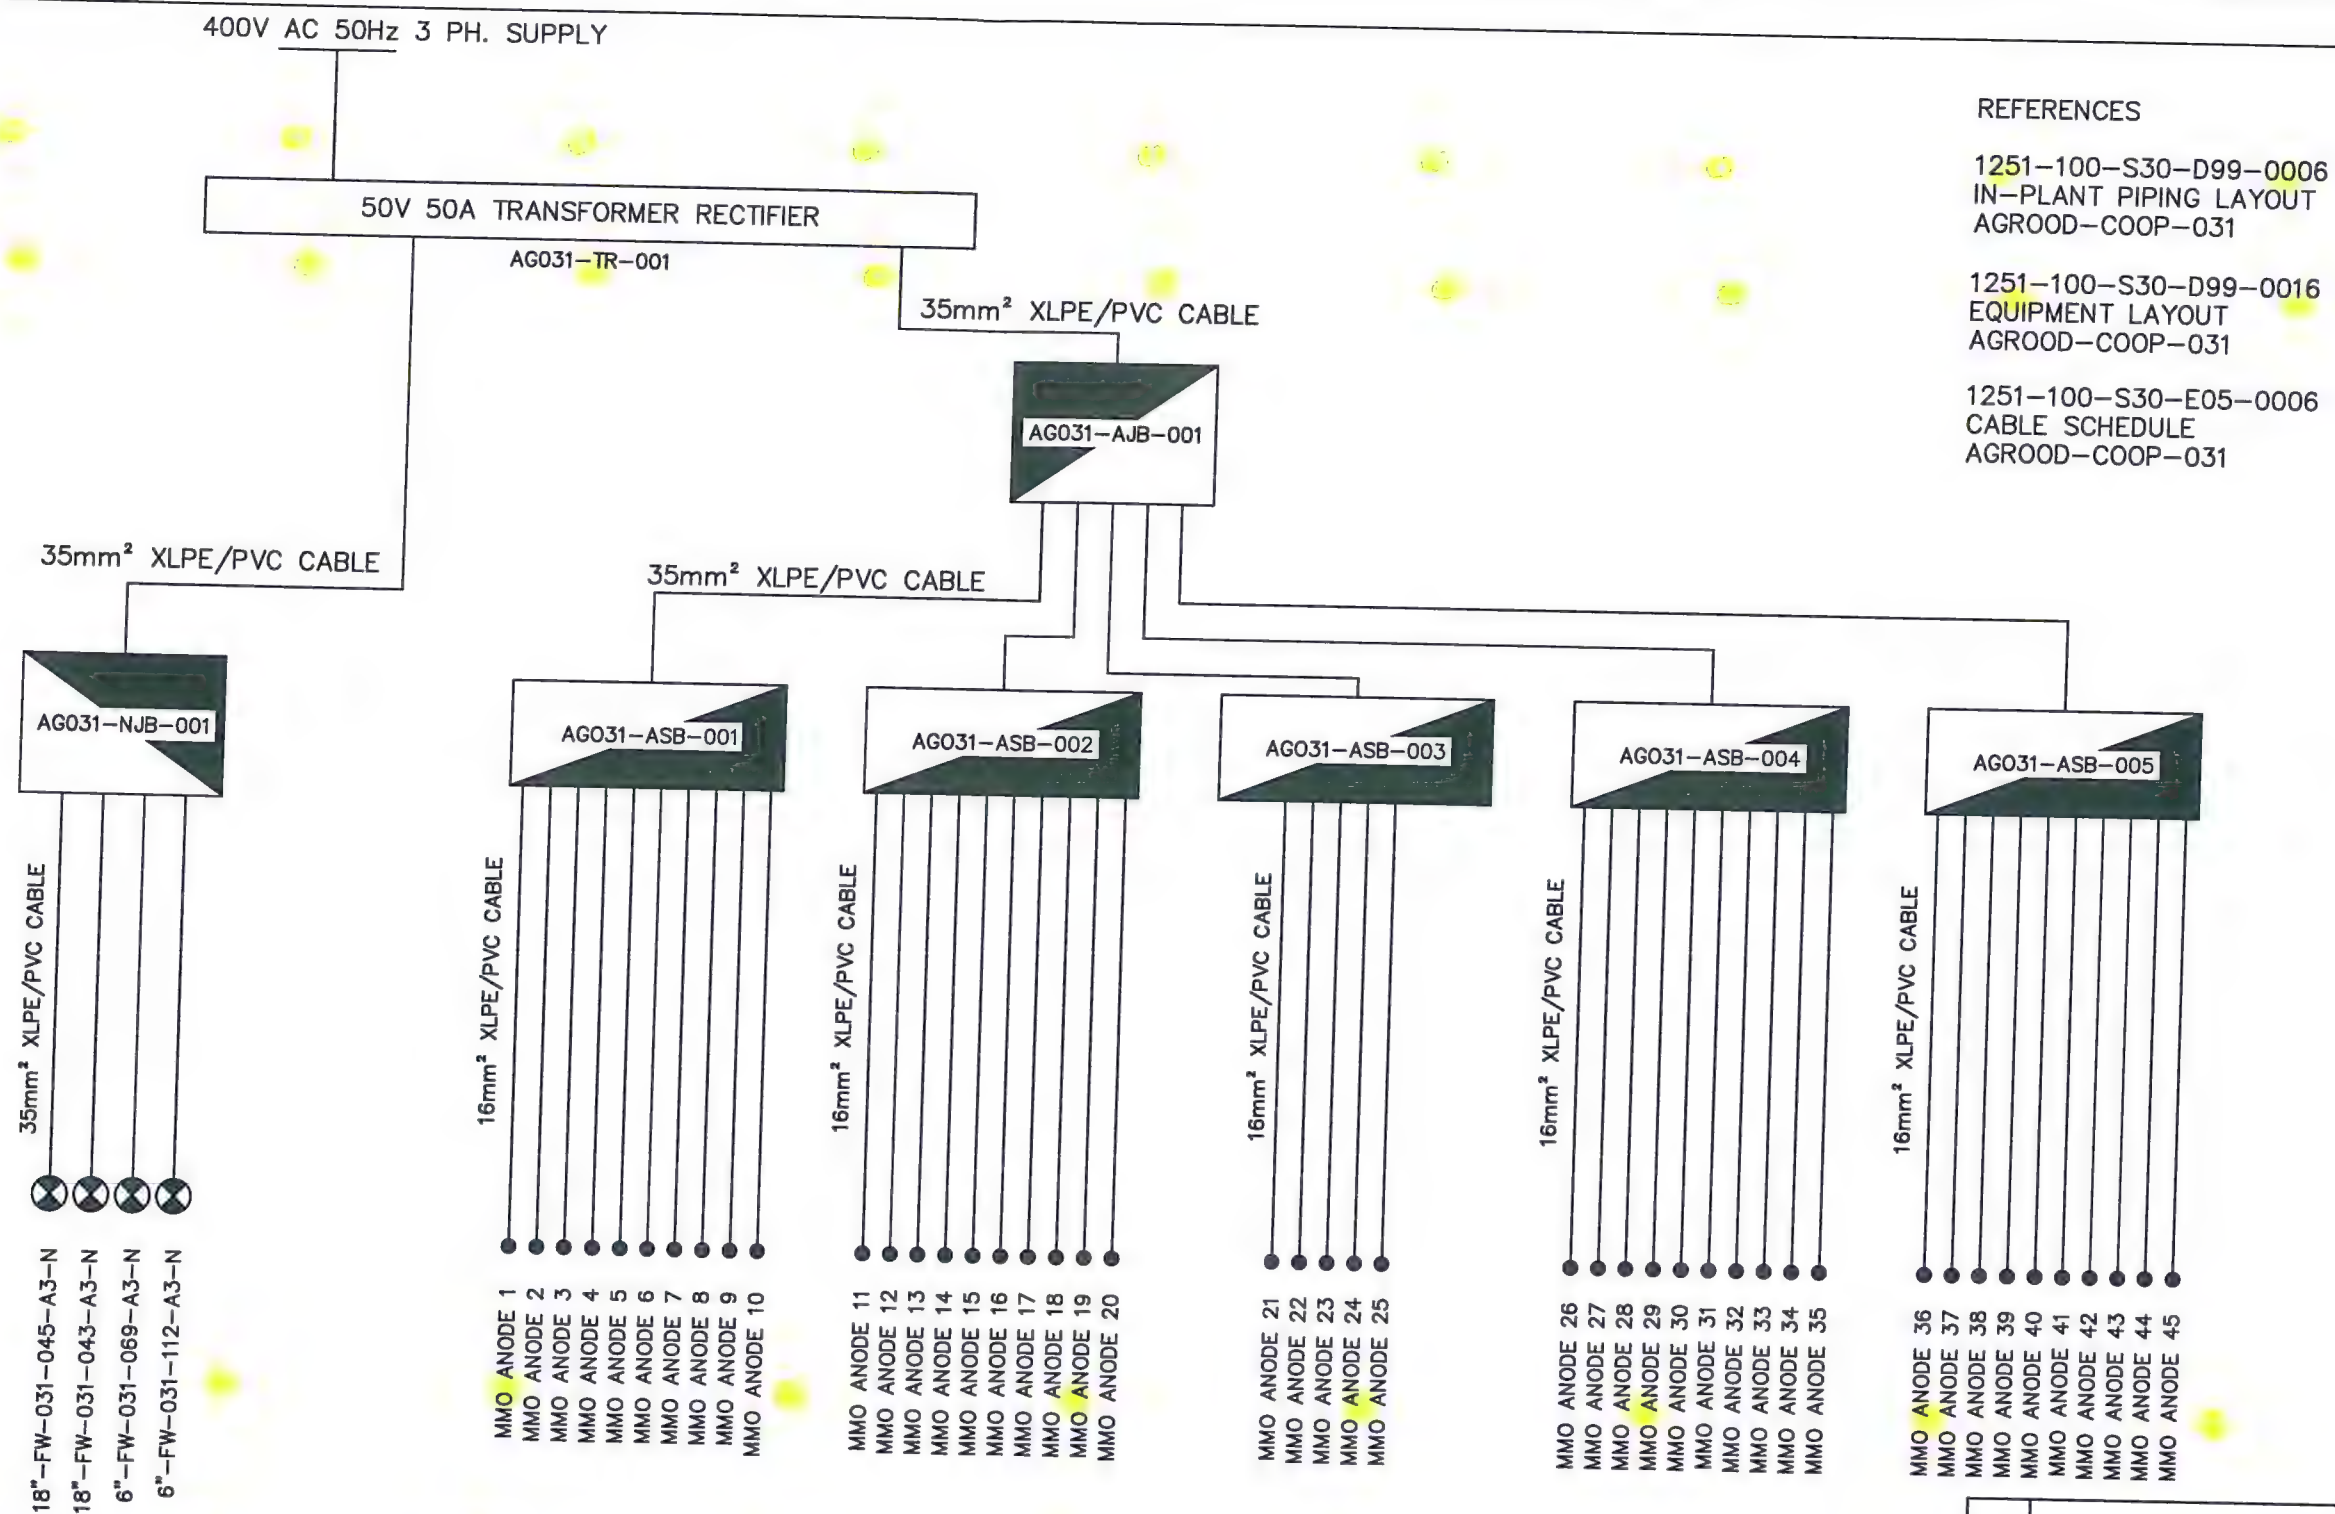


Corpro[®]
An Aegion[™] Company

Adam Street, Bowesfield Lane,
Stockton-on-Tees, Cleveland TS18 3HQ.
Tel: (01642) 614106. Fax: 614100 Telex: 587388

Information shown on this drawing is confidential and must not be copied or conveyed to third parties without the express permission of Corpro Companies Europe Ltd.
Certain items shown on this drawing are subject to worldwide patent applications.

ENPPI	NEW CRUDE OIL TANK FARM PROJECT				
SINGLE LINE DIAGRAM AGROOD-GPC-030					
Drawn	PB	Date	23/10/2020	Checked	DC
Scale	NTS	DRG. No.	34501020-DWC-030	Issue No.	1



REFERENCES

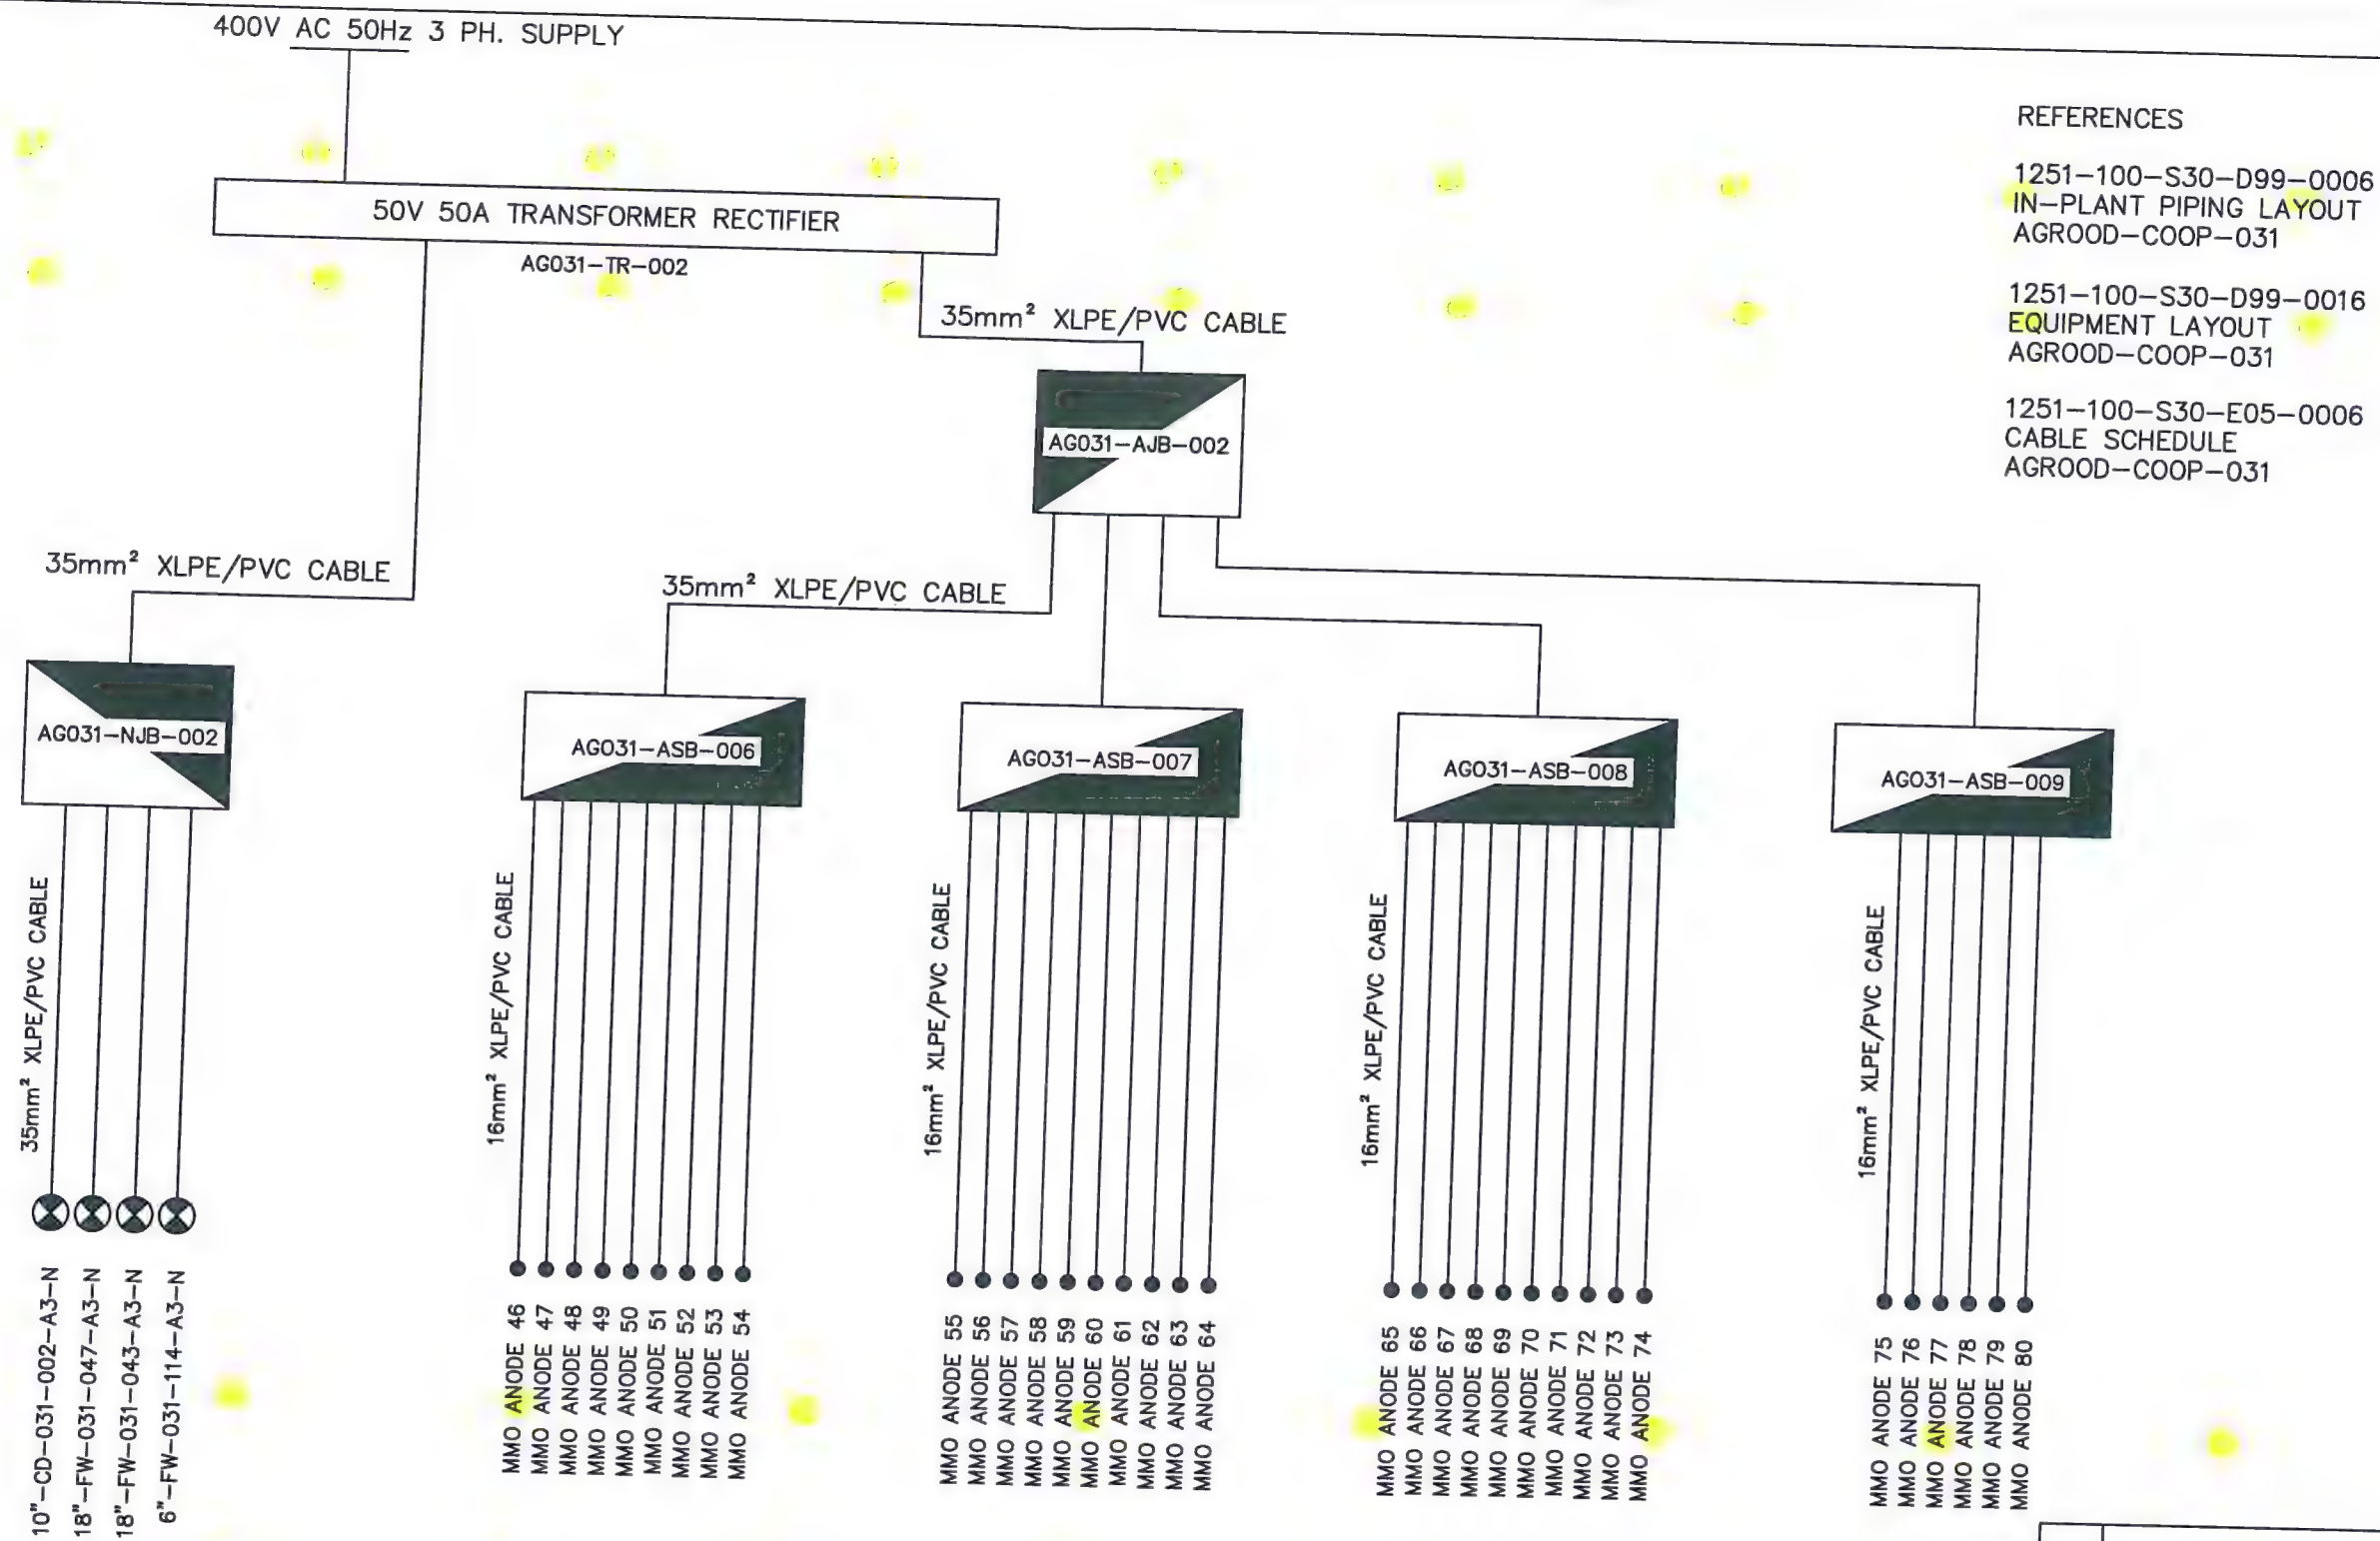
1251-100-S30-D99-0006
IN-PLANT PIPING LAYOUT
AGROOD-COOP-031

1251-100-S30-D99-0016
EQUIPMENT LAYOUT
AGROOD-COOP-031

1251-100-S30-E05-0006
CABLE SCHEDULE
AGROOD-COOP-031

SUPPLIER DOUMENT REVIEW		PROJECT TITLE		NEW CRUDE OIL TANK FARM PROJECT	
<input checked="" type="checkbox"/> 1. Work may proceed. <input type="checkbox"/> 2. Revise and resubmit in accordance with comments,work may proceed subject to incorporation of changes indicated <input type="checkbox"/> 3. Revise and resubmit.(major comments)work may not proceed <input type="checkbox"/> 4. Rejected.(reason to be specified on the document). <input type="checkbox"/> 5. Hold for a specific reason(to be specified on the document).		PACKAGE DESCRIPTION		CATHODIC PROTECTION	
PERMISSION TO PROCEED DOES NOT CONSTITUTE ACCEPTANCE OR APPROVAL OF DESIGN DETAILS, CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS DEVELOPED OR SELECTED BY SUPPLIER FROM FULL COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.		EQUIPMANT TAG			
NAME Mohamed Mohsen Abdelbaeth		CODE IDENTIFIER		E10	SHEET 1 OF 4
SIGNATURE <i>MH</i>		DOCUMENT NUMBER		1251-100-S30-E10-0006	
DATE:		REVISION		1	

1 ISSUED FOR APPROVAL		N/A	PB	DC	14/01/21
0 ISSUED FOR REVIEW		N/A	PB	DC	24/08/20
No.	DESCRIPTION	DCR No.	BY	CHECK	DATE
corrpro An Aegion™ Company Adam Street,Bowesfield Lane, Stockton-on-Tees,Cleveland TS18 3HQ. Tel: (01642) 614106. Fax: 614100 Telex: 587388					
Information shown on this drawing is confidential and must not be copied or conveyed to third parties without the express permission of Corpro Companies Europe Ltd. Certain items shown on this drawing are subject to worldwide patent applications.					
ENPPI		NEW CRUDE OIL TANK FARM PROJECT			
SINGLE LINE DIAGRAM AGROOD-COOP-031					
Drawn	PB	Date	24/08/2020	Checked	DC
Scale	NTS	DRG. No.	34501020-DWG-031	Date	24/08/2020
					Issue No. 1



REFERENCES

1251-100-S30-D99-0006
IN-PLANT PIPING LAYOUT
AGROOD-COOP-031

1251-100-S30-D99-0016
EQUIPMENT LAYOUT
AGROOD-COOP-031

1251-100-S30-E05-0006
CABLE SCHEDULE
AGROOD-COOP-031

SUPPLIER DOUMENT REVIEW		PROJECT TITLE		NEW CRUDE OIL TANK FARM PROJECT	
<input type="checkbox"/> 1. Work may proceed.		PACKAGE DESCRIPTION		CATHODIC PROTECTION	
<input type="checkbox"/> 2. Revise and resubmit in accordance with comments,work may proceed subject to incorporation of changes indicated		EQUIPMANT TAG			
<input type="checkbox"/> 3. Revise and resubmit.(major comments)work may not proceed		CODE IDENTIFIER		E10 SHEET 2 OF 4	
<input type="checkbox"/> 4. Rejected.(reason to be specified on the document).		DOCUMENT NUMBER		1251-100-S30-E10-0006	
<input type="checkbox"/> 5. Hold for a specific reason(to be specified on the document).		REVISION		1	
PERMISSION TO PROCEED DOES NOT CONSTITUTE ACCEPTANCE OR APPROVAL OF DESIGN DETAILS, CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS DEVELOPED OR SELECTED BY SUPPLIER FROM FULL COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.					
NAME					
SIGNATURE		DATE:			

1	ISSUED FOR APPROVAL	N/A	PB	DC	14/01/21
0	ISSUED FOR REVIEW	N/A	PB	DC	24/08/20
No.	DESCRIPTION	DCR No.	BY	CHECK	DATE
corrpro An Aegion™ Company					
Adam Street,Bowesfield Lane, Stockton-on-Tees,Cleveland TS18 3HQ. Tel: (01642) 614106. Fax: 614100 Telex: 587388					
Information shown on this drawing is confidential and must not be copied or conveyed to third parties without the express permission of Corpro Companies Europe Ltd. Certain items shown on this drawing are subject to worldwide patent applications.					
ENPPI		NEW CRUDE OIL TANK FARM PROJECT			
SINGLE LINE DIAGRAM AGROOD-COOP-031					
Drawn	PB	Date	24/08/2020	Checked	DC
Scale	NTS	DRG. No.	34501020-DWC-031	Issue No.	1
		Date	24/08/2020		
















REFERENCES	
DOCUMENT NUMBER	DESCRIPTION
1251-100-530-D99-0024	TEST POSTS AND REFERENCE ELECTRODE INSTALLATION DETAILS
1251-100-530-099-0024	ANODE INSTALLATION DRAWING
1251-100-530-001-0001	TRANSFORMER RECTIFIER GENERAL ARRANGEMENT
1251-100-530-001-0003	JUNCTION BOX GENERAL ARRANGEMENT
1251-100-530-K09-0001	CATHODIC PROTECTION EQUIPMENT DATA SHEETS
1251-100-530-C03-0007	DETAILED DESIGN REPORT AGROOD COP 031
1251-100-031-HGH-001	ELECTRICAL HAZARDOUS AREA CLASSIFICATION LAYOUT (AGROOD AREA - MODULE-2)
1251-100-530-P99-0001	INSTALLATION, COMMISSIONING, OPERATIONS AND MAINTENANCE MANUAL

NOTES

1. THIS DRAWING HAS BEEN ISSUED FOR CATHODIC PROTECTION EQUIPMENT INSTALLATION PURPOSES ONLY BASED ON DWG(1251-100-S30-099-0006) FOR ANY OTHER INFORMATION PLEASE REFER TO EHPH1 ISSUED DRAWING DWG (1251-100-031-RUP-001 TO 004)
2. CARE MUST BE GIVEN THAT THE INSTALLATION OF THE TRs AND JBs FOLLOWS THE COORDINATES INDICATED WITHIN THE DRAWING
3. EQUIPMENT SHALL BE INSTALLED IN AN UNCLASSIFIED AREA, INFORMATION REGARDING AREA CLASSIFICATION IS GIVEN IN WITHIN DRAWING NUMBER 1251-100-031-RUP-001 TO 004
4. A MAXIMUM ALLOWABLE VARIATION FOR LOCATION OF TRs AND JUNCTION BOXES IS (10 meters)
5. IN CASE OF ANY CONFLICT PLEASE REFER TO THE CATHODIC PROTECTION ENGINEER FOR RESOLUTION
6. ALL INSTALLATION WORKS SHALL CONSIDER INSTALLATION MANUAL ISSUED BY RIL CORP.


LEGEND

	- MMO ANODES
	- TRANSFORMER RECTIFIER
	- ANODE SPLITTING JUNCTION BOX
	- NEGATIVE JUNCTION BOX
	- POSITIVE JUNCTION BOX
	- TEST STATION WITH RE & COUPON
	- 35mm ² XLPE/PVC POSITIVE FEEDER BLACK CABLE
	- 35mm ² XLPE/PVC NEGATIVE FEEDER BLACK CABLE
	- 16mm ² XLPE/PVC ANODE TAIL BLACK CABLE
	- 16mm ² XLPE/PVC MONITORING BLACK CABLE
	- 10mm ² XLPE/PVC REFERENCE ELECTRODE RED CABLE
	- 10mm ² XLPE/PVC POLARISATION COUPON BLUE CABLE



4	1 JUL 2020	RE-ISSUED FOR REVIEW	SD	DC	CL
3	25 JUN 2020	RE-ISSUED FOR REVIEW	SD	DC	CL
2	1 JUL 2020	RE-ISSUED FOR REVIEW	SD	DC	CL
1	14 JUN 2020	RE-ISSUED FOR REVIEW	SD	DC	CL
0	18 JUN 2020	ISSUED FOR REVIEW	SD	DC	CL
REV DATE		DESCRIPTION	BY	CHECKED	APPROVED

NOTICE



COMPANY PROJ. No. : NJR	FOR : EGPC	BY : G. Hamed Hamed Hamed g/hp
ENRPT PROJ. No. : 01251-100	AT : RAS BADRAN AREA	Scale : 1/25


EGPC CRUDE OIL TANK FARM
RAS BADRAN AREA (MODULE-2)
PLANT PIPING LAYOUT - AGROOD-COOP-03

الشركة الهندسية للصناعات البترولية والكيميائية
Enppi انببي
ENGINEERING FOR THE PETROLEUM AND PROCESS INDUSTRIES

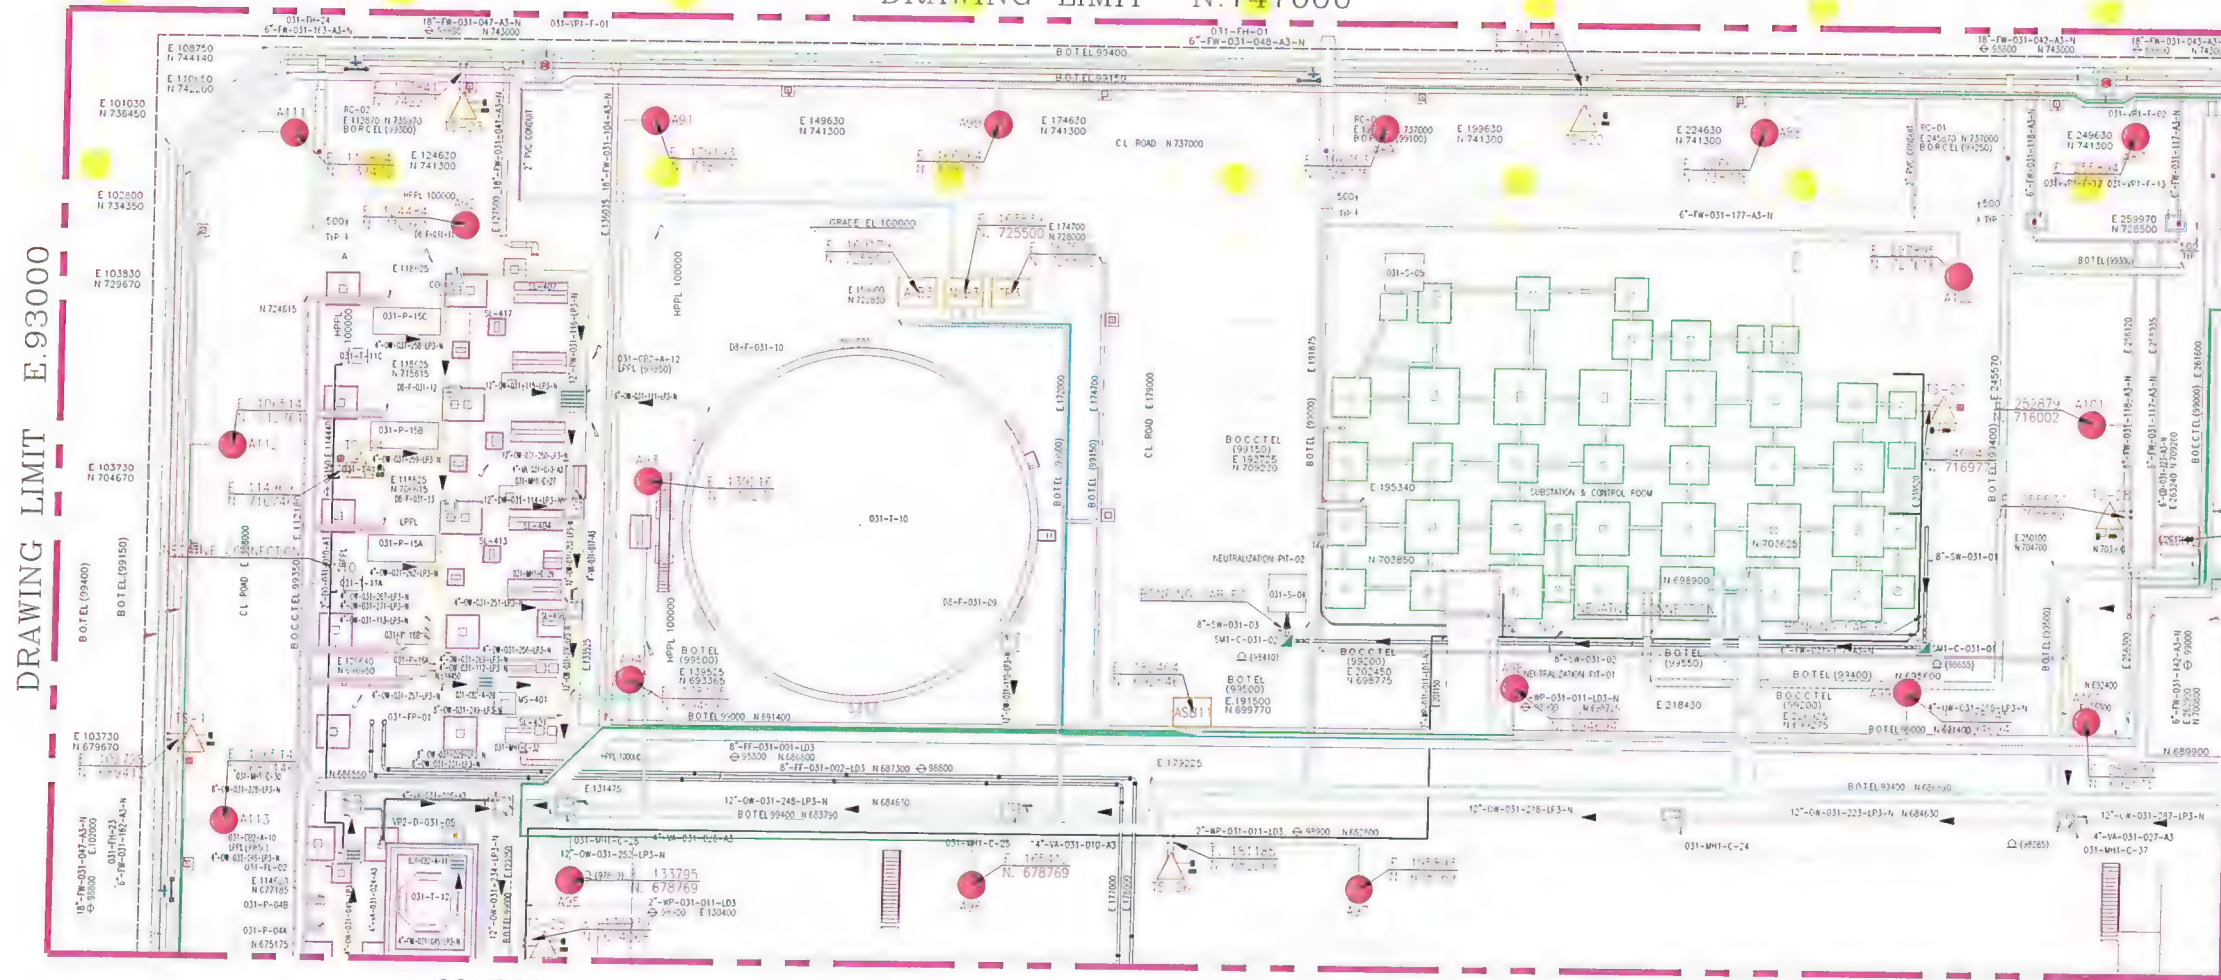
SCALE	ENPP: DRAWING NUMBER	SHEET	REVISION
1:200	1251-100-S30-D99-0006	01/04	4

SUPPLIER DOCUMENT REVIEW		PROJECT TITLE	NEW CRUDE OIL TANK FARM PROJECT
1	Work may proceed	PACKAGE DESCRIPTION	CATHODIC PROTECTION
2	Review and resubmit in accordance with comments/and/or instructions to incorporation of changes indicated		
3	Review and resubmit (any comments) work may not proceed		
4	Rejected (reason to be specified on the document)		
5	Hold for a specific reason(s) to be specified on the document)		
PERMIT TO PROCEED DOES NOT CONSTITUTE ACCEPTANCE OR APPROVAL OF DESIGN DETAILS, CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS DEVELOPED OR SELECTED BY CONTRACTOR. PLEASE FULL COMPLIANCE WITH CONTRACT OBLIGATIONS		EQUIPMENT TAG	
		CODE IDENTIFIER	D99 SHEET 1 OF 1
NAME	Mohamed Mohsen Abdelbarr	DOCUMENT NUMBER	REVISION
SIGNATURE	DATE: 18/08/2020	1251-100-530-D99-0006	4





DRAWING LIMIT N.747000



DRAWING LIMIT E.93000

MATCH LINE N.672500 FOR CONT. SEE DWG. NO. 01251-100-031-PUP-003

MATCH LINE E.264000 FOR CONT.
SEE DWG. NO. 01251-100-031-PUP-001

REFERENCES	
DOCUMENT NUMBER	DESCRIPTION
1251-100-S30-D99-0024	TEST POSTS AND REFERENCE ELECTRODE INSTALLATION DETAILS
1251-100-S30-D99-0024	ANODE INSTALLATION DRAWING
1251-100-S30-D01-0001	TRANSFORMER RECTIFIER GENERAL ARRANGEMENT
1251-100-S30-D01-0003	JUNCTION BOX GENERAL ARRANGEMENT
1251-100-S30-K09-0001	CATHODIC PROTECTION EQUIPMENT DATA SHEETS
1251-100-S30-C03-0007	DETAILED DESIGN REPORT AGROOD COOP 031
1251-100-031-K04-001	ELECTROLYTIC AREA CLASSIFICATION LAYOUT (AGROOD AREA - MODULE-2)
1251-100-S30-P99-0001	INSTALLATION, COMMISSIONING, OPERATIONS AND MAINTENANCE MANUAL

NOTES	
1.	THIS DRAWING HAS BEEN ISSUED FOR CATHODIC PROTECTION EQUIPMENT INSTALLATION PURPOSES ONLY BASED ON DWG(1251-100-S30-D99-0006) FOR ANY OTHER INFORMATION PLEASE REFER TO ENPPI ISSUED DRAWING DWG (1251-100-031-PUP-001 to 004)
2.	CARE MUST BE GIVEN THAT THE INSTALLATION OF THE TRs AND JBS FOLLOWS THE COORDINATES INDICATED WITHIN THE DRAWING
3.	EQUIPMENT SHALL BE INSTALLED IN AN UNCLASSIFIED AREA, INFORMATION REGARDING AREA CLASSIFICATION IS GIVEN IN WITHIN DRAWING NUMBER (1251-100-031-K04-001)
4.	A MAXIMUM ALLOWABLE VARIATION FOR LOCATION OF TRs AND JUNCTION BOXES IS (10 meters)
5.	IN CASE OF ANY CONFLICT PLEASE RAISE TO THE CATHODIC PROTECTION ENGINEER FOR RESOLUTION
6.	ALL INSTALLATION WORKS SHALL CONSIDER INSTALLATION MANUAL ISSUED BY CORROPRO.

LEGEND	
	- IMMO ANODES
	- TRANSFORMER RECTIFIER
	- ANODE SPLITTING JUNCTION BOX
	- NEGATIVE JUNCTION BOX
	- POSITIVE JUNCTION BOX
	- TEST STATION WITH RE & COUPON
	- 35mm² XLPE/PVC POSITIVE FEEDER BLACK CABLE
	- 35mm² XLPE/PVC NEGATIVE FEEDER BLACK CABLE
	- 16mm² XLPE/PVC ANODE TAIL BLACK CABLE
	- 16mm² XLPE/PVC MONITORING BLACK CABLE
	- 10mm² XLPE/PVC REFERENCE ELECTRODE RED CABLE
	- 10mm² XLPE/PVC POLARISATION COUPON BLUE CABLE

KEY PLAN	

4	RE-ISSUED FOR REVIEW	SD	DC	CL
3	RE-ISSUED FOR REVIEW	SD	DC	CL
2	RE-ISSUED FOR REVIEW	SD	DC	CL
1	RE-ISSUED FOR REVIEW	SD	DC	CL
0	ISSUED FOR REVIEW	SD	DC	CL
REV DATE	DESCRIPTION	BY	CHECKED	APPROVED

NOTES
THIS DRAWING HAS BEEN REVISED IN THE LIGHT OF THE COMMENTS OF THE CLIENT AND THE DESIGNER. THE REVISED DRAWING SHALL BE USED FOR THE CONSTRUCTION OF THE PROJECT. THE REVISED DRAWING SHALL BE USED FOR THE CONSTRUCTION OF THE PROJECT. THE REVISED DRAWING SHALL BE USED FOR THE CONSTRUCTION OF THE PROJECT.

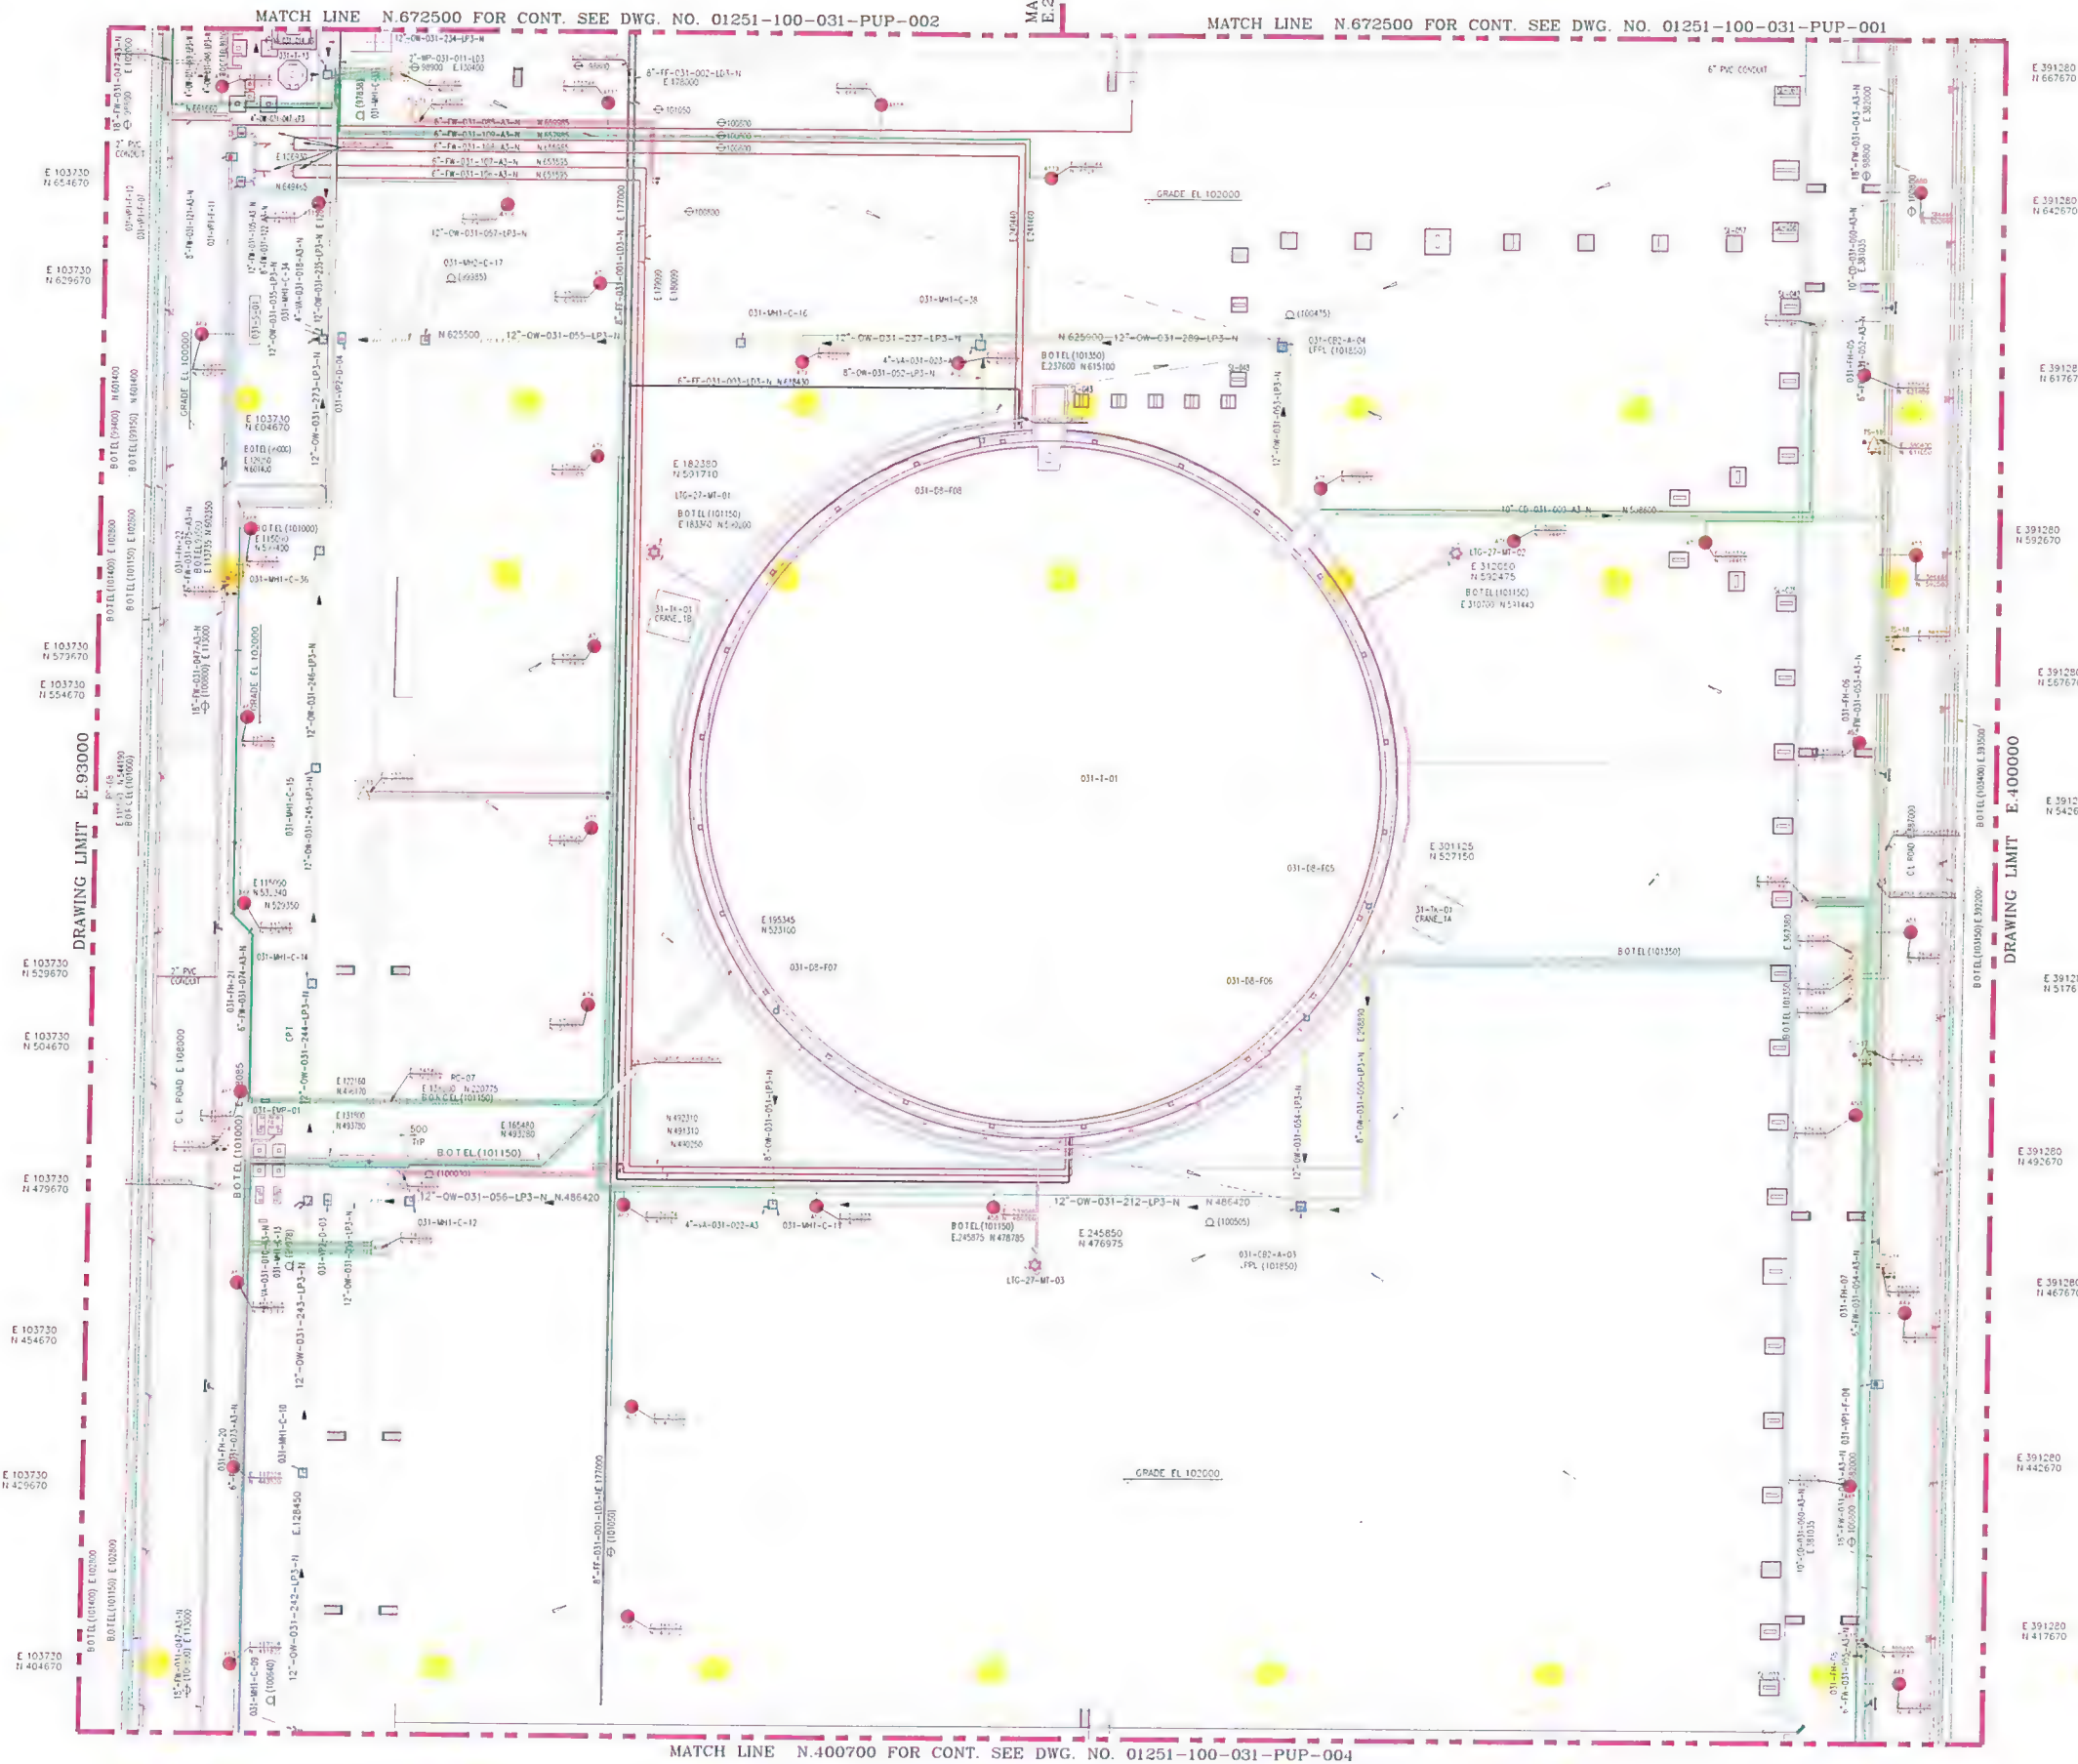

EGPC

COMPANY PROJECT NO: 01251-100 FOR: EPC PROJECT NO: 01251-100 AT: RAS BADRAN AREA SHEET NO: 02/04

EGPC CRUDE OIL TANK FARM
RAS BADRAN AREA (MODULE-2)
PLANT PIPING LAYOUT - AGROOD-COOP-031

Enppi
ENGINEERING FOR THE PETROLEUM AND PROCESS INDUSTRIES

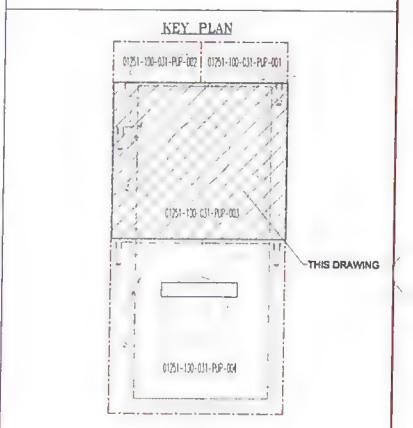
SCALE: 1:200 ENPPI DRAWING NUMBER: 1251-100-S30-D99-0006 SHEET: 02/04 REVISION: 4



REFERENCES	
DOCUMENT NUMBER	DESCRIPTION
1251-100-530-D99-0024	TEST POSTS AND REFERENCE ELECTRODE INSTALLATION DATA
1251-100-530-D99-0024	ANODE INSTALLATION DRAWING
1251-100-530-D01-0001	TRANSFORMER RECTIFIER GENERAL ARRANGEMENT
1251-100-530-D01-0003	JUNCTION BOX GENERAL ARRANGEMENT
1251-100-530-K09-0001	CATHODIC PROTECTION EQUIPMENT DATA SHEETS
1251-100-530-C03-0007	DETAILED DESIGN REPORT AGROOD COOP 031
1251-100-031-HGH-001	ELECTRICAL HAZARDOUS AREA CLASSIFICATION LAYOUT (AGROOD AREA - MODULE-2)
1251-100-530-P99-0001	INSTALLATION, COMMISSIONING, OPERATIONS AND MAINTENANCE MANUAL

- NOTES
- THIS DRAWING HAS BEEN ISSUED FOR CATHODIC PROTECTION EQUIPMENT INSTALLATION PURPOSES ONLY BASED ON DWG(1251-100-530-D99-0006) FOR ANY OTHER INFORMATION PLEASE REFER TO ENPPI ISSUED DRAWING DWG (1251-100-031-PUP-001 to 004)
 - CARE MUST BE GIVEN THAT THE INSTALLATION OF THE TRS AND JBS FOLLOWS THE COORDINATES INDICATED WITHIN THE DRAWING
 - EQUIPMENT SHALL BE INSTALLED IN AN UNCLASSIFIED AREA, INFORMATION REGARDING AREA CLASSIFICATION IS GIVEN IN WITHIN DRAWING NUMBER (1251-100-031-HGH-001)
 - A MAXIMUM ALLOWABLE VARIATION FOR LOCATION OF TRS AND JUNCTION BOXES IS (10 meters)
 - IN CASE OF ANY CONFLICT PLEASE RAISE TO THE CATHODIC PROTECTION ENGINEER FOR RESOLUTION
 - ALL INSTALLATION WORKS SHALL CONSIDER INSTALLATION MANUAL ISSUED BY CORROPRO.

- LEGEND
- MMO ANODES
 - TRANSFORMER RECTIFIER
 - ANODE SPLITTING JUNCTION BOX
 - NEGATIVE JUNCTION BOX
 - POSITIVE JUNCTION BOX
 - TEST STATION WITH RE & COUPON
 - 35mm² XLPE/PVC POSITIVE FEEDER BLACK CABLE
 - 35mm² XLPE/PVC NEGATIVE FEEDER BLACK CABLE
 - 16mm² XLPE/PVC ANODE TAIL BLACK CABLE
 - 16mm² XLPE/PVC MONITORING BLACK CABLE
 - 10mm² XLPE/PVC REFERENCE ELECTRODE RED CABLE
 - 10mm² XLPE/PVC POLARISATION COUPON BLUE CABLE



REV	DATE	DESCRIPTION	BY	CHECKED	APPROVED
4	17/01/2024	RE-ISSUED FOR REVIEW	S.B.	D.C.	C.L.
3	27/01/2024	RE-ISSUED FOR REVIEW	S.B.	D.C.	C.L.
2	01/02/2024	RE-ISSUED FOR REVIEW	S.B.	D.C.	C.L.
1	04/02/2024	RE-ISSUED FOR REVIEW	S.B.	D.C.	C.L.
0	28/01/2024	ISSUED FOR REVIEW	S.B.	D.C.	C.L.

NOTICE
THIS DRAWING HAS NOT BEEN PUBLISHED. IT IS THE SOLE PROPERTY OF ENPPI. IT IS LOANED TO THE CLIENT FOR HIS CONSTRUCTION USE ONLY. ANY REVISIONS TO THE DRAWING SHALL BE MADE BY ENPPI. THE CLIENT SHALL BE RESPONSIBLE FOR THE PROTECTION OF THE DRAWING. THE CLIENT SHALL NOT BE RESPONSIBLE FOR THE PROTECTION OF THE DRAWING. THE CLIENT SHALL NOT BE RESPONSIBLE FOR THE PROTECTION OF THE DRAWING.

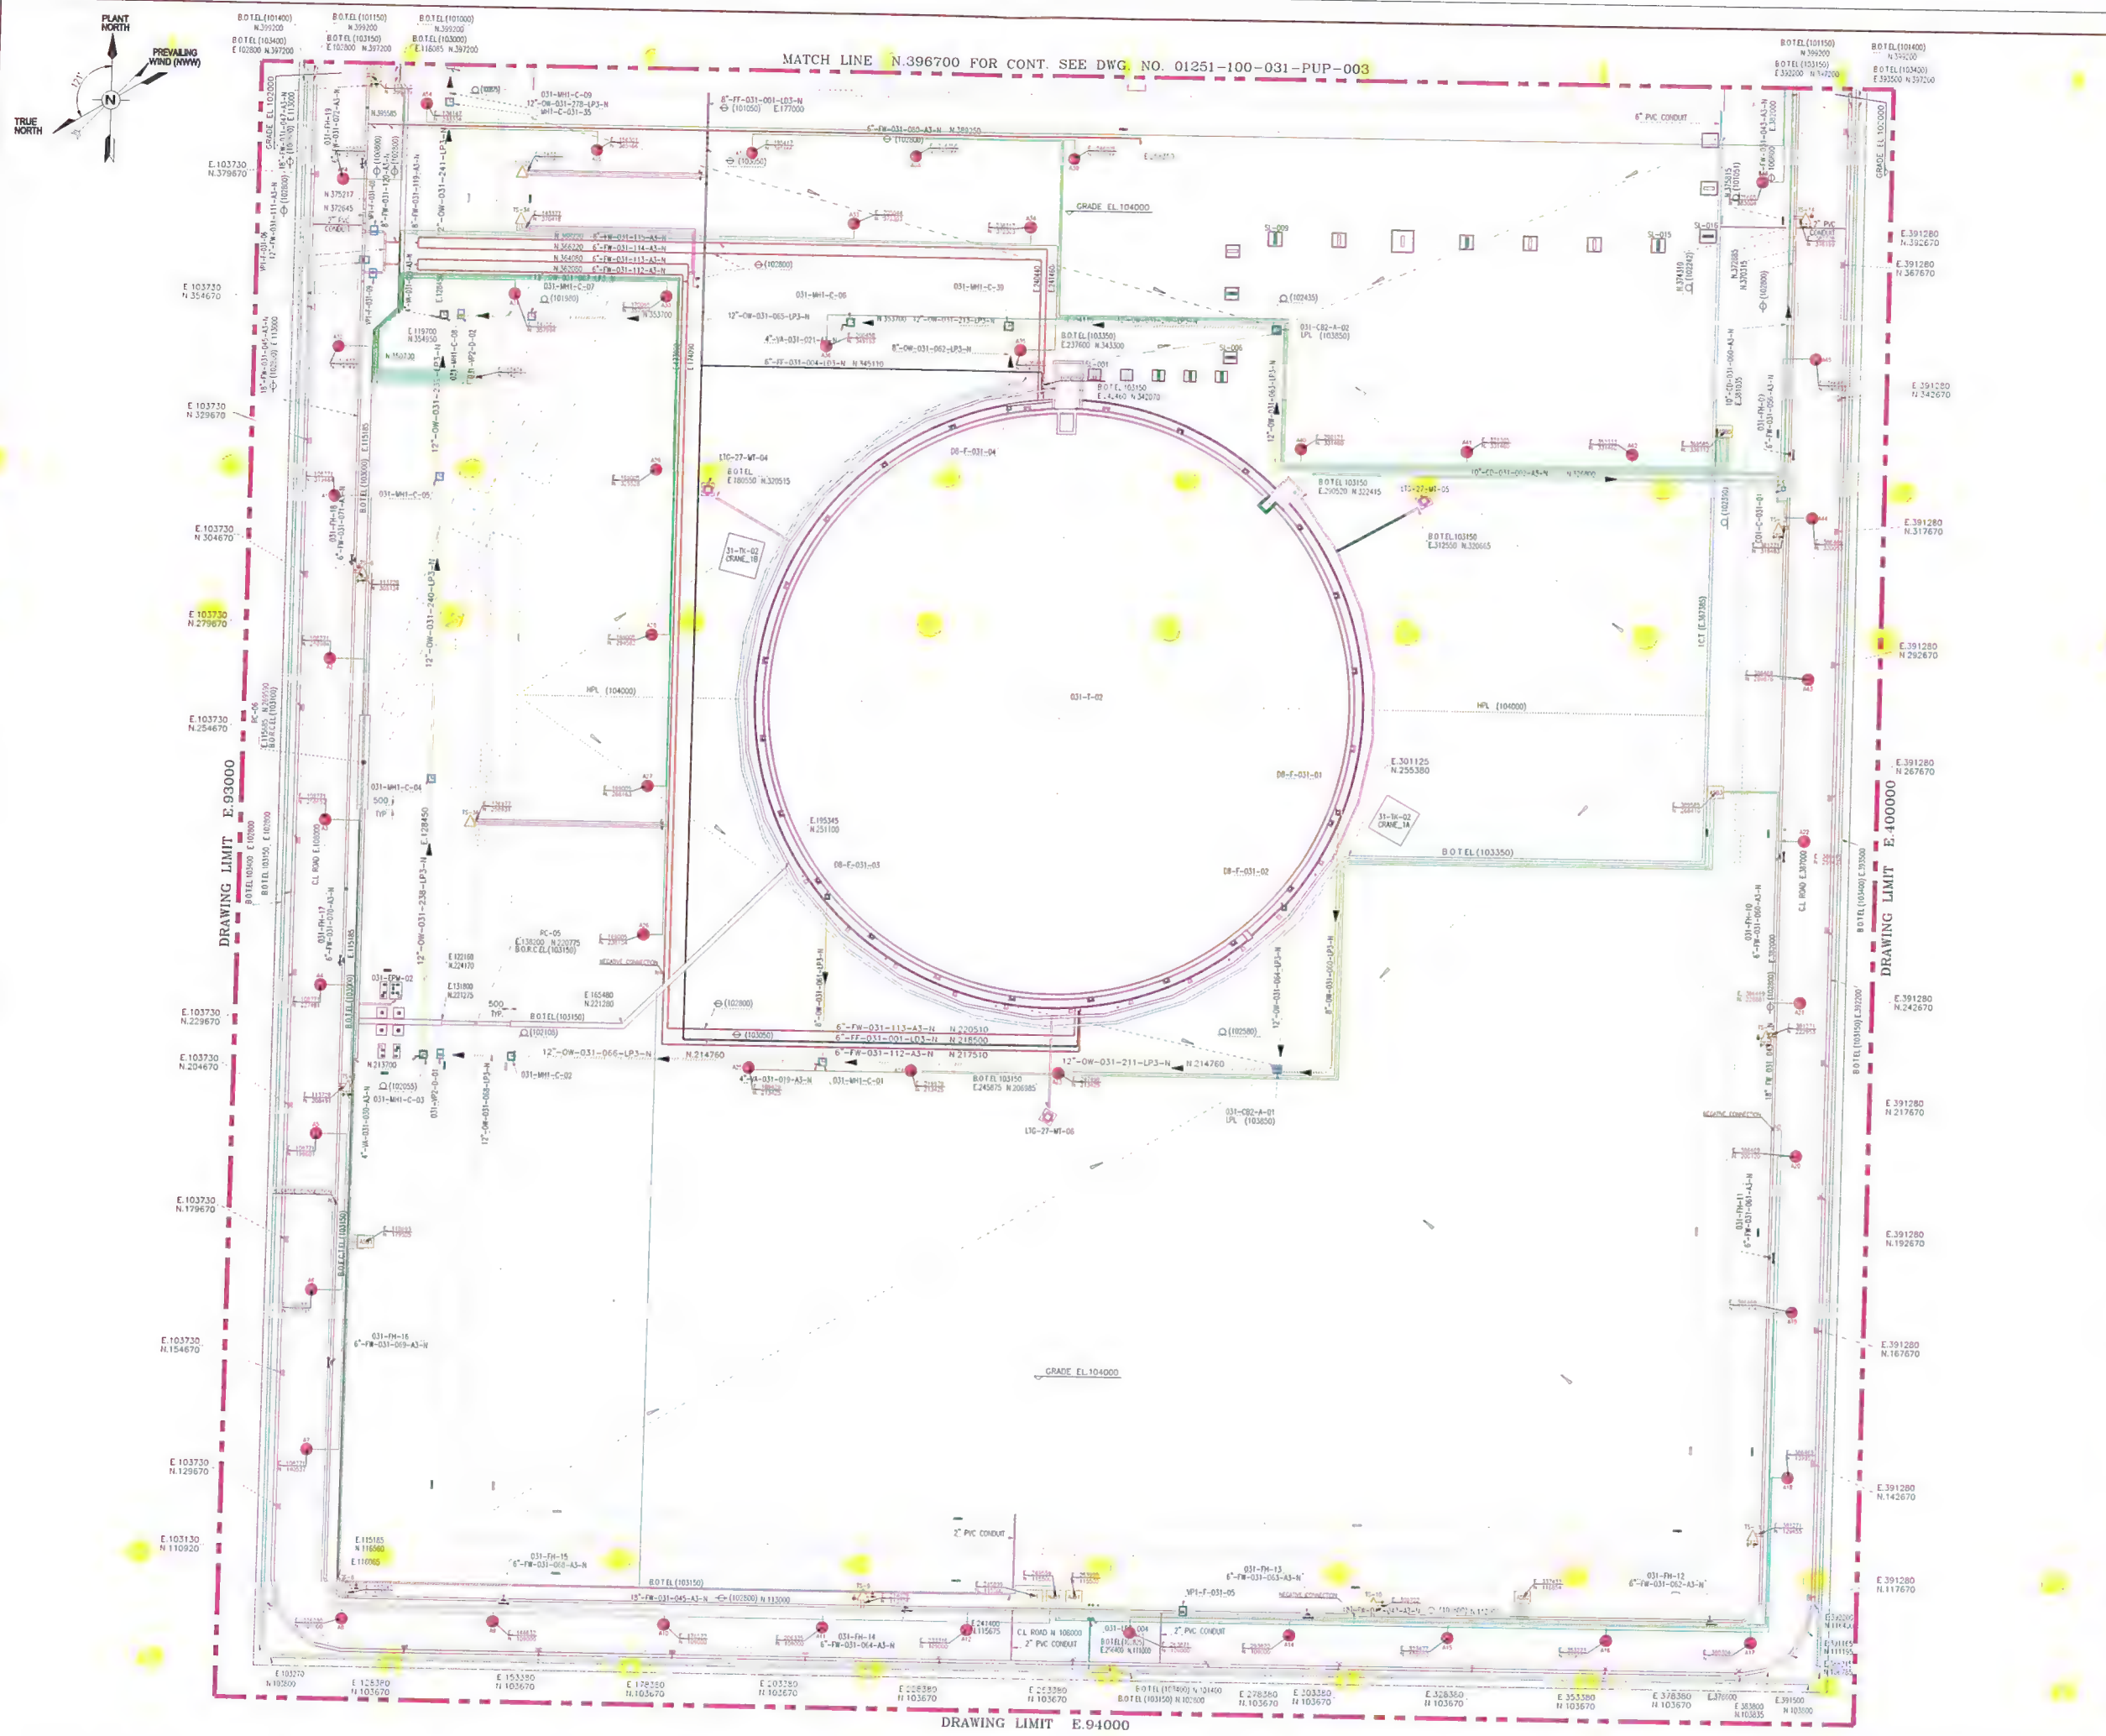
EGPC

COMPANY PROJECT NO. 01251-100-530-D99-0006 FOR EGPC BY: G. Mohamed Elmaghrabi
ENPPI PROJECT NO. 01251-100-530-D99-0006 AT AGROOD SITE PROJECT NO. 01251-100-530-D99-0006

**EGPC CRUDE OIL TANK FARM
AGROOD AREA (MODULE-2)
PLANT PIPING LAYOUT - AGROOD-COOP-031**

انبي
Enppi
ENGINEERING FOR THE PETROLEUM AND PROCESS INDUSTRIES

SCALE: 1:400 ENPPI DRAWING NUMBER: 1251-100-530-D99-0006 SHEET: 03/04 REVISION: 4



DOCUMENT NUMBER		DESCRIPTION
1251-100-030-D99-0004	TEST POINTS AND REFERENCE ELECTRODE INSTALLATION DETAILS	
1251-100-030-D99-0004	ANODE INSTALLATION DRAWING	
1251-100-030-D01-0001	TRANSFORMER RECTIFIER GENERAL ARRANGEMENT	
1251-100-030-D01-0003	JUNCTION BOX GENERAL ARRANGEMENT	
1251-100-030-D01-0001	CATHODIC PROTECTION EQUIPMENT DATA SHEETS	
1251-100-030-D03-0007	DETAILED DESIGN REPORT AGROOD COOP 031	
1251-100-031-KGH-001	ELECTROLYTIC AREA CLASSIFICATION LAYOUT (AGROOD AREA - MODULE-2)	
1251-100-030-P99-0001	INSTALLATION, COMMISSIONING, OPERATIONS AND MAINTENANCE MANUAL	

NOTES

- THIS DRAWING HAS BEEN ISSUED FOR CATHODIC PROTECTION EQUIPMENT INSTALLATION PURPOSES ONLY BASED ON EAG(1251-100-030-D99-0004) FOR ANY OTHER INFORMATION PLEASE REFER TO ENPPI ISSUED DRAWING (1251-100-031-PUP-001) IN COA.
- CARE MUST BE GIVEN THAT THE INSTALLATION OF THE TRs AND JBS FOLLOW THE COORDINATES INDICATED WITHIN THE DRAWING.
- EQUIPMENT SHALL BE INSTALLED IN AN UNCLASSIFIED AREA, INFORMATION REGARDING AREA CLASSIFICATION IS GIVEN IN WITHIN DRAWING NUMBER (1251-100-031-KGH-001).
- A MAXIMUM ALLOWABLE VARIATION FOR LOCATION OF TRs AND JUNCTION BOXES IS (10 METERS).
- IN CASE OF ANY CONFLICT PLEASE PASE TO THE CATHODIC PROTECTION ENGINEER FOR RESOLUTION.
- ALL INSTALLATION WORKS SHALL CONSIDER INSTALLATION MANUAL ISSUED BY CORPRO.

LEGEND

- MMO ANODES
- TRANSFORMER RECTIFIER
- ANODE SPLITTING JUNCTION BOX
- NEGATIVE JUNCTION BOX
- POSITIVE JUNCTION BOX
- TEST STATION WITH RE & COUPON
- 35mm² XLPE/PVC POSITIVE FEEDER BLACK CABLE
- 35mm² XLPE/PVC NEGATIVE FEEDER BLACK CABLE
- 16mm² XLPE/PVC ANODE TAIL BLACK CABLE
- 16mm² XLPE/PVC MONITORING BLACK CABLE
- 10mm² XLPE/PVC REFERENCE ELECTRODE RED CABLE
- 10mm² XLPE/PVC POLARISATION COUPON BLUE CABLE

KEY PLAN

REV	DATE	DESCRIPTION	BY	CHECKED	APPROVED
1	12/01/2020	RE-ISSUED FOR REVIEW	SD	DC	CL
2	12/01/2020	RE-ISSUED FOR REVIEW	SD	DC	CL
3	12/01/2020	RE-ISSUED FOR REVIEW	SD	DC	CL
4	12/01/2020	RE-ISSUED FOR REVIEW	SD	DC	CL
5	12/01/2020	RE-ISSUED FOR REVIEW	SD	DC	CL
6	12/01/2020	ISSUED FOR REVIEW	SD	DC	CL

NOTICE

THIS DRAWING HAS NOT BEEN PUBLISHED. IT IS THE SOLE PROPERTY OF ENPPI. IT IS TO BE USED FOR THE PROJECT ONLY AND NOT TO BE REPRODUCED OR TRANSMITTED IN ANY FORM OR BY ANY MEANS, ELECTRONIC OR MECHANICAL, WITHOUT PERMISSION IN WRITING FROM ENPPI. ANY UNAUTHORIZED REPRODUCTION OR TRANSMISSION OF THIS DRAWING IS STRICTLY PROHIBITED AND WILL BE PROSECUTED TO THE FULL EXTENT OF THE LAW.

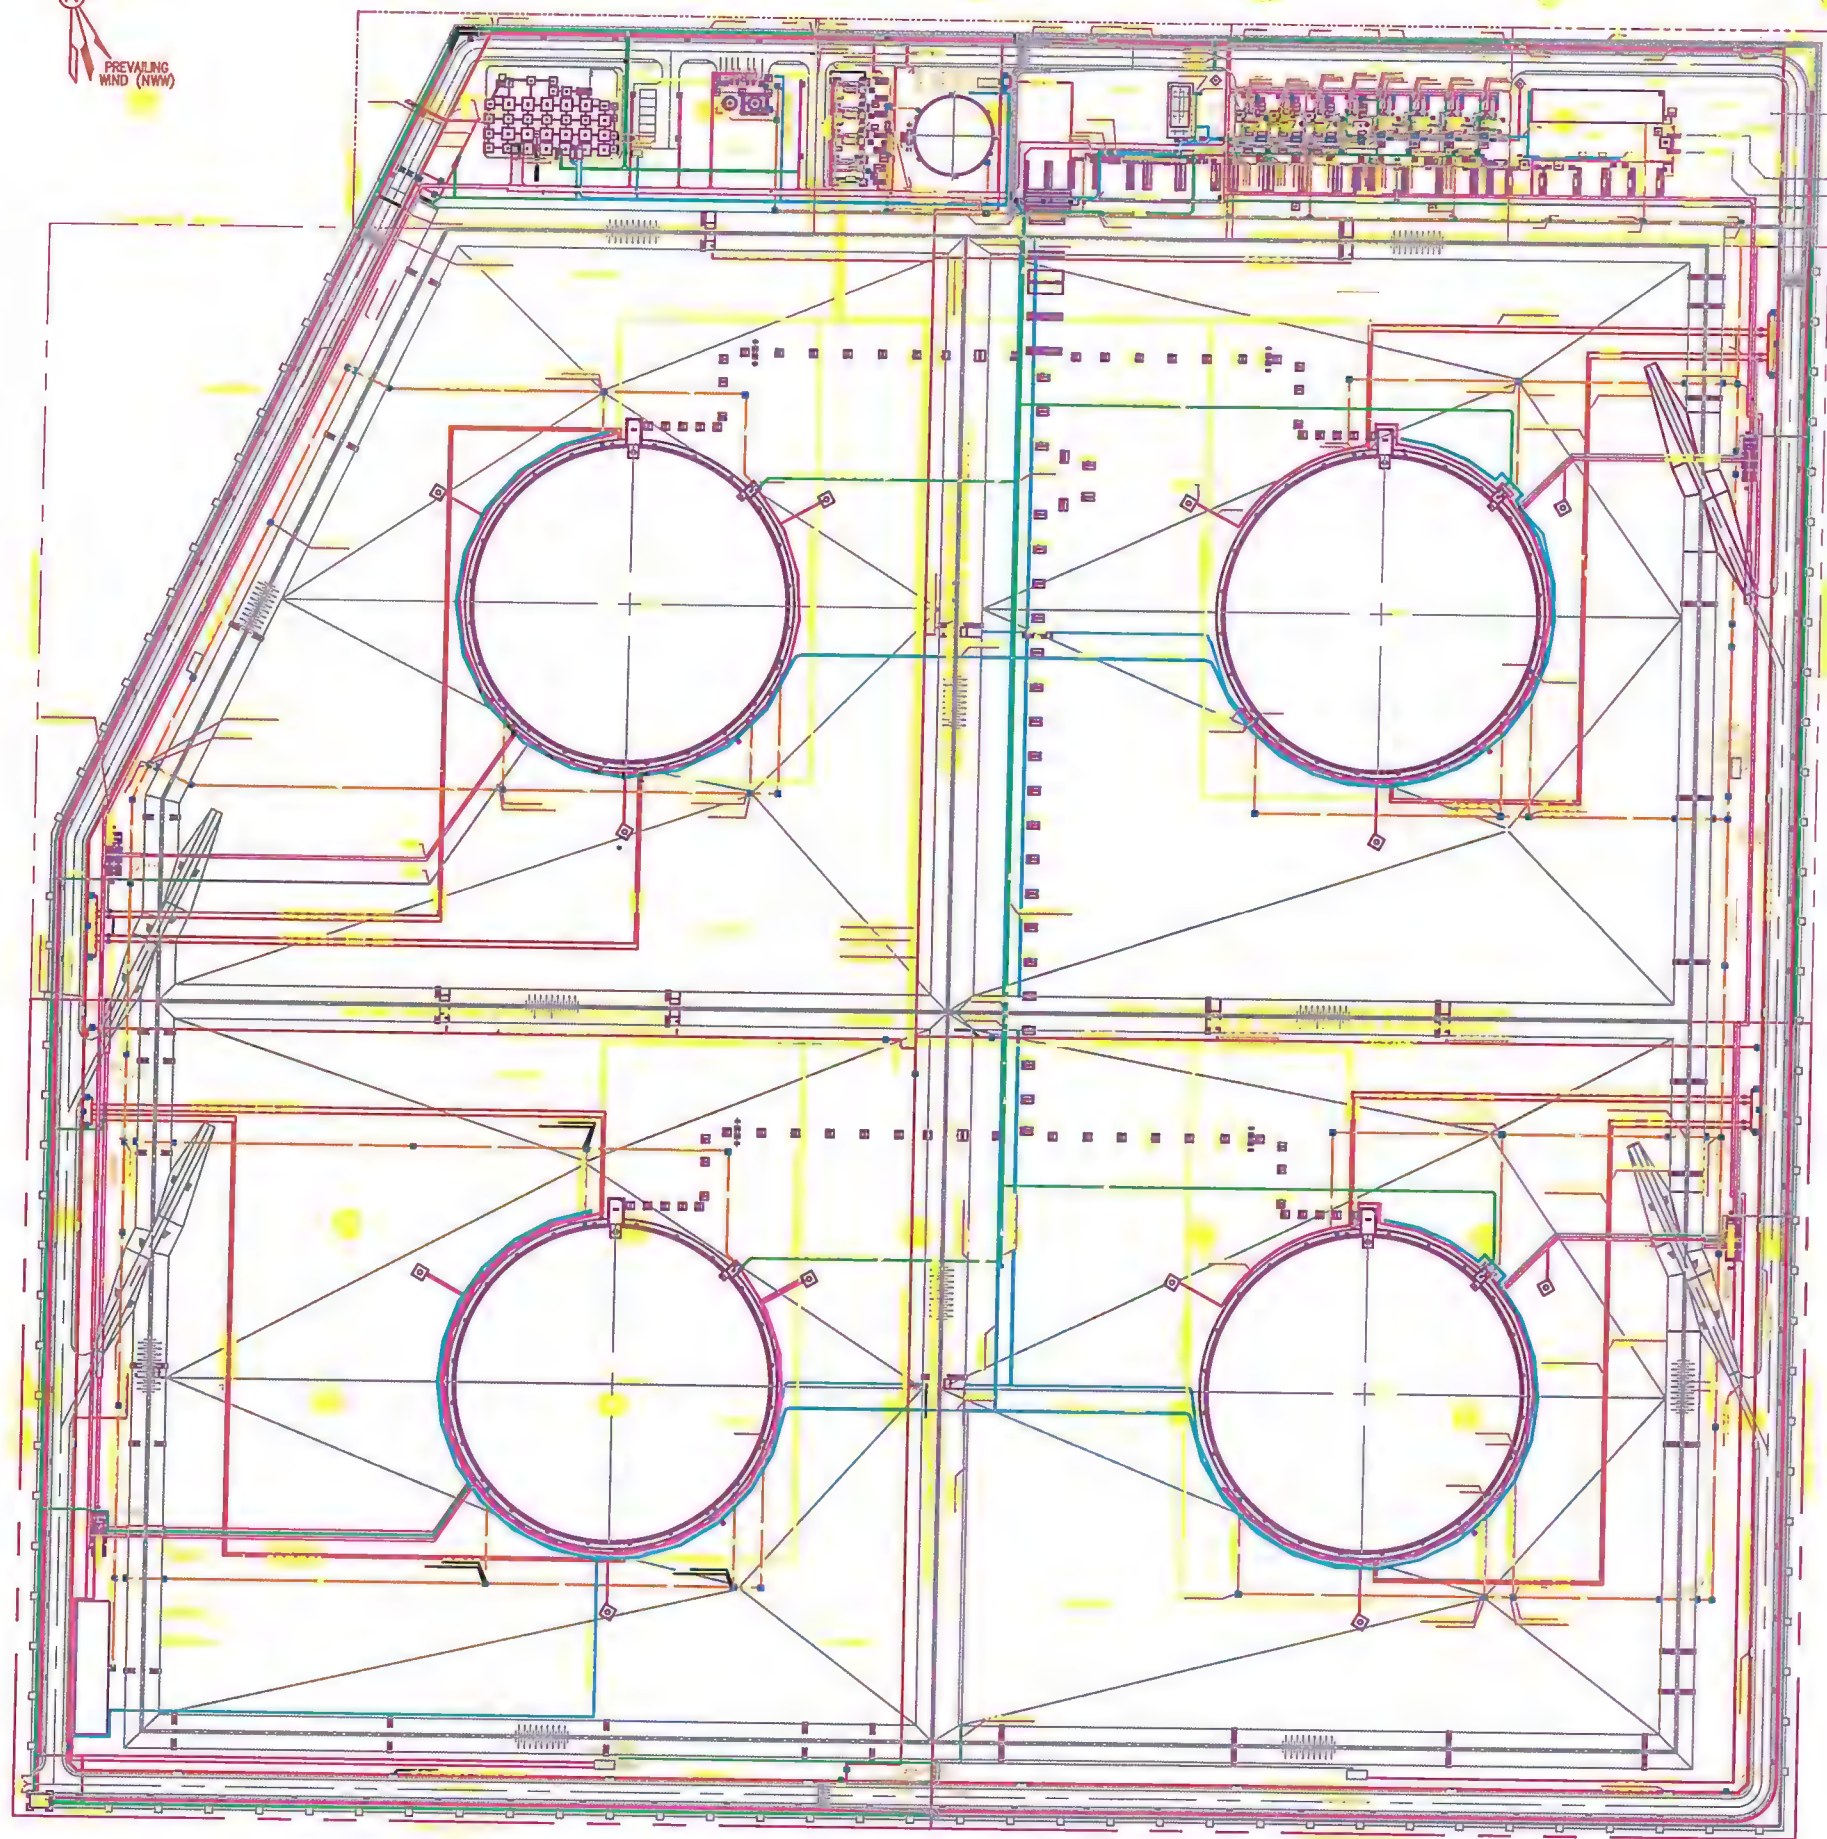

EGPC CRUDE OIL TANK FARM
AGROOD AREA (MODULE-2)
PLANT PIPING LAYOUT - AGROOD-COOP-031

SCALE: 1:400

ENPPI DRAWING NUMBER: 1251-100-S30-D99-0006

SHEET: 04/04

REVISION: 4



EQUIPMENT FACILITY		
EQUIPMENT FACILITY	EASTING	NORTHING
TRANSFORMER RECTIFIER TR1	413429	706548
ANODE JUNCTION BOX AJB1	420749	706548
NEGATIVE JUNCTION BOX NJB1	418089	706548
ANODE SPLITTER BOX ASB1	300823	707584
ANODE SPLITTER BOX ASB2	420749	709387
ANODE SPLITTER BOX ASB3	584322	718438
ANODE SPLITTER BOX ASB4	501091	687150

EQUIPMENT FACILITY		
EQUIPMENT FACILITY	EASTING	NORTHING
TRANSFORMER RECTIFIER TR2	689326	469563
ANODE JUNCTION BOX AJB2	689326	476962
NEGATIVE JUNCTION BOX NJB2	689326	473236
ANODE SPLITTER BOX ASB5	681194	609072
ANODE SPLITTER BOX ASB6	689904	449728
ANODE SPLITTER BOX ASB7	689904	444693
ANODE SPLITTER BOX ASB8	689326	480622

EQUIPMENT FACILITY		
EQUIPMENT FACILITY	EASTING	NORTHING
TRANSFORMER RECTIFIER TR3	687129	285082
ANODE JUNCTION BOX AJB3	687129	292904
NEGATIVE JUNCTION BOX NJB3	687129	289257
ANODE SPLITTER BOX ASB9	694605	118096
ANODE SPLITTER BOX ASB10	680182	186306
ANODE SPLITTER BOX ASB11	686072	337432
ANODE SPLITTER BOX ASB12	419008	116603

EQUIPMENT FACILITY		
EQUIPMENT FACILITY	EASTING	NORTHING
TRANSFORMER RECTIFIER TR4	299100	117500
ANODE JUNCTION BOX AJB4	306420	117500
NEGATIVE JUNCTION BOX NJB4	302760	117500
ANODE SPLITTER BOX ASB13	404297	116603
ANODE SPLITTER BOX ASB14	407740	116603
ANODE SPLITTER BOX ASB15	310130	117500
ANODE SPLITTER BOX ASB16	411273	116603

EQUIPMENT FACILITY		
EQUIPMENT FACILITY	EASTING	NORTHING
TRANSFORMER RECTIFIER TR5	124122	317489
ANODE JUNCTION BOX AJB5	124122	324842
NEGATIVE JUNCTION BOX NJB5	124122	321206
ANODE SPLITTER BOX ASB17	124113	356279
ANODE SPLITTER BOX ASB18	125860	202250
ANODE SPLITTER BOX ASB19	115749	378836
ANODE SPLITTER BOX ASB20	129874	427046

EQUIPMENT FACILITY		
EQUIPMENT FACILITY	EASTING	NORTHING
TRANSFORMER RECTIFIER TR6	413429	703464
ANODE JUNCTION BOX AJB6	420749	703464
NEGATIVE JUNCTION BOX NJB6	417089	703464
ANODE SPLITTER BOX ASB21	406941	659809
ANODE SPLITTER BOX ASB22	397906	659809
ANODE SPLITTER BOX ASB23	424972	656309
ANODE SPLITTER BOX ASB24	195980	598071

REFERENCES

DOCUMENT NUMBER	DESCRIPTION
01251-100-030-KPP-002	PLOT PLAN
01251-100-030-PUP-001	AGROOD AREA MODULE 1 - UNDERGROUND PIPING COMPOSITE PLAN
01251-100-030-PUP-002	AGROOD AREA MODULE 1 - UNDERGROUND PIPING COMPOSITE PLAN
01251-100-030-PUP-003	AGROOD AREA MODULE 1 - UNDERGROUND PIPING COMPOSITE PLAN
01251-100-030-PUP-004	AGROOD AREA MODULE 1 - UNDERGROUND PIPING COMPOSITE PLAN
01251-100-030-PUP-005	AGROOD AREA MODULE 1 - UNDERGROUND PIPING COMPOSITE PLAN
01251-100-030-PUP-006	AGROOD AREA MODULE 1 - UNDERGROUND PIPING COMPOSITE PLAN
01251-100-030-PUP-007	AGROOD AREA MODULE 1 - UNDERGROUND PIPING COMPOSITE PLAN
01251-100-030-PUP-008	AGROOD AREA MODULE 1 - UNDERGROUND PIPING COMPOSITE PLAN

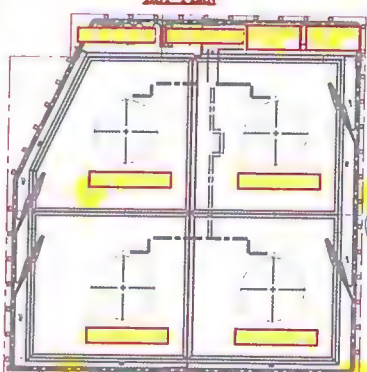
NOTES

LEGEND

LEGEND :

- TRANSFORMER RECTIFIER
- ANODE SPLITTING JUNCTION BOX
- NEGATIVE JUNCTION BOX
- POSITIVE JUNCTION BOX

KEY PLAN



1	DESIGNED FOR APPROVAL	P.E.	S.C.	C.L.
2	DESIGNED FOR APPROVAL	P.E.	S.C.	C.L.
3	DESIGNED FOR APPROVAL	P.E.	S.C.	C.L.
4	DESIGNED FOR APPROVAL	P.E.	S.C.	C.L.
5	DESIGNED FOR APPROVAL	P.E.	S.C.	C.L.
6	DESIGNED FOR APPROVAL	P.E.	S.C.	C.L.
7	DESIGNED FOR APPROVAL	P.E.	S.C.	C.L.
8	DESIGNED FOR APPROVAL	P.E.	S.C.	C.L.
9	DESIGNED FOR APPROVAL	P.E.	S.C.	C.L.
10	DESIGNED FOR APPROVAL	P.E.	S.C.	C.L.

EGPC CRUDE OIL TANK FARM PROJECT

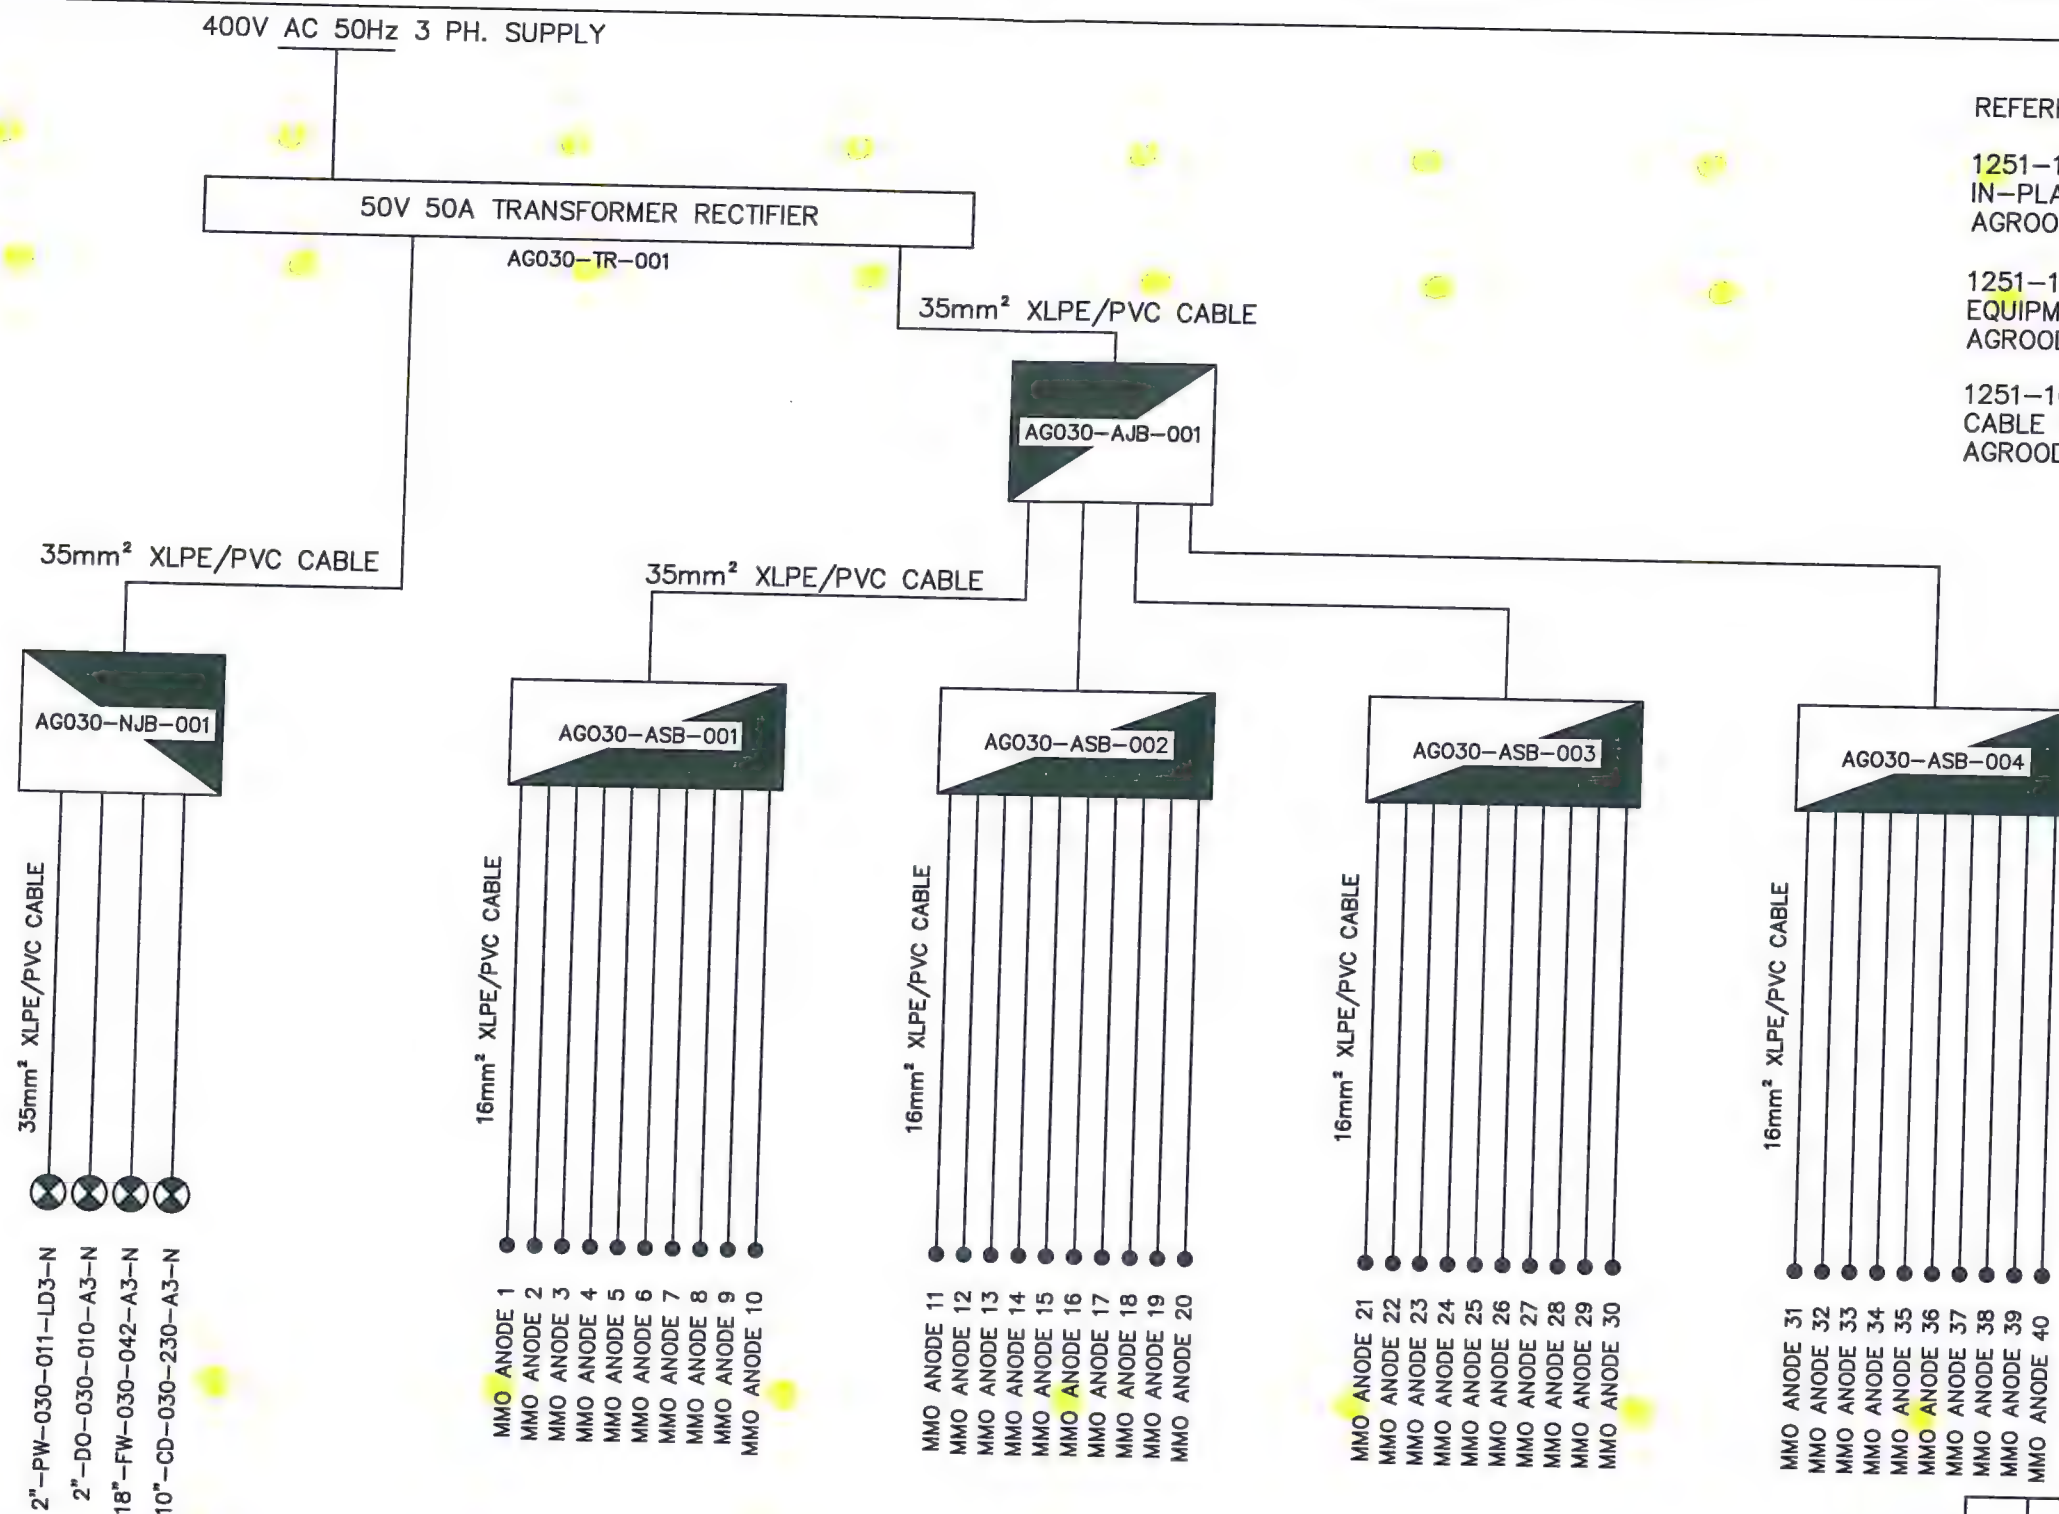
EGPC

EGPC CRUDE OIL TANK FARM
AGROOD AREA (MODULE-1) -
EQUIPMENT LAYOUT - AGROOD-GPC-030

Hnppl

SUPPLIER DOCUMENT REVIEW		PROJECT TITLE	NEW CRUDE OIL TANK FARM PROJECT	
1. Work may proceed.		PACKAGE DESCRIPTION	CATHODIC PROTECTION	
2. Review and feedback to be provided to the supplier.		EQUIPMENT TAG		
3. Review and feedback to be provided to the supplier.		CODE IDENTIFIER	D99	SHEET 1 OF 1
4. Review and feedback to be provided to the supplier.		NAME		
5. Review and feedback to be provided to the supplier.		SIGNATURE	DATE	
6. Review and feedback to be provided to the supplier.		DOCUMENT NUMBER	1251-100-S30-D99-0017	REVISION 6

1:150	1251-100-S30-D99-0017	01/01	6
-------	-----------------------	-------	---



REFERENCES

1251-100-S30-D99-0005
IN-PLANT PIPING LAYOUT
AGROOD-GPC-030

1251-100-S30-D99-0015
EQUIPMENT LAYOUT
AGROOD-GPC-030

1251-100-S30-E05-0005
CABLE SCHEDULE
AGROOD-GPC-030

SUPPLIER DOUMENT REVIEW		PROJECT TITLE		NEW CRUDE OIL TANK FARM PROJECT	
<input checked="" type="checkbox"/> 1. Work may proceed. <input type="checkbox"/> 2. Revise and resubmit in accordance with comments,work may proceed subject to incorporation of changes indicated <input type="checkbox"/> 3. Revise and resubmit.(major comments)work may not proceed <input type="checkbox"/> 4. Rejected.(reason to be specified on the document). <input type="checkbox"/> 5. Hold for a specific reason(to be specified on the document).		PACKAGE DESCRIPTION		CATHODIC PROTECTION	
PERMISSION TO PROCEED DOES NOT CONSTITUTE ACCEPTANCE OR APPROVAL OF DESIGN DETAILS, CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS DEVELOPED OR SELECTED BY SUPPLIER FROM FULL COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.		EQUIPMANT TAG			
NAME Mohamed Mohsen Abdelbaeth		CODE IDENTIFIER		E10	SHEET 1 OF 7
SIGNATURE <i>M. Abdelbaeth</i>		DATE:		DOCUMENT NUMBER	REVISION
				1251-100-S30-E10-0005	1

1	ISSUED FOR APPROVAL	N/A	PB	DC	14/01/21
0	ISSUED FOR REVIEW	N/A	PB	DC	23/10/20
No.	DESCRIPTION	DCR No.	BY	CHECK	DATE
Corpro An Aegion™ Company Adam Street, Bowesfield Lane, Stockton-on-Tees, Cleveland TS18 3HQ. Tel: (01642) 614106. Fax: 614100 Telex: 587388					
Information shown on this drawing is confidential and must not be copied or conveyed to third parties without the express permission of Corpro Companies Europe Ltd. Certain items shown on this drawing are subject to worldwide patent applications.					
ENPPI		NEW CRUDE OIL TANK FARM PROJECT			
SINGLE LINE DIAGRAM AGROOD-GPC-030					
Drawn	PB	Date	23/10/2020	Checked	DC
Scale	NTS	DRG. No.	34501020-DWG-030	Date	23/10/2020
					Issue No. 1

400V AC 50Hz 3 PH. SUPPLY

50V 50A TRANSFORMER RECTIFIER

AG030-TR-002

35mm² XLPE/PVC CABLE

AG030-AJB-002

35mm² XLPE/PVC CABLE

AG030-NJB-002

35mm² XLPE/PVC CABLE

AG030-ASB-005

AG030-ASB-006

AG030-ASB-007

AG030-ASB-008

35mm² XLPE/PVC CABLE

6"-FW-030-054-A3-N
10"-CD-030-002-A3-N
6"-FW-030-109-A3-N
6"-FW-030-106-A3-N

16mm² XLPE/PVC CABLE

MMO ANODE 41
MMO ANODE 42
MMO ANODE 43
MMO ANODE 44
MMO ANODE 45
MMO ANODE 46
MMO ANODE 47
MMO ANODE 48
MMO ANODE 49
MMO ANODE 50

16mm² XLPE/PVC CABLE

MMO ANODE 51
MMO ANODE 52
MMO ANODE 53
MMO ANODE 54
MMO ANODE 55
MMO ANODE 56
MMO ANODE 57
MMO ANODE 58
MMO ANODE 59
MMO ANODE 60

16mm² XLPE/PVC CABLE

MMO ANODE 61
MMO ANODE 62
MMO ANODE 63
MMO ANODE 64
MMO ANODE 65
MMO ANODE 66
MMO ANODE 67
MMO ANODE 68
MMO ANODE 69
MMO ANODE 70

16mm² XLPE/PVC CABLE

MMO ANODE 71
MMO ANODE 72
MMO ANODE 73
MMO ANODE 74
MMO ANODE 75
MMO ANODE 76
MMO ANODE 77
MMO ANODE 78
MMO ANODE 79
MMO ANODE 80

REFERENCES


1251-100-S30-D99-0005
IN-PLANT PIPING LAYOUT
AGROOD-GPC-030

1251-100-S30-D99-0015
EQUIPMENT LAYOUT
AGROOD-GPC-030

1251-100-S30-E05-0005
CABLE SCHEDULE
AGROOD-GPC-030

SUPPLIER DOUMENT REVIEW		PROJECT TITLE		NEW CRUDE OIL TANK FARM PROJECT	
<input type="checkbox"/> 1. Work may proceed.		PACKAGE DESCRIPTION		CATHODIC PROTECTION	
<input type="checkbox"/> 2. Revise and resubmit in accordance with comments,work may proceed subject to incorporation of changes indicated		EQUIPMANT TAG			
<input type="checkbox"/> 3. Revise and resubmit.(major comments)work may not proceed		CODE IDENTIFIER		E10 SHEET 2 OF 7	
<input type="checkbox"/> 4. Rejected.(reason to be specified on the document).		NAME		DOCUMENT NUMBER	
<input type="checkbox"/> 5. Hold for a specific reason(to be specified on the document).		SIGNATURE		DATE:	
PERMISSION TO PROCEED DOES NOT CONSTITUTE ACCEPTANCE OR APPROVAL OF DESIGN DETAILS, CALCULATIONS, ANALYSIS, TEST METHODS OR MATERIALS DEVELOPED OR SELECTED BY SUPPLIER FROM FULL COMPLIANCE WITH CONTRACTUAL OBLIGATIONS.		1251-100-S30-E10-0005		1	

1	ISSUED FOR APPROVAL	N/A	PB	DC	14/01/21
0	ISSUED FOR REVIEW	N/A	PB	DC	23/10/20
No.	DESCRIPTION	DCR No.	BY	CHECK	DATE
corrpro An Aegion™ Company		Information shown on this drawing is confidential and must not be copied or conveyed to third parties without the express permission of Corpro Companies Europe Ltd. Certain items shown on this drawing are subject to worldwide patent applications.			
Adam Street,Bowesfield Lane, Stockton-on-Tees,Cleveland TS18 3HQ. Tel: (01642) 614106. Fax: 614100 Telex: 587388					
ENPPI		NEW CRUDE OIL TANK FARM PROJECT			
SINGLE LINE DIAGRAM AGROOD-GPC-030					
Drawn	PB	Date	23/10/2020	Checked	DC
Scale	NTS	DRG. No.	34501020-DWG-030	Issue No.	1





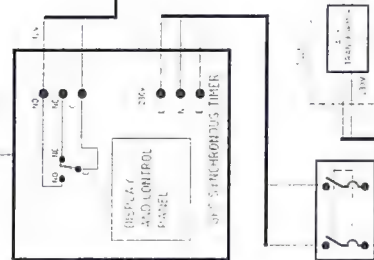
PROJECT	NEW CHAUDE OIL TANK FARM PROJECT	
TITLE	CATHODIC PROTECTION	
PROPOSED	DESCRIPTION	
<p>1. The proposed project is to install a cathodic protection system for the new Chaude Oil Tank Farm project.</p> <p>2. The proposed project is to install a cathodic protection system for the new Chaude Oil Tank Farm project.</p> <p>3. The proposed project is to install a cathodic protection system for the new Chaude Oil Tank Farm project.</p>		
DATE	099	SHEET 1 OF 1
DOCUMENT NUMBER	REVISION	

[illegible]

- 1 ALL SINGLE CODE VARIABLES ARE NUMERICAL AND COLOR CODED AND ALL MULTIPLE
VARIABLES ARE CATEGORICAL AND COLOR CODED
2 DASHES ARE USED TO INDICATE
3 UNASSIGNED QUESTIONS
4
5
6
7
8
9
10
11
12
13
14
15
16
17
18
19
20
21
22
23
24
25
26
27
28
29
30
31
32
33
34
35
36
37
38
39
40
41
42
43
44
45
46
47
48
49
50
51
52
53
54
55
56
57
58
59
60
61
62
63
64
65
66
67
68
69
70
71
72
73
74
75
76
77
78
79
80
81
82
83
84
85
86
87
88
89
90
91
92
93
94
95
96
97
98
99
100
101
102
103
104
105
106
107
108
109
110
111
112
113
114
115
116
117
118
119
120
121
122
123
124
125
126
127
128
129
130
131
132
133
134
135
136
137
138
139
140
141
142
143
144
145
146
147
148
149
150
151
152
153
154
155
156
157
158
159
160
161
162
163
164
165
166
167
168
169
170
171
172
173
174
175
176
177
178
179
180
181
182
183
184
185
186
187
188
189
190
191
192
193
194
195
196
197
198
199
200
201
202
203
204
205
206
207
208
209
210
211
212
213
214
215
216
217
218
219
220
221
222
223
224
225
226
227
228
229
230
231
232
233
234
235
236
237
238
239
240
241
242
243
244
245
246
247
248
249
250
251
252
253
254
255
256
257
258
259
260
261
262
263
264
265
266
267
268
269
270
271
272
273
274
275
276
277
278
279
280
281
282
283
284
285
286
287
288
289
290
291
292
293
294
295
296
297
298
299
300
301
302
303
304
305
306
307
308
309
310
311
312
313
314
315
316
317
318
319
320
321
322
323
324
325
326
327
328
329
330
331
332
333
334
335
336
337
338
339
340
341
342
343
344
345
346
347
348
349
350
351
352
353
354
355
356
357
358
359
360
361
362
363
364
365
366
367
368
369
370
371
372
373
374
375
376
377
378
379
380
381
382
383
384
385
386
387
388
389
390
391
392
393
394
395
396
397
398
399
400
401
402
403
404
405
406
407
408
409
410
411
412
413
414
415
416
417
418
419
420
421
422
423
424
425
426
427
428
429
430
431
432
433
434
435
436
437
438
439
440
441
442
443
444
445
446
447
448
449
450
451
452
453
454
455
456
457
458
459
460
461
462
463
464
465
466
467
468
469
470
471
472
473
474
475
476
477
478
479
480
481
482
483
484
485
486
487
488
489
490
491
492
493
494
495
496
497
498
499
500
501
502
503
504
505
506
507
508
509
510
511
512
513
514
515
516
517
518
519
520
521
522
523
524
525
526
527
528
529
530
531
532
533
534
535
536
537
538
539
540
541
542
543
544
545
546
547
548
549
550
551
552
553
554
555
556
557
558
559
560
561
562
563
564
565
566
567
568
569
570
571
572
573
574
575
576
577
578
579
580
581
582
583
584
585
586
587
588
589
590
591
592
593
594
595
596
597
598
599
600
601
602
603
604
605
606
607
608
609
610
611
612
613
614
615
616
617
618
619
620
621
622
623
624
625
626
627
628
629
630
631
632
633
634
635
636
637
638
639
640
641
642
643
644
645
646
647
648
649
650
651
652
653
654
655
656
657
658
659
660
661
662
663
664
665
666
667
668
669
670
671
672
673
674
675
676
677
678
679
680
681
682
683
684
685
686
687
688
689
690
691
692
693
694
695
696
697
698
699
700
701
702
703
704
705
706
707
708
709
710
711
712
713
714
715
716
717
718
719
720
721
722
723
724
725
726
727
728
729
730
731
732
733
734
735
736
737
738
739
740
741
742
743
744
745
746
747
748
749
750
751
752
753
754
755
756
757
758
759
760
761
762
763
764
765
766
767
768
769
770
771
772
773
774
775
776
777
778
779
780
781
782
783
784
785
786
787
788
789
790
791
792
793
794
795
796
797
798
799
800
801
802
803
804
805
806
807
808
809
810
811
812
813
814
815
816
817
818
819
820
821
822
823
824
825
826
827
828
829
830
831
832

350 351 352 353 354 355 356 357 358 359 360 361 362 363 364 365 366 367 368 369 370 371 372 373 374 375 376 377 378 379 380 381 382 383 384 385 386 387 388 389 390 391 392 393 394 395 396 397 398 399 400 401 402 403 404 405 406 407 408 409 410 411 412 413 414 415 416 417 418 419 420 421 422 423 424 425 426 427 428 429 430 431 432 433 434 435 436 437 438 439 440 441 442 443 444 445 446 447 448 449 450 451 452 453 454 455 456 457 458 459 460 461 462 463 464 465 466 467 468 469 470 471 472 473 474 475 476 477 478 479 480 481 482 483 484 485 486 487 488 489 490 491 492 493 494 495 496 497 498 499 500 501 502 503 504 505 506 507 508 509 510 511 512 513 514 515 516 517 518 519 520 521 522 523 524 525 526 527 528 529 530 531 532 533 534 535 536 537 538 539 540 541 542 543 544 545 546 547 548 549 550 551 552 553 554 555 556 557 558 559 560 561 562 563 564 565 566 567 568 569 570 571 572 573 574 575 576 577 578 579 580 581 582 583 584 585 586 587 588 589 590 591 592 593 594 595 596 597 598 599 600 601 602 603 604 605 606 607 608 609 610 611 612 613 614 615 616 617 618 619 620 621 622 623 624 625 626 627 628 629 630 631 632 633 634 635 636 637 638 639 640 641 642 643 644 645 646 647 648 649 650 651 652 653 654 655 656 657 658 659 660 661 662 663 664 665 666 667 668 669 670 671 672 673 674 675 676 677 678 679 680 681 682 683 684 685 686 687 688 689 690 691 692 693 694 695 696 697 698 699 700 701 702 703 704 705 706 707 708 709 710 711 712 713 714 715 716 717 718 719 720 721 722 723 724 725 726 727 728 729 730 731 732 733 734 735 736 737 738 739 740 741 742 743 744 745 746 747 748 749 750 751 752 753 754 755 756 757 758 759 760 761 762 763 764 765 766 767 768 769 770 771 772 773 774 775 776 777 778 779 780 781 782 783 784 785 786 787 788 789 790 791 792 793 794 795 796 797 798 799 800 801 802 803 804 805 806 807 808 809 810 811 812 813 814 815 816 817 818 819 820 821 822 823 824 825 826 827 828 829 830 831 832 833 834 835 836 837 838 839 840 841 842 843 844 845 846 847 848 849 850 851 852 853 854 855 856 857 858 859 860 861 862 863 864 865 866 867 868 869 870 871 872 873 874 875 876 877 878 879 880 881 882 883 884 885 886 887 888 889 890 891 892 893 894 895 896 897 898 899 900 901 902 903 904 905 906 907 908 909 910 911 912 913 914 915 916 917 918 919 920 921 922 923 924 925 926 927 928 929 930 931 932 933 934 935 936 937 938 939 940 941 942 943 944 945 946 947 948 949 950 951 952 953 954 955 956 957 958 959 960 961 962 963 964 965 966 967 968 969 970 971 972 973 974 975 976 977 978 979 980 981 982 983 984 985 986 987 988 989 990 991 992 993 994 995 996 997 998 999 1000 1001 1002 1003 1004 1005 1006 1007 1008 1009 1010 1011 1012 1013 1014 1015 1016 1017 1018 1019 1020 1021 1022 1023 1024 1025 1026 1027 1028 1029 1030 1031 1032 1033 1034 1035 1036 1037 1038 1039 1040 1041 1042 1043 1044 1045 1046 1047 1048 1049 1050 1051 1052 1053 1054 1055 1056 1057 1058 1059 1060 1061 1062 1063 1064 1065 1066 1067 1068 1069 1070 1071 1072 1073 1074 1075 1076 1077 1078 1079 1080 1081 1082 1083 1084 1085 1086 1087 1088 1089 1090 1091 1092 1093 1094 1095 1096 1097 1098 1099 1100 1101 1102 1103 1104 1105 1106 1107 1108 1109 1110 1111 1112 1113 1114 1115 1116 1117 1118 1119 1120 1121 1122 1123 1124 1125 1126 1127 1128 1129 1130 1131 1132 1133 1134 1135 1136 1137 1138 1139 1140 1141 1142 1143 1144 1145 1146 1147 1148 1149 1150 1151 1152 1153 1154 1155 1156 1157 1158 1159 1160 1161 1162 1163 1164 1165 1166 1167 1168 1169 1170 1171 1172 1173 1174 1175 1176 1177 1178 1179 1180 1181 1182 1183 1184 1185 1186 1187 1188 1189 1190 1191 1192 1193 1194 1195 1196 1197 1198 1199 1200 1201 1202 1203 1204 1205 1206 1207 1208 1209 1210 1211 1212 1213 1214 1215 1216 1217 1218 1219 1220 1221 1222 1223 1224 1225 1226 1227 1228 1229 1230 1231 1232 1233 1234 1235 1236 1237 1238 1239 1240 1241 1242 1243 1244 1245 1246 1247 1248 1249 1250 1251 1252 1253 1254 1255 1256 1257 1258 1259 1260 1261 1262 1263 1264 1265 1266 1267 1268 1269 1270 1271 1272 1273 1274 1275 1276 1277 1278 1279 1280 1281 1282 1283 1284 1285 1286 1287 1288 1289 1290 1291 1292 1293 1294 1295 1296 1297 1

GPS ANTENNA
APPROX. 3.5 FEET
(1.0M)



CONSTITUTIONAL
REPUBLIC OF
THE UNITED STATES
OF AMERICA

[illegible]

1
2
3
4
5
6
7
8
9
10
11
12
13
14
15
16
17
18
19
20
21
22
23
24
25
26
27
28
29
30
31
32
33
34
35
36
37
38
39
40
41
42
43
44
45
46
47
48
49
50
51
52
53
54
55
56
57
58
59
60
61
62
63
64
65
66
67
68
69
70
71
72
73
74
75
76
77
78
79
80
81
82
83
84
85
86
87
88
89
90
91
92
93
94
95
96
97
98
99
100
101
102
103
104
105
106
107
108
109
110
111
112
113
114
115
116
117
118
119
120
121
122
123
124
125
126
127
128
129
130
131
132
133
134
135
136
137
138
139
140
141
142
143
144
145
146
147
148
149
150
151
152
153
154
155
156
157
158
159
160
161
162
163
164
165
166
167
168
169
170
171
172
173
174
175
176
177
178
179
180
181
182
183
184
185
186
187
188
189
190
191
192
193
194
195
196
197
198
199
200
201
202
203
204
205
206
207
208
209
210
211
212
213
214
215
216
217
218
219
220
221
222
223
224
225
226
227
228
229
230
231
232
233
234
235
236
237
238
239
240
241
242
243
244
245
246
247
248
249
250
251
252
253
254
255
256
257
258
259
260
261
262
263
264
265
266
267
268
269
270
271
272
273
274
275
276
277
278
279
280
281
282
283
284
285
286
287
288
289
290
291
292
293
294
295
296
297
298
299
300
301
302
303
304
305
306
307
308
309
310
311
312
313
314
315
316
317
318
319
320
321
322
323
324
325
326
327
328
329
330
331
332
333
334
335
336
337
338
339
340
341
342
343
344
345
346
347
348
349
350
351
352
353
354
355
356
357
358
359
360
361
362
363
364
365
366
367
368
369
370
371
372
373
374
375
376
377
378
379
380
381
382
383
384
385
386
387
388
389
390
391
392
393
394
395
396
397
398
399
400
401
402
403
404
405
406
407
408
409
410
411
412
413
414
415
416
417
418
419
420
421
422
423
424
425
426
427
428
429
430
431
432
433
434
435
436
437
438
439
440
441
442
443
444
445
446
447
448
449
450
451
452
453
454
455
456
457
458
459
460
461
462
463
464
465
466
467
468
469
470
471
472
473
474
475
476
477
478
479
480
481
482
483
484
485
486
487
488
489
490
491
492
493
494
495
496
497
498
499
500
501
502
503
504
505
506
507
508
509
510
511
512
513
514
515
516
517
518
519
520
521
522
523
524
525
526
527
528
529
530
531
532
533
534
535
536
537
538
539
540
541
542
543
544
545
546
547
548
549
550
551
552
553
554
555
556
557
558
559
560
561
562
563
564
565
566
567
568
569
570
571
572
573
574
575
576
577
578
579
580
581
582
583
584
585
586
587
588
589
590
591
592
593
594
595
596
597
598
599
600
601
602
603
604
605
606
607
608
609
610
611
612
613
614
615
616
617
618
619
620
621
622
623
624
625
626
627
628
629
630
631
632
633
634
635
636
637
638
639
640
641
642
643
644
645
646
647
648
649
650
651
652
653
654
655
656
657
658
659
660
661
662
663
664
665
666
667
668
669
670
671
672
673
674
675
676
677
678
679
680
681
682
683
684
685
686
687
688
689
690
691
692
693
694
695
696
697
698
699
700
701
702
703
704
705
706
707
708
709
710
711
712
713
714
715
716
717
718
719
720
721
722
723
724
725
726
727
728
729
730
731
732
733
734
735
736
737
738
739
740
741
742
743
744
745
746
747
748
749
750
751
752
753
754
755
756
757
758
759
760
761
762
763
764
765
766
767
768
769
770
771
772
773
774
775
776
777
778
779
780
781
782
783
784
785
786
787
788
789
790
791
792
793
794
795
796
797
798
799
800
801
802
803
804
805
806
807
808
809
810
811
812
813
814
815
816
817
818
819
820
821
822
823
824
825
826
827
828
829
830
831
832
833
834
835
836
837
838
839
840
84

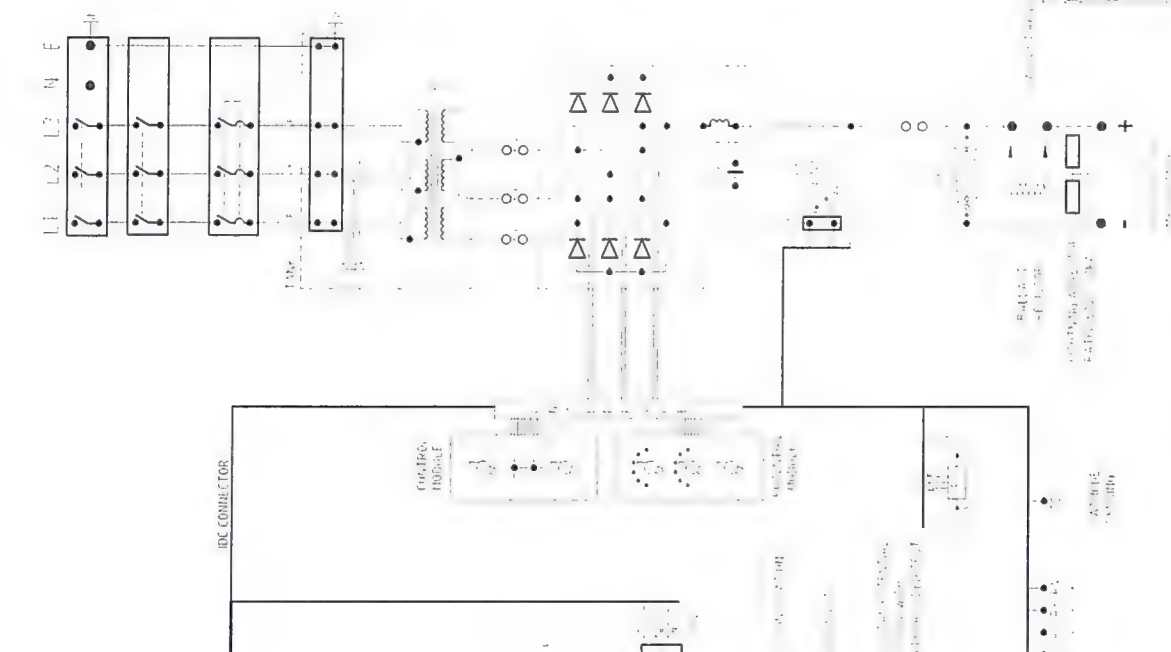
人

 Δ

1997, 1998, 1999, 2000, 2001, 2002, 2003, 2004, 2005, 2006, 2007, 2008, 2009, 2010, 2011, 2012, 2013, 2014, 2015, 2016, 2017, 2018, 2019, 2020, 2021, 2022, 2023, 2024, 2025, 2026, 2027, 2028, 2029, 2030, 2031, 2032, 2033, 2034, 2035, 2036, 2037, 2038, 2039, 2040, 2041, 2042, 2043, 2044, 2045, 2046, 2047, 2048, 2049, 2050, 2051, 2052, 2053, 2054, 2055, 2056, 2057, 2058, 2059, 2060, 2061, 2062, 2063, 2064, 2065, 2066, 2067, 2068, 2069, 2070, 2071, 2072, 2073, 2074, 2075, 2076, 2077, 2078, 2079, 2080, 2081, 2082, 2083, 2084, 2085, 2086, 2087, 2088, 2089, 2090, 2091, 2092, 2093, 2094, 2095, 2096, 2097, 2098, 2099, 2100, 2101, 2102, 2103, 2104, 2105, 2106, 2107, 2108, 2109, 2110, 2111, 2112, 2113, 2114, 2115, 2116, 2117, 2118, 2119, 2120, 2121, 2122, 2123, 2124, 2125, 2126, 2127, 2128, 2129, 2130, 2131, 2132, 2133, 2134, 2135, 2136, 2137, 2138, 2139, 2140, 2141, 2142, 2143, 2144, 2145, 2146, 2147, 2148, 2149, 2150, 2151, 2152, 2153, 2154, 2155, 2156, 2157, 2158, 2159, 2160, 2161, 2162, 2163, 2164, 2165, 2166, 2167, 2168, 2169, 2170, 2171, 2172, 2173, 2174, 2175, 2176, 2177, 2178, 2179, 2180, 2181, 2182, 2183, 2184, 2185, 2186, 2187, 2188, 2189, 2190, 2191, 2192, 2193, 2194, 2195, 2196, 2197, 2198, 2199, 2200, 2201, 2202, 2203, 2204, 2205, 2206, 2207, 2208, 2209, 2210, 2211, 2212, 2213, 2214, 2215, 2216, 2217, 2218, 2219, 2220, 2221, 2222, 2223, 2224, 2225, 2226, 2227, 2228, 2229, 2230, 2231, 2232, 2233, 2234, 2235, 2236, 2237, 2238, 2239, 2240, 2241, 2242, 2243, 2244, 2245, 2246, 2247, 2248, 2249, 2250, 2251, 2252, 2253, 2254, 2255, 2256, 2257, 2258, 2259, 2260, 2261, 2262, 2263, 2264, 2265, 2266, 2267, 2268, 2269, 2270, 2271, 2272, 2273, 2274, 2275, 2276, 2277, 2278, 2279, 2280, 2281, 2282, 2283, 2284, 2285, 2286, 2287, 2288, 2289, 2290, 2291, 2292, 2293, 2294, 2295, 2296, 2297, 2298, 2299, 2300, 2301, 2302, 2303, 2304, 2305, 2306, 2307, 2308, 2309, 2310, 2311, 2312, 2313, 2314, 2315, 2316, 2317, 2318, 2319, 2320, 2321, 2322, 2323, 2324, 2325, 2326, 2327, 2328, 2329, 2330, 2331, 2332, 2333, 2334, 2335, 2336, 2337, 2338, 2339, 2340, 2341, 2342, 2343, 2344, 2345, 2346, 2347, 2348, 2349, 2350, 2351, 2352, 2353, 2354, 2355, 2356, 2357, 2358, 2359, 2360, 2361, 2362, 2363, 2364, 2365, 2366, 2367, 2368, 2369, 2370, 2371, 2372, 2373, 2374, 2375, 2376, 2377, 2378, 2379, 2380, 2381, 2382, 2383, 2384, 2385, 2386, 2387, 2388, 2389, 2390, 2391, 2392, 2393, 2394, 2395, 2396, 2397, 2398, 2399, 2400, 2401, 2402, 2403, 2404, 2405, 2406, 2407, 2408, 2409, 2410, 2411, 2412, 2413, 2414, 2415, 2416, 2417, 2418, 2419, 2420, 2421, 2422, 2423, 2424, 2425, 2426, 2427, 2428, 2429, 2430, 2431, 2432, 2433, 2434, 2435, 2436, 2437, 2438, 2439, 2440, 2441, 2442, 2443, 2444, 2445, 2446, 2447, 2448, 2449, 2450, 2451, 2452, 2453, 2454, 2455, 2456, 2457, 2458, 2459, 2460, 2461, 2462, 2463, 2464, 2465, 2466, 2467, 2468, 2469, 2470, 2471, 2472, 2473, 2474, 2475, 2476, 2477, 2478, 2479, 2480, 2481, 2482, 2483, 2484, 2485, 2486, 2487, 2488, 2489, 2490, 2491, 2492, 2493, 2494, 2495, 2496, 2497, 2498, 2499, 2500, 2501, 2502, 2503, 2504, 2505, 2506, 2507, 2508, 2509, 2510, 2511, 2512, 2513, 2514, 2515, 2516, 2517, 2518, 2519, 2520, 2521, 2522, 2523, 2524, 2525, 2526, 2527, 2528, 2529, 2530, 2531, 2532, 2533, 2534, 2535, 2536, 2537, 2538, 2539, 2540, 2541, 2542, 2543, 2544, 2545, 2546, 2547, 2548, 2549, 2550, 2551, 2552, 2553, 2554, 2555, 2556, 2557, 2558, 2559, 2560, 2561, 2562, 2563, 2564, 2565, 2566, 2567, 2568, 2569, 2570, 2571, 2572, 2573, 2574, 2575, 2576, 2577, 2578, 2579, 2580, 2581, 2582, 2583, 2584, 2585, 2586, 2587, 2588, 2589, 2590, 2591, 2592, 2593, 2594, 2595, 2596, 2597, 2598, 2599, 2600, 2601, 2602, 2603, 2604, 2605, 2606, 2607, 2608, 2609, 2610, 2611, 2612, 2613, 2614, 2615, 2616, 2617, 2618, 2619, 2620, 2621, 2622, 2623, 2624, 2625, 2626, 2627, 2628, 2629, 2630, 2631, 2632, 2633, 2634, 2635, 2636, 2637, 2638, 2639, 2640, 2641, 2642, 2643, 2644, 2645, 2646, 2647, 2648, 2649, 2650, 2651, 2652, 2653, 2654, 2655, 2656, 2657, 2658, 2659, 2660, 2661, 2662, 2663, 2664, 2665, 2666, 2667, 2668, 2669, 2670, 2671, 2672, 2673, 2674, 2675, 2676, 2677, 2678, 26

[illegible]

Figure 1 is a schematic representation of the experimental design. It shows a sequence of events: a subject is presented with a stimulus (a circle with a dot), then a response is recorded (a circle with a dot), and finally, the subject is presented with a stimulus (a circle with a dot). The response is recorded, and the stimulus is presented again. The sequence is labeled 'Stimulus', 'Response', and 'Stimulus'.



Rev.	Details	Drawn	Checked	Date
5	RE ISSUED FOR APPROVAL	SMP	DS	23/06/20
4	RE ISSUED FOR APPROVAL	SMP	DS	15/05/20
3	RE ISSUED FOR APPROVAL	SMP	DS	14/05/20
2	RE ISSUED FOR APPROVAL	SMP	DS	09/04/20
1	RE ISSUED FOR APPROVAL	SMP	DS	30/03/20
0	ISSUED FOR APPROVAL	SMP	DS	13/03/20

1251-210-S30-M04-0001 - DATA SHEETS
1251-100-S30-G99-0004 - TAG NUMBERS
Reference Drawings

Journal of Management Inquiry 22(4)

<p>MOHAMED MOHSEN</p> <p>15/07</p>	<p>THE CATHODIC PROTECTION SYSTEM TRANSFORMER</p> <p>RECTIFIER AUTOMATIC 3PH SCHEMATIC</p> <p>CIRCUIT DIAGRAM SHEET NO. 50V DC</p>	<p>Drawn SMP Checked DS Date 13/03/20 Scale NTS A3 Sup</p>	<div data-bbox="1367 271 1393 342"> </div> <div data-bbox="1394 271 1410 342"> <p>ROCKWAY CORPORATION</p> </div> <div data-bbox="1412 271 1428 342"> <p>10000 34500000000</p> </div> <div data-bbox="1430 271 1445 342"> <p>COMPANY REVISION</p> </div> <div data-bbox="1447 271 1463 342"> <p>CD-0375-1001</p> </div> <div data-bbox="1465 271 1481 342"> <p>10000 34500000000</p> </div> <div data-bbox="1482 271 1498 342"> <p>COMPANY REVISION</p> </div> <div data-bbox="1500 271 1506 342"> <p>10000 34500000000</p> </div>
------------------------------------	--	--	--





Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

12.03- Motor Datasheets




Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

12.04- Electrical Cables Schedule

PAGE	Cable Mark	GL1	FROM	TO	GL2	CABLE SERVICE	SERVICE VOLTAGE	KW	SIZE	TYPE	L
31	P-030-1T0-C/PR	WP	030-SUB-ASP-1 (Q37)	CP Transformer for Fire Water Tank	EX	3PH POWER FEEDER	400VAC	2.5	3x10	3C	150
31	P-AG030-TR-001	WP	030-SUB-ASP-1 (Q38)	CP Transformer-1 for U/G Piping	EX	3PH POWER FEEDER	400VAC	2.5	3x10	3C	320
31	P-AG030-TR-002	WP	030-SUB-ASP-1 (Q39)	CP Transformer-2 for U/G Piping	EX	3PH POWER FEEDER	400VAC	2.5	3x10	3C	770
31	P-AG030-TR-003	WP	030-SUB-ASP-1 (Q40)	CP Transformer-3 for U/G Piping	EX	3PH POWER FEEDER	400VAC	2.5	3x10	3C	1230
31	P-AG030-TR-004	WP	030-SUB-ASP-1 (Q41)	CP Transformer-4 for U/G Piping	EX	3PH POWER FEEDER	400VAC	2.5	3x10	3C	880
31	P-AG030-TR-005	WP	030-SUB-ASP-1 (Q42)	CP Transformer-5 for U/G Piping	EX	3PH POWER FEEDER	400VAC	2.5	3x10	3C	330
31	P-AG030-TR-006	WP	030-SUB-ASP-1 (Q43)	CP Transformer-6 for U/G Piping	EX	3PH POWER FEEDER	400VAC	2.5	3x10	3C	240
46	P-030-1T0-C/PR	WP	030-EPM1-LVSWG-1 (A2.4)	CP Transformer for Crude Oil Tank	WP	3PH POWER FEEDER	400VAC	15	3x10	3C	130
51	P-030-1T0-C/PR	WP	030-EPM2-LVSWG-1 (A2.4)	CP Transformer for Crude Tank	WP	3PH POWER FEEDER	400VAC	15	3x10	3C	130
56	P-030-1T0-C/PR	WP	030-EPM3-LVSWG-1 (A2.4)	CP Transformer for Crude Tank	WP	3PH POWER FEEDER	400VAC	15	3x35	3C	300
61	P-030-1T0-C/PR	WP	030-EPM4-LVSWG-1 (A2.4)	CP Transformer for Crude Tank	WP	3PH POWER FEEDER	400VAC	15	3x35	3C	330





Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID

030-CP-001

System Description

Piping Cathodic Protection System

12.05- Electrical Cables Laying Certificates




Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)




System ID	030-CP-001
System Description	Piping Cathodic Protection System

12.06- Electrical Cables Testing Certificates



EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE INSULATION RESISTANCE TEST

INSPECTION REPORT NUMBER
RFI- 262

SYSTEM NO.:

INSTRUMENT TYPE:

DOCUMENT No.
ITR-EL-0006A

SHEET NO

INSPECTION DATE & TIME

DISCIPLINE
ELECTRICAL

AREA / PACKAGE:

SERIAL:

SERVICE VOLTAGE:
220 V

TEST VOLTAGE:
1kv

NO	Item/Tag NO.	CABLE SIZE	Continuity Test	PHASE TO PHASE "M.Ohm"			PHASE TO NEUTRAL "M.Ohm"			PHASES & NEUTRAL TO ARMOR "M.Ohm"			RESULT	
				BR-BK	BR-GR	BK-GR	BR-B	BK-B	GR-B	BR-ARM	BK-ARM	GR-ARM	B-ARM	Pass
1	P-030-SUB-ACUPS-1A	3.5x120	✓											
2	P-030-SUB-ACUPS-1B	3.5x120	✓											
3	P-030-SUB-ACUPS-BP	3.5x50	✓											
4	C-030-SUB-PC-1	3x2.5	✓											
5	P-030-TEL-CPR	3x16	✓											
6														
7														
8														
9														
10														
11														
12														
13														
14														
15														
16														
17														
18														
19														
20														
21														

Remarks :-

Reference :-

NAME :

SIGNATURE

DATE

PETROJET

ENPPI

PMC

R Islam Shriv

R Islam Shriv

R Islam Shriv

ITR-EL-0006A



Enppi

EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE INSULATION RESISTANCE TEST

INSPECTION REPORT NUMBER

REF: 177

INSTRUMENT TYPE:

SERIAL:

INSPECTION DATE & TIME

DOCUMENT No
ITR-EL-0006A

SYSTEM NO

SHEET NO

DISCIPLINE
ELECTRICAL

AREA / PACKAGE

SERVICE VOLTAGE
220 V

TEST VOLTAGE
1kv

N O	Item/Tag NO.	CABLE SIZE	Continuity Test	PHASE TO PHASE "M. Ohm"			PHASE TO NUETRAL "M. Ohm"			PHASES & NUETRAL TO ARMOR "M. Ohm"				RESULT	
				BR-BK	BR-GR	BK-GR	BR-B	BK-B	GR-B	BR-ARM	BK-ARM	GR-ARM	B-ARM	Pass	FAIL
1	PAGE 01-18-01	N/D	✓				0.5							✓	
2	PAGE 01-18-02	N/D	✓				0.5							✓	
3	PAGE 01-18-03	N/D	✓				0.5							✓	
4	PAGE 01-18-04	N/D	✓				0.5							✓	
5															
6			✓												
7															
8															
9															
10															
11															
12															
13															
14															
15															
16															
17															
18															

Remarks :-

Reference :-

PETROJET		ENPPI		PMC
NAME				
SIGNATURE				
DATE				

ITR-EL-0006A

CABLE INSULATION RESISTANCE TEST

INSPECTION REPORT NUMBER

PTJ-ELE-RFI-214

INSTRUMENT TYPE:

HIGH VOLTAGE INSULATION TESTER-SANWA-MG5000

INSPECTION DATE & TIME

13/06/2021, ITR-EL-0006A

DISCIPLINE

ELECTRICAL

SHEET NO

1000

AREA / PACKAGE:

SUBSTATION

SERIAL:

17015900385

SERVICE VOLTAGE: 400

TEST VOLTAGE:

1000

NO	Item/Tag NO.	CABLE SIZE	Continuity Test	PHASE TO PHASE			PHASE TO NEUTRAL "M.Ohm"			PHASES & NEUTRAL TO ARMOR			RESULT		
				BR-BK	BR-GR	BK-GR	BR-B	BK-B	GR-B	BR-ARM	BK-ARM	GR-ARM	B-ARM	Pass	FAIL
16	M-030-MXM-04E, JB	3x95	✓											✓	
17	M 030-MXM-04E	3x50	✓											✓	
18	M 030-MXM-04F, JB	3x95	✓											✓	
19	M 030-MXM-04F	3x50	✓											✓	
20	P 030 SW 004	3x4	✓											✓	
21	P 030 LI 004C	3x4	✓											✓	
22	P-AG030-TR-003	3x10	✓											✓	
23	P 030-T04-CPTR	3x35	✓											✓	
24	P-030-SOV-104	4 X 4	✓											✓	
25															
26															
27															
28															
29															
30															
31															

Remarks :-

Reference :-



Enppi

EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE INSULATION RESISTANCE TEST

INSPECTION REPORT NUMBER
PTJ-ELE-RF1

INSTRUMENT TYPE:

HIGH VOLTAGE INSULATION TESTER-SANWA-MG5000

INSPECTION DATE & TIME

03/07/2021

DOCUMENT No

ITR-EL-0006A

DISCIPLINE

ELECTRICAL

SYSTEM NO :

SHEET NO

SERIAL:

17015900385

SERVICE VOLTAGE: 400

TEST VOLTAGE: 1000

AREA / PACKAGE:

SUBSTATION

NO	Item/Tag NO.	CABLE SIZE	Continuity Test	PHASE TO PHASE			PHASE TO NEUTRAL "M.Ohm"			PHASES & NEUTRAL TO ARMOR			RESULT	
				BR-BK	BR-GR	BK-GR	BR-B	BK-B	GR-B	BR-ARM	BK-ARM	GR-ARM	Pass	FAIL
1	P-AG030-TR-002	3x10	✓	OK	OK	OK							✓	
2	N1-030-EPM2-LTG	3x10	✓	OK	OK	OK							✓	
3	P-030-T02-CPIR	3x10	✓										✓	
4	P1-030-EPM2-CR-1	3x16	✓										✓	
5	P-030-SW-002	3x4	✓										✓	
6	P-030-LI-002C	3x4	✓										✓	
7	M-030-MXM-02A	3x50	✓										✓	
8	M-030-MXM-02B	3x50	✓										✓	
9	M-030-MXM-02C	3x50	✓										✓	
10	M-030-MXM-02D	3x50	✓										✓	
11	M-030-MXM-02E	3x50	✓										✓	
12	M-030-MXM-02F	3x50	✓										✓	
13	M-030-MXM-02A, JB	3x95	✓										✓	
14	M-030-MXM-02B, JB	3x95	✓										✓	
15	M-030-MXM-02C, JB	3x95	✓										✓	
16	M-030-MXM-02D, JB	3x95	✓										✓	
17	M-030-MXM-02E, JB	3x95	✓										✓	
18	M-030-MXM-02F, JB	3x95	✓										✓	

Remarks :-

Reference :-

PETROJET		ENRPI	PMC
NAME :		Isam	
SIGNATURE			
DATE			

ITR-EL-0006A



Enppi

EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE INSULATION RESISTANCE TEST

INSPECTION REPORT NUMBER

PTJ-ELE-RFI-

INSTRUMENT TYPE:

HIGH VOLTAGE INSULATION TESTER-SANWA-MG5000

INSPECTION DATE & TIME

28/06/2021

DOCUMENT No.

ITR-EL-0006A

DISCIPLINE

ELECTRICAL

SYSTEM NO.:

SHEET NO

SERIAL:

17015900385

SERVICE VOLTAGE: 400

TEST VOLTAGE: 1000

AREA / PACKAGE:

SUBSTATION

NO	Item/Tag NO.	CABLE SIZE	Continuity Test	PHASE TO PHASE			PHASE TO NEUTRAL "M.Ohm"			PHASES & NEUTRAL TO ARMOR			RESULT			
				BR-BK	BR-GR	BK-GR	BR-B	BK-B	GR-B	BR-ARM	BK-ARM	GR-ARM	B-ARM	Pass	FAIL	
19	C1-030-PM-06B	12x2.5	✓												✓	
20	C3-030-PM-06B	8x(3x2.5)	✓												✓	
21	H-030-PM-06C	3x10	✓												✓	
22	C1-030-PM-06C	12x2.5	✓												✓	
23	C3-030-PM-06C	8x(3x2.5)	✓												✓	
24	H-030-PM-06D	3x10	✓												✓	
25	C1-030-PM-06D	12x2.5	✓												✓	
26	C3-030-PM-06D	8x(3x2.5)	✓												✓	
27	M-030-PM-03A	3x35	✓												✓	
28	C1-030-PM-03A	10x2.5	✓												✓	
29	C3-030-PM-03A	1x3x2.5	✓												✓	
30	M-030-PM-03B	3x35	✓												✓	
31	C1-030-PM-03B	10x2.5	✓												✓	
32	C3-030-PM-03B	1x3x2.5	✓												✓	
33	P-030-T10-CPTR	3x10	✓												✓	
34	P-AG030-TR-001	3x10	✓												✓	
35	P-AG030-TR-006	3x10	✓												✓	
36	P-030-MOV-004	4x4	✓												✓	

Remarks :-

Reference :-

	PETROJET	ENPPI	PMC



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

12.07- Electrical Cables Termination Certificates

**Enppi**

EGPC CRUDE OIL TANK FARM



Owner : Egyptian General Petroleum Corporation (EGPC)

Project No: 01251-100-030
:01251-100-031

Contractor CONSORTIUM (ENPPI / PETROJET)

Document No: ITR-QC-0001
Revision No. : 00**REQUEST FOR INSPECTION**

ACTIVITY : CABLE TERMINATION AND SPLICING

NOTIFICATION NO. : PTJ-ELEC-RFI-262 DISCIPLINE : E&I

DATE : 10/23/2021

NO.	DESCRIPTION	LOCATION	DATE / TIME	INSPECTION			REMARKS
				PETROJET	ENPPI	PMC	
	CABLE TERMINATION AND SPLICING	MODULE 1	23-Oct-21				
1	P-030-SUB-ACUPS-1A						
2	P-030-SUB-ACUPS-1B						
3	P-030-SUB-ACUPS-BP						
4	C-030-SUB-PC-I						
5	P-030-T01-CPTR						
6							
7							
8							
9							
10							
11							
12							
13							
14							
15							
16							
17							
18							
19							
20							
21							

NOTE:

Inspection result : A - Approved B - Reject C - Approved with Comment

	PETROJET	ENPPI	PMC
NAME :			
SIGNATURE			
DATE			

ITR-QC-0001

**Enppi**

PETROJET

EGPC CRUDE OIL TANK FARM

INSPECTION AND TEST REPORT FOR

CABLE TERMINATION AND SPLICING

SYSTEM NO.:

INSPECTION REPORT NUMBER

INSPECTION DATE & TIME

ITR NUMBER

DISCIPLINE

SHEET NO

ITR-EL-0009

ELEC

1 OF 1

Item/Tag NO.

Type :-

Core:

Size:

NO.	Description of check	RESULT		
		ACCEPT	REJECT	N/A.
1	Check cable glands are correct type and size as per cable schedule.	✓		
2	Check there are no damages to cores, termination chamber layout is satisfactory, core identification is correct, crimped and pins satisfactory.	✓		
3	Check cable tag is done correctly.	✓		
4	Test and confirm conductor, phase continuity.	✓		
5	Check insulation resistance test (megger) is completed *1	✓		
6	Check Hi-pot test is completed, only for MV/HV cables **			✓
7	Connect all cores at both ends and confirm all connections are correct as per termination diagram.	✓		
8	Confirm spare cores, screens are earthed and conform to design drawings/specifications	✓		
9	Check enclosure cover is installed, no damages and no bolts are missing	✓		
10	Calibration test certificate of testing equipment to be checked.			✓

Remarks :

	PETROJET	ENPPI	PMC
NAME :			
SIGNATURE			
DATE			

ITR-EL-0009

**Enppi**

EGPC TANK FARM



Owner : Egyptian General Petroleum Corporation (EGPC)

Project No: 01251-100-030
:01251-100-031

Contractor CONSORTIUM (ENPPI / PETROJET)

Document No: ITR-QC-0001
Revision No. : 00**REQUEST FOR INSPECTION**

ACTIVITY : Test Post / ANODE Installation

NOTIFICATION NO. : PTJ-ELE-RFI-178

DISCIPLINE : Cathodic

DATE : 4/26/2021

NO.	DESCRIPTION	LOCATION	DATE / TIME	INSPECTION			REMARKS
				PETROJET	ENPPI	PMC	
	Test Post/ANODE Installation	AGROOD #01					
16	ANODE 125						
17	ANODE 126						
18	ANODE 127						
19	CONNECTION POINT 4						
20	CONNECTION POINT 9						
21	AG030-TR-004						
22	ANODE JB						
23	NEGATIVE JB						
24	AG030-TR-005						
25	ANODE JB						
26	NEGATIVE JB						
27	030-T03-CPTR						
28	2 ANODE JB						
29	NEGATIVE JB						
30	030-T04-CPTR						

NOTE:

Inspection result : A - Approved B - Reject C - Approved with Comment

	PETROJET	ENPPI	PMC
NAME			
SIGNATURE			
DATE			



PETROJET
The Petroleum Projects and
Technical Consultations Co
One of the Egyptian General Petroleum Corporation
Companies

INSPECTION AND TEST REPORT FOR

MMO ANODE INSTALLATION

INSPECTION REPORT NUMBER

→ RFI-178

INSPECTION DATE & TIME

DOCUMENT No.

ITR-CP-0006

DISCIPLINE

ELECTRICAL

SHEET NO

1 OF 1

JOB DESCRIPTION

PIPELINE CATHODIC PROTECTION SYSTEM

AREA DESCRIPTION

AGROUD MODULE 2 PIPELINE

ITEM TAG NO.

DRAWING NO.

1251-100-S30-D99-0006

LOCATION

NO.	INSPECTION	RESULT		
		ACCEPT	REJECT	N/A.
1	Anode installation area free from metallic debris prior to installation and level	✓		
2	Anode visually inspected for damage prior to installation	✓		
3	MMO installed as relevant drawing	✓		
4	Conductor Bar installed as relevant drawing	✓		
5	Continuity test shall be conducted between Conductor bar and MMO anode prior to backfilling			✓
6	All spot welding at crossing locations visually inspected and checked			✓
7	Power feed connectors installed at correct locations as relevant drawing			✓
8	Power feed cables have no physical damage with sufficient slack cable to permit exit from ring beam and termination in junction box	✓		
9	Continuity test shall be conducted for all Power feed cables before and after backfilling.			✓
10	No Interference or contact with the tank external surfaces			✓
11	Cable routing	✓		
12	Carefully backfill sand over anode to required depth under the tank which is free from rocks, boulders and metallic debris	✓		
13	Output current measurement at power feed cables			✓
14	Waste materials removed from site	✓		

REMARKS:

CONSORTIUM (ENPPI /PETROJET)		EGPC
NAME		
SIGNATURE		
NAME	Islam Sherif	

ITR-CP-0006



#REF.



PETROJET
The Petroleum Projects and
Technical Consultations Co
One of the Egyptian General Petroleum
Corporation Companies

INSPECTION AND TEST REPORT FOR

TRANSFORMER RECTIFIER INSTALLATION

INSPECTION REPORT NUMBER

INSPECTION DATE & TIME

DOCUMENT No

DISCIPLINE

SHEET NO

TR-CP-0003

ELECTRICAL

1 OF 1

JOB DESCRIPTION

AREA DESCRIPTION

ITEM / TAG NO

DRAWING NO.

LOCATION

NO.	INSPECTION	RESULT		
		ACCEPT	REJECT	N/A.
1	Correct transformer rectifier installed and at correct location	✓		
2	Location of junction box and precast foundation to be identified	✓		
3	Transformer rectifier is properly secured on the concrete plinch and positioned with easy access for monitoring and adjustment	✓		
4	Terminated cables were provided with sufficient slack to permit cables to be removed from the connection terminals	✓		
5	Installation of junction box and identification	✓		
6	Cable identification and termination as per approved IFC drawing	✓		
7	All other TR UNIT external components (silica gel breather, thermometer, oil indicator, sunshade, etc) are secured and inspected any physical damage	✓		
8	Specified T/R cooling oil is filled to the recommended oil level	✓		
9	T/R unit is completely installed without any physical damage (internal or external) and with proper earthing	✓		
10	Final visual inspection	✓		

REFERENCE DOCUMENTS:

CONSORTIUM (ENPPI / PETROJET

EGPC

ITR-CP-0003



EGPC CELESTE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

TERMINAL BOXES AND TEST STATIONS INSTALLATION

INSPECTION REPORT NUMBER

INSPECTION DATE & TIME

DOCUMENT No

DISCIPLINE

SHEET NO

ELECTRICAL

1 OF 1

JOB DESCRIPTION

AREA DESCRIPTION

JOB NO.

TP 4.5


DRAWING NO.

LOCATION

NO.	INSPECTION	RESULT		
		ACCEPT	REJECT	N/A.
1	Connection areas cleaned to bright metal	✓		
2	Visual examination of connection	✓		
3	Cable to Structure connection encapsulated and sealed with suitable coating repair/insulation material	✓		
4	Check terminal boxes, test station type and installed location			✓
5	Terminal boxes, test station installed without any damages			✓
6	Cable terminated with sufficient slack (where possible) to permit cables to be removed from the connection terminals			✓
7	Cables are correctly terminated inside the junction box and correctly identified with permanent cable tag			✓
8	Cable glands are securely fitted around cables and blanking plugs fitted where necessary			✓
9	Terminal boxes, test station & mounting frame secured in the concrete footing			✓
10	Terminal boxes, test stations are installed at sufficient height from the ground level			✓
11	Final visual inspection	✓		

REMARKS:

	PETROJET	ENPPI	PMC
NAME			
SIGNATURE			
DATE			



EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

TERMINAL BOXES AND TEST STATIONS INSTALLATION

INSPECTION REPORT NUMBER

INSPECTION DATE & TIME

DOCUMENT No.

DISCIPLINE

SHEET NO

ELECTRICAL

1 OF 1

JOB DESCRIPTION

AREA DESCRIPTION

TERMINAL BOXES AND TEST STATIONS INSTALLATION

ITEM TAG NO

Junction Boxes

DRAWING NO

LOCATION

NO.	INSPECTION	RESULT		
		ACCEPT	REJECT	N/A.
1	Connection areas cleaned to bright metal	✓		
2	Visual examination of connection	✓		
3	Cable to Structure connection encapsulated and sealed with suitable coating repair/insulation material	✓		
4	Check terminal boxes, test station type and installed location	✓		
5	Terminal boxes, test station installed without any damages	✓		
6	Cable terminated with sufficient slack (where possible) to permit cables to be removed from the connection terminals	✓		
7	Cables are correctly terminated inside the junction box and correctly identified with permanent cable tag	✓		
8	Cable glands are securely fitted around cables and blanking plugs fitted where necessary	✓		
9	Terminal boxes, test station & mounting frame secured in the concrete footing	✓		
10	Terminal boxes, test stations are installed at sufficient height from the ground level	✓		
11	Final visual inspection	✓		

REMARKS:

	PETROJET	ENPPI	PMC
NAME			
SIGNATURE	<i>[Signature]</i>	<i>[Signature]</i>	<i>[Signature]</i>
DATE			

**Enppi**

EGPC CRUDE OIL TANK FARM



Owner : Egyptian General Petroleum Corporation (EGPC)

Project No: 01251-100-030
:01251-100-031

Contractor CONSORTIUM (ENPPI / PETROJET)

Document No: ITR-QC-0001
Revision No. : 00**REQUEST FOR INSPECTION**

ACTIVITY : CATHODIC PROTECTION TRANSFORMER & JB INSTALLATION

NOTIFICATION NO. : PTJ-elec-RFI- 226 DISCIPLINE : E&I

DATE : 6/26/2021

NO.	DESCRIPTION	LOCATION	DATE / TIME	INSPECTION			REMARKS
				PETROJET	ENPPI	PMC	
	CATHODIC PROTECTION TRANSFORMER & JB INSTALLATION	MODULE 1	26-Jun-21				
1	AG030-TR-002						
1.1	NJB2						
1.2	AJB2						
1.3	AG030						
2	AG030-TR-006						
2.1	NJB6						
2.2	AJB6						
3	AG030-TR-001						
3.1	NJB1						
3.2	AJB1						
3.3	AG030						
4	030-T10-CPTR						
4.1	NJB						
4.2	AJB						
5.1	030-T02-CPTR						
5.2	2 AJB						
5.3	NJB						
	030-T01-CPTR	AG030-TR-003					
	2 AJB	NJB03					
	NJB	AJB03					

NOTE:

Inspection result : A - Approved B - Reject C - Approved with Comment

Marked-up to be done Supplier checklist to be followed

	PETROJET	ENPPI	PMC
NAME			
SIGNATURE			
DATE			

ITR-QC-0001



EGPC CRUDE OIL TANK FARM



PETROJET
The Petroleum Projects and
Technical Consultations Co
One of the Egyptian General Petroleum
Corporation Companies

INSPECTION AND TEST REPORT FOR

TRANSFORMER RECTIFIER INSTALLATION

INSPECTION REPORT NUMBER

226

INSPECTION DATE & TIME

DOUCUMENT No.

ITR-CP-0003

DISCIPLINE

ELECTRICAL

SHEET NO

1 OF 1

JOB DESCRIPTION

AREA DESCRIPTION

ITEM / TAG NO.

DRAWING NO.

LOCATION

NO.	INSPECTION	RESULT		
		ACCEPT	REJECT	N/A.
1	Correct transformer rectifier installed and at correct location	✓		
2	Location of junction box and precast foundation to be identified	✓		
3	Transformer rectifier is properly secured on the concrete plinch and positioned with easy access for monitoring and adjustment	✓		
4	Terminated cables were provided with sufficient slack to permit cables to be removed from the connection terminals	✓		
5	Installation of junction box and identification	✓		
6	Cable identification and termination as per approved IFC drawing	✓		
7	All other TR UNIT external components (silica gel breather, thermometer, oil indicator, sunshade, etc) are secured and inspected any physical damage	✓		
8	Specified T/R cooling oil is filled to the recommended oil level	✓		
9	T/R unit is completely installed without any physical damage (internal or external) and with proper earthing	✓		
10	Final visual inspection	✓		

REFERENCE DOCUMENTS:

PETROJET		ENPPI	
NAME		NAME	
SIGNATURE		SIGNATURE	
DATE		DATE	

ITR-CP-0003



EGPC CRUDE OIL TANK FARM



PETROJET
The Petroleum Projects and
Technical Consultations Co
One of the Egyptian General Petroleum
Corporation Companies

INSPECTION AND TEST REPORT FOR

TERMINAL BOXES AND TEST STATIONS INSTALLATION

INSPECTION REPORT NUMBER

226

INSPECTION DATE & TIME

DOCUMENT No.

ITR-CP-0004

DISCIPLINE

ELECTRICAL

SHEET NO

1 OF 1

JOB DESCRIPTION

AREA DESCRIPTION

ITEM / TAG NO.

DRAWING NO.

LOCATION

NO.	INSPECTION	RESULT		
		ACCEPT	REJECT	N/A.
1	Check terminal boxes, test station type and installed location	✓		
2	Terminal boxes, test station installed without any damages	✓		
3	Cable terminated with sufficient slack (where possible) to permit cables to be removed from the connection terminals	✓		
4	Cables are correctly terminated inside the junction box and correctly identified with permanent cable tag	✓		
5	Cable glands are securly fitted around cables and blanking plugs fitted where necessary	✓		
6	Terminal boxes, test station & mounting frame secured in the concrete footing	✓		
7	Terminal boxes, test stations are installed at sufficient height from the ground level	✓		
8	Final visual inspection	✓		

REMARKS:

PETROJET

NAME:

SIGNATURE

DATE

NAME

SIGNATURE

DATE

ENPPI

ITR-CP-0004



Enppi

EGPC



Owner : Egyptian General Petroleum Corporation (EGPC)

Project No: 01251-100-030
:01251-100-031

Contractor CONSORTIUM (ENPPI / PETROJET)

Document No: ITR-QC-0001
Revision No. : 00

REQUEST FOR INSPECTION

ACTIVITY : cable termination and splicing

NOTIFICATION NO. : PTJ-ELEC-RFI-179 DISCIPLINE : E&I

DATE : 4/26/2021

NO.	DESCRIPTION	LOCATION	DATE / TIME	INSPECTION			REMARKS
				PETROJET	ENPPI	PMC	
	cable termination	MODULE 1	26-Apr-21				
1	Plugs to be installed in transformer side (Done) Sd						
2	5.5 tag for the cables to be installed (Done) Sd						
3							
4							
5							
6							
7							
8							
9							
10							
11							
12							
13							
14							
15							
16							
17							
18							

NOTE:

1- plugs to be installed in transformer side (Done) Sd
2- 5.5 tag for the cables to be installed (Done) Sd

Inspection result : A - Approved B - Reject C - Approved with Comment

	PETROJET	ENPPI	PMC
NAME		Sherrif	
SIGNATURE			
DATE			

ITR-QC-0001



EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE TERMINATION AND SPLICING

SYSTEM NO.:

INSPECTION REPORT NUMBER

INSPECTION DATE & TIME

ITR NUMBER

DISCIPLINE

SHEET NO

P. 001 ITR-EL-0009

ITR-EL-0009

ELEC

1 OF 1

Item/Tag NO.

Type :-

Core:

Size:

NO.	Description of check	RESULT		
		ACCEPT	REJECT	N/A.
1	Check cable glands are correct type and size as per cable schedule.	✓		
2	Check there are no damages to cores, termination chamber layout is satisfactory, core identification is correct, crimped and pins satisfactory.	✓		
3	Check cable tag is done correctly.	✓		
4	Test and confirm conductor, phase continuity.	✓		
5	Check insulation resistance test (megger) is completed *I	✓		
6	Check Hi-pot test is completed, only for MV/HV cables *II			✓
7	Connect all cores at both ends and confirm all connections are correct as per termination diagram.	✓		
8	Confirm spare cores, screens are earthed and conform to design drawings/specifications			✓
9	Check enclosure cover is installed, no damages and no bolts are missing	✓		
10	Calibration test certificate of testing equipment to be checked.	✓		

Remarks :

	PETROJET	ENPPI	PMC
NAME			
SIGNATURE			
DATE			

ITR-EL-0009

**Enppi****EGPC CRUDE OIL TANK FARM**

Owner : - Egyptian General Petroleum Corporation (EGPC)

Project No: 01251-100-030
:01251-100-031

Contractor CONSORTIUM (ENPPI / PETROJET)

Document No: ITR-QC-0001
Revision No. : 00**REQUEST FOR INSPECTION**

ACTIVITY : CABLE TERMINATION AND TEST

NOTIFICATION NO. : PTJ-ELE-RFI-230 DISCIPLINE : ELEC

DATE : 28/06/2021

NO.	DESCRIPTION	LOCATION	DATE / TIME	INSPECTION			REMARKS
				PETROJET	ENPPI	PMC	
18	H-030-PM-06B	SUBSTAION					
19	C1-030-PM-06B	SUBSTAION					
20	C3-030-PM-06B	SUBSTAION					
21	H-030-PM-06C	SUBSTAION					
22	C1-030-PM-06C	SUBSTAION					
23	C3-030-PM-06C	SUBSTAION					
24	H-030-PM-06D	SUBSTAION					
25	C1-030-PM-06D	SUBSTAION					
26	C3-030-PM-06D	SUBSTAION					
27	M-030-PM-03A	SUBSTAION					
28	C1-030-PM-03A	SUBSTAION					
29	C3-030-PM-03A	SUBSTAION					
30	M-030-PM-03B	SUBSTAION					
31	C1-030-PM-03B	SUBSTAION					
32	C3-030-PM-03B	SUBSTAION					
33	P-030-T10-CPTR	SUBSTAION	✓				
34	P-AG030-TR-001	SUBSTAION	✓				
35	P-AG030-TR-006	SUBSTAION	✓				

NOTE:

Inspection result : A - Approved B - Reject C - Approved with Comment

	PETROJET	ENPPI	PMC
NAME :			
SIGNATURE			
DATE			

ITR-QC-0001



EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE TERMINATION AND SPLICING

SYSTEM NO.:

INSPECTION REPORT NUMBER

INSPECTION DATE & TIME

ITR NUMBER

DISCIPLINE

SHEET NO

PTJ-ELE-RFI- 230

03/07/2021

ITR-EL-0009

ELEC

1 OF 1

Item/Tag NO.

For All Cables tags in PTJ-ELE-RFI-

Type :-

Core:

Size:

NO.	Description of check	RESULT		
		ACCEPT	REJECT	N/A.
1	Check cable glands are correct type and size as per cable schedule.	✓		
2	Check there are no damages to cores, termination chamber layout is satisfactory, core identification is correct, crimped and pins satisfactory.	✓		
3	Check cable tag is done correctly.	✓		
4	Test and confirm conductor, phase continuity.	✓		
5	Check insulation resistance test (megger) is completed *I	✓		
6	Check Hi-pot test is completed, only for MV/HV cables *II			✓
7	Connect all cores at both ends and confirm all connections are correct as per termination diagram.	✓		
8	Confirm spare cores, screens are earthed and conform to design drawings/specifications	✓		
9	Check enclosure cover is installed, no damages and no bolts are missing	✓		
10	Calibration test certificate of testing equipment to be checked.	✓		

Remarks :

*I : ITR-EL-006A/B

*II : ITR-EL-008

	PETROJET	ENPPI	PMC
NAME			
SIGNATURE			
DATE			

ITR-EL-0009

**Enppi**

EGPC CRUDE OIL TANK FARM



Owner: Egyptian General Petroleum Corporation (EGPC)

Project No: 01251-100-030
:01251-100-031

Contractor: CONSORTIUM (ENPPI / PETROJET)

Document No: ITR-QC-0001
Revision No.: 00**REQUEST FOR INSPECTION**

ACTIVITY: CABLE TERMINATION AND TEST

NOTIFICATION NO.: PTJ-ELE-RFI-214 DISCIPLINE: ELEC

DATE: 13/06/2021

NO.	DESCRIPTION	LOCATION	DATE / TIME	INSPECTION			REMARKS
				PETROJET	ENPPI	PMC	
18	M-030-MXM-04E	FIELD					
19	C1-030-MXM-04E	FIELD					
20	C3-030-MXM-04E	FIELD					
21	M-030-MXM-04F, JB	FIELD					
22	M-030-MXM-04F	FIELD					
23	C1-030-MXM-04F	FIELD					
24	C3-030-MXM-04F	FIELD					
25	P-030-SW-004	FIELD					
26	P-030-LI-004C	FIELD					
27	P1-030-EPM4-CR-1	FIELD					
28	L1-030-EPM4-FT	FIELD					
29	L2-030-EPM4-FT	FIELD					
30	L3-030-EPM4-FT	FIELD					
31	N1-030-EPM4-LTG	FIELD					
32	E1-030-EPM4-LTG	FIELD					
33	E2-030-EPM4-LTG	FIELD					
34	P-AG030-TR-003	FIELD					
35	P-030-T04-CPTR	FIELD					

NOTE: P-030-SOV-104

Inspection result: A - Approved B - Reject C - Approved with Comment

	PETROJET	ENPPI	PMC
NAME:			
SIGNATURE			
DATE			

ITR-QC-0001



EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE TERMINATION AND SPLICING

INSPECTION REPORT NUMBER

INSPECTION DATE & TIME

ITR NUMBER

SYSTEM NO

DISPLINE

SHEET NO

PTJ-ELE-RFI- 214

13/06/2021

ITR-EL-0009

ELEC

1 OF 1

Item/Tag NO.

For All Cables tags in PTJ-ELE-RFI.

Type :-

Core:

Size:

NO.	Description of check	RESUNT		
		ACCEPT	REJECT	N/A.
1	Check cable glands are correct type and size as per cable schedule.	✓		
2	Check there are no damages to cores, termination chamber layout is satisfactory, core identification is correct, crimped and pins satisfactory.	✓		
3	Check cable tag is done correctly.		✓	
4	Test and confirm conductor, phase continuity.	✓		
5	Check insulation resistance test (megger) is completed *I	✓		
6	Check Hi-pot test is completed, only for MV/HV cables *II			✓
7	Connect all cores at both ends and confirm all connections are correct as per termination diagram.	✓		
8	Confirm spare cores, screens are earthed and conform to design drawings/specifications	✓		
9	Check enclosure cover is installed, no damages and no bolts are missing	✓		
10	Calibration test certificate of testing equipment to be checked.			✓

Remarks :

*I : ITR-EL-006A/B

*II : ITR-EL-008

	PETROJET	ENRPI	PMC
NAME			
SIGNATURE			
DATE			

ITR-EL-0009

**Enppi**

EGPC CRUDE OIL TANK FARM



Owner : Egyptian General Petroleum Corporation (EGPC)

Project No: 01251-100-030
:01251-100-031

Contractor CONSORTIUM (ENPPI / PETROJET)

Document No: ITR-QC-0001
Revision No. : 00**REQUEST FOR INSPECTION**

ACTIVITY : CABLE TERMINATION AND TEST

NOTIFICATION NO. : PTJ-ELE-RFI- 232 DISCIPLINE : ELEC

DATE : 03/07/2021

NO.	DESCRIPTION	LOCATION	DATE / TIME	INSPECTION			REMARKS
				PETROJET	ENPPI	PMC	
1	P-AG030-TR-002	FIELD					
2	P1-030-EPM2-CR-1	FIELD					
3	L1-030-EPM2-FT	FIELD					
4	L2-030-EPM2-FT	FIELD					
5	L3-030-EPM2-FT	FIELD					
6	N1-030-EPM2-LTG	FIELD					
7	E1-030-EPM2-LTG	FIELD					
8	E2-030-EPM2-LTG	FIELD					
9	M-030-MXM-02A, JB	FIELD					
10	M-030-MXM-02A	FIELD					
11	C1-030-MXM-02A	FIELD					
12	C3-030-MXM-02A	FIELD					
13	M-030-MXM-02B, JB	FIELD					
14	M-030-MXM-02B	FIELD					
15	C1-030-MXM-02B	FIELD					
16	C3-030-MXM-02B	FIELD					
17	M-030-MXM-02C, JB	FIELD					

NOTE:

Inspection result : A - Approved B - Reject C - Approved with Comment

	PETROJET	ENPPI	PMC
NAME :			
SIGNATURE			
DATE			

ITR-QC-0001

**Enppi****EGPC CRUDE OIL TANK FARM**Owner : **Egyptian General Petroleum Corporation (EGPC)**Project No: 01251-100-030
:01251-100-031Contractor **CONSORTIUM (ENPPI / PETROJET)**Document No: ITR-QC-0001
Revision No. : 00**REQUEST FOR INSPECTION**ACTIVITY : **CABLE TERMINATION AND TEST**NOTIFICATION NO. : **PTJ-ELE-RFI- 232** DISCIPLINE : **ELEC**DATE : **03/07/2021**

NO.	DESCRIPTION	LOCATION	DATE / TIME	INSPECTION			REMARKS
				PETROJET	ENPPI	PMC	
18	M-030-MXM-02C	FIELD					
19	C1-030-MXM-02C	FIELD					
20	C3-030-MXM-02C	FIELD					
21	M-030-MXM-02D, JB	FIELD					
22	M-030-MXM-02D	FIELD					
23	C1-030-MXM-02D	FIELD					
24	C3-030-MXM-02D	FIELD					
25	M-030-MXM-02E, JB	FIELD					
26	M-030-MXM-02E	FIELD					
27	C1-030-MXM-02E	FIELD					
28	C3-030-MXM-02E	FIELD					
29	M-030-MXM-02F, JB	FIELD					
30	M-030-MXM-02F	FIELD					
31	C1-030-MXM-02F	FIELD					
32	C3-030-MXM-02F	FIELD					
33	P-030-T02-CPTR	FIELD					
34	P-030-SDV-102	FIELD					
35	P-030-SW-002	FIELD					
36	P-030-LI-002C	FIELD					

NOTE:

Inspection result : A - Approved B - Reject C - Approved with Comment

	PETROJET	ENPPI	PMC
NAME :			
SIGNATURE			
DATE			

ITR-QC-0001



EGPC CRUDE OIL TANK FARM



INSPECTION AND TEST REPORT FOR

CABLE TERMINATION AND SPLICING

SYSTEM NO.

INSPECTION REPORT NUMBER

INSPECTION DATE & TIME

ITR NUMBER

DISPLINE

SHEET NO

PTJ-ELE-RFI- 232

14/06/2021

ITR-EL-0009

ELEC

1 OF 1

Item/Tag NO.

For All Cables tages in PTJ-ELE-RFI-

Type :-

Core:

Size:

NO.	Description of check	RESUNT		
		ACCEPT	REJECT	N/A.
1	Check cable glands are correct type and size as per cable schedule.	✓		
2	Check there are no damages to cores, termination chamber layout is satisfactory, core identification is correct, crimped and pins satisfactory.	✓		
3	Check cable tag is done correctly.			
4	Test and confirm conductor, phase continuity.	✓		
5	Check insulation resistance test (megger) is completed *'	✓		
6	Check Hi-pot test is completed, only for MV/HV cables *''			✓
7	Connect all cores at both ends and confirm all connections are correct as per termination diagram.	✓		
8	Confirm spare cores, screens are earthed and conform to design drawings/specifications	✓		
9	Check enclosure cover is installed , no damages and no bolts are missing	✓		
10	Calibration test certificate of testing equipment to be checked.			✓

Remarks :

*': ITR-EL-006A/B

*'' : ITR-EL-008

	PETROJET	ENPPI	PMC
NAME :			
SIGNATURE			
DATE			

ITR-EL-0009



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

12.08- FAT Reports & Certificates



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

12.09- SAT Reports & Certificates


PLANT PIPING CATHODIC PROTECTION SYSTEM PRE-COMMISSIONING AS-FOUND POTENTIALS AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC


corrpro
an AEGION company

S.No.	Test Station ID	Pipe As-Found Potential (mV) with portable RE	Pipe As-Found Potential (-mV) with permanent RE	Magnesium Open Circuit Potential (-mV)	Magnesium Current (A)	Continuity between pipe cable 1 and pipe cable 2 (ohms)	Coupon (-mV)		AC Potential (V)	Portable RE to Permanent RE (mV)	Reed Switch Functioning (Yes/No)	Remarks
							On	Off				
1	TS-1	462	459	-	-	0.1	461	624	0	3.3	Yes	
2	TS-2	459	463	-	-	0.1	458	510	0	3	Yes	
3	TS-3	445	715	1573	0.065	0.2	443	375	0	276.9	Yes	Concreted Area
4	TS-4	446	526	1566	0.019	0.1	446	461	0	79.9	Yes	Concreted Area
5	TS-5	431	396	-	-	0.5	431	594	0	33.4	Yes	Concreted Area
6	TS-6	485	465	-	-	0.1	486	496	0	21.3	Yes	
7	TS-7	491	456	-	-	0.1	494	596	0	33	Yes	
8	TS-8	485	678	1556	0.073	0.3	482	630	0	193.9	Yes	
9	TS-9	469	454	-	-	0.2	469	623	0	15.6	Yes	
10	TS-10	733	547	1601	0.012	0.3	732	571	0	176	Yes	
11	TS-11	649	572	1583	0.028	0.1	643	512	0	72.2	Yes	
12	TS-12	504	511	-	-	0.1	504	464	0	6.9	Yes	
13	TS-13	510	457	-	-	0.1	510	475	0	11.5	Yes	
14	TS-14	586	808	1530	0.02	0.4	584	428	0	225.6	Yes	
15	TS-15	475	427	-	-	0.1	475	388	0	41.9	Yes	
16	TS-16	491	498	1499	0.028	0.1	490	514	0	8.6	Yes	anode cable was not connected
17	TS-17	474	355	-	-	0.1	474	549	0	119.6	Yes	
18	TS-18	975	713	1609	0.04	0.1	975	885	0	257.7	Yes	
19	TS-19	486	486	-	-	0.1	486	590	0	0.6	Yes	
20	TS-20	477	481	1559	0.064	0.1	476	575	0	4.3	Yes	anode cable was not connected
21	TS-21	504	506	-	-	0.1	504	470	0	1.6	Yes	
22	TS-22	435	350	-	-	0.1	435	446	0.022	28.7	Yes	
23	TS-23	448	451	-	-	0.1	448	641	0.021	2.4	Yes	
24	TS-24	466	474	-	-	0.1	466	614	0	9.9	Yes	
25	TS-25	471	445	-	-	0.1	464	495	0.022	29.1	Yes	
26	TS-26	455	451	-	-	0.1	455	581	0.021	2.4	Yes	
27	TS-27	437	372	1551	0.046	0.1	437	418	0.026	44	Yes	anode cable was not connected
28	TS-28	446	331	-	-	0.1	446	425	0.021	51.3	Yes	
29	TS-29	450	358	-	-	0.1	448	546	0	20.8	Yes	
30	TS-30	469	488	-	-	0.1	469	475	0	18.4	Yes	
31	TS-31	465	473	-	-	2400000	465	322	0	8.5	Yes	
32	TS-32	435	389	1362	0.028	0.1	435	450	0	25.8	Yes	
33	TS-33	470	453	-	-	0.1	470	461	0	14.6	Yes	
34	TS-34	474	487	-	-	0.1	473	581	0	13.1	Yes	
35	TS-35	501	421	-	-	0.6	502	453	0	33.7	Yes	TP terminated outside of bund wall
36	TS-36	406	557	1507	0.011	0.5	407	260	0	150.1	Yes	TP terminated outside of bund wall
37	TS-37	476	465	-	-	0.4	476	528	0.024	5.1	Yes	
38	TS-38	465	430	1549	0.015	0.4	465	546	0	33.4	Yes	
39	TS-39	472	469	-	-	0.4	472	510	0	2.6	Yes	
40	TS-40	474	464	-	-	0.2	471	422	0.024	7.2	Yes	

For Corrpro

Signature: 
Name: Amr Jowaid
Date: 23/11/2021

For ENPPI

Signature: 
Name: Mohamed Mohamed
Date: 23/11/2021

For PPC

Signature: 
Name: Mohamed Ibrahim
Date: 

PLANT PIPING CATHODIC PROTECTION SYSTEM PRE-COMMISSIONING AS-FOUND POTENTIALS AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC

corrpro
an AEGION company

S.No.	Test Station ID	Pipe As-Found Potential (-mV) with portable RE	Pipe As-Found Potential (-mV) with permanent RE	Magnesium Open Circuit Potential (-mV)	Magnesium Current (A)	Continuity between pipe cable 1 and pipe cable 2 (ohms)	Coupon (-mV)		AC Potential (V)	Portable RE to Permanent RE (mV)	Reed Switch Functioning (Yes/No)	Remarks
							On	Off				
41	TS-41	475	430	-	-	0.1	473	433	0.024	41.5	Yes	
42	TS-42	608	618	1593	0.041	0.2	606	459	0	10.4	Yes	
43	TS-43	389	545	1568	0.016	0.1	385	285	0	160.8	Yes	
44	TS-44	466	481	-	-	0.2	466	368	0	15	Yes	
45	TS-45	465	475	-	-	0.1	465	422	0	9.8	Yes	
46	TS-46	476	481	-	-	0.3	473	362	0	6.2	Yes	
47	TS-47	461	471	-	-	0.1	461	436	0	10.1	Yes	
48	TS-48	528	761	1526	0.016	0.1	527	427	0	249	Yes	
49	TS-49	481	476	-	-	0.1	485	471	0	5.7	Yes	
50	TS-50	469	468	-	-	0.1	468	443	0	0.4	Yes	
51	TS-51	469	418	-	-	0.2	468	412	0	27.5	Yes	
52	TS-52	463	458	-	-	0.3	465	476	0	2.4	Yes	
53	TS-53	483	493	-	-	0.1	484	594	0	9.8	Yes	
54	TS-54	722	1186	1580	0.016	0.2	722	633	0	466.9	Yes	
55	TS-55	492	286	-	-	0.1	492	506	0	40.8	Yes	TP terminated outside of bund wall
56	TS-56	496	421	-	-	0.4	496	409	0	64	Yes	TP terminated outside of bund wall
57	TS-57	497	477	-	-	0.3	497	428	0	15.6	Yes	TP terminated outside of bund wall
58	TS-58	582	512	1533	0.002	0.3	582	389	0	0.7	Yes	TP terminated outside of bund wall
59	TS-59	465	417	-	-	0.1	464	503	0	43.6	Yes	
60	TS-60	569	579	-	-	0.6	569	548	0	9.6	Yes	TP terminated outside of bund wall
61	TS-61	501	522	-	-	0.2	501	920	0	21.4	Yes	TP terminated outside of bund wall
62	TS-62	465	448	-	-	0.1	465	519	0	16.1	Yes	
63	TS-63	507	537	-	-	0.5	507	476	0	24.8	Yes	TP terminated outside of bund wall
64	TS-64	412	438	-	-	0.1	412	335	0.021	27.3	Yes	
65	TS-65	408	563	1616	0.036	14.6	408	434	0	243.8	Yes	TP terminated outside of bund wall
66	TS-66	399	183	-	-	0.3	398	474	0	214.7	Yes	TP terminated outside of bund wall

For Corrpro

Signature- 
Name- Amr Jassid
Date- 23/11/2021

For ENPPI

Signature- 
Name- Mohamed Mohsen
Date- 23/11/2021

For PPC

Signature- 
Name- 
Date- 

PLANT PIPING CATHODIC PROTECTION SYSTEM PRE-COMMISSIONING DEPOLARIZED POTENTIALS AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC


corrpro
an AEGION company

S.No.	Test Station ID	Pipe Depolarized Potential (-mV) with portable RE	Pipe Depolarized Potential (-mV) with permanent RE	Magnesium Open Circuit Potential (-mV)	Coupon (-mV)	AC Potentail (V)	Portable RE to Permanent RE (mV)	Remarks
1	TS-1	429	427	-	429	0	1.8	
2	TS-2	427	432	-	427	0	5.3	
3	TS-3	352	354	-	200	0	10.8	
4	TS-4	310	364	1556	310	0	55.7	
5	TS-5	425	391	1528	426	0	33	
6	TS-6	442	433	-	442	0	10.8	
7	TS-7	461	425	1564	461	0	36	
8	TS-8	323	307	1590	322	0	16	
9	TS-9	435	419	-	435	0	14.2	
10	TS-10	431	412	-	205	0	22.4	
11	TS-11	467	457	1527	341	0	3.5	
12	TS-12	472	480	-	414	0	7.4	
13	TS-13	512	456	-	439	0	10.9	
14	TS-14	486	498	1553	488	0	9.3	
15	TS-15	452	405	-	245	0	39.9	
16	TS-16	460	470	1491	460	0	19.1	
17	TS-17	447	316	-	447	0	132	
18	TS-18	421	420	1558	421	0	1	
19	TS-19	432	440	-	432	0	3.7	
20	TS-20	446	451	1557	447	0	5.2	
21	TS-21	474	476	-	362	0	2.1	
22	TS-22	422	336	-	422	0	26.4	
23	TS-23	430	434	-	430	0	5	
24	TS-24	430	438	-	429	0	11.6	
25	TS-25	450	414	-	451	0	35.8	
26	TS-26	443	434	-	422	0	9.5	
27	TS-27	423	357	1549	344	0	42	
28	TS-28	431	316	-	346	0	48	
29	TS-29	434	351	-	434	0	18	
30	TS-30	452	464	-	452	0	12.6	
31	TS-31	444	449	-	444	0	4.9	
32	TS-32	423	376	1378	248	0	27.4	
33	TS-33	448	437	-	448	0	8.4	
34	TS-34	447	456	-	447	0	9.1	
35	TS-35	511	428	-	511	0	34.3	
36	TS-36	398	409	1502	351	0	10.9	

For Corrpro

Signature- 
Name- Ahmed Jawaid
Date- 23/11/2021

For ENPPI

Signature- 
Name- Mohamed Hekson
Date- 23/11/2021

For PPC

Signature- 
Name-
Date- 


PLANT PIPING CATHODIC PROTECTION SYSTEM PRE-COMMISSIONING DEPOLARIZED POTENTIALS AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC




S.No.	Test Station ID	Pipe Depolarized Potential (-mV) with portable RE	Pipe Depolarized Potential (-mV) with permanent RE	Magnesium Open Circuit Potential (-mV)	Coupon (-mV)	AC Potentail (V)	Portable RE to Permanent RE (mV)	Remarks
37	TS-37	439	439	-	438	0	0.4	
38	TS-38	440	437	1542	440	0	3.1	
39	TS-39	448	443	-	448	0	4	
40	TS-40	451	440	-	240	0	8.8	
41	TS-41	450	401	-	438	0	50.6	
42	TS-42	444	443	1568	444	0	1.9	
43	TS-43	378	330	1513	340	0	43.9	
44	TS-44	441	452	-	441	0	11	
45	TS-45	443	445	-	443	0	3.9	
46	TS-46	453	450	-	343	0	0.8	
47	TS-47	430	442	-	381	0	11.3	
48	TS-48	428	378	1508	324	0	30.2	
49	TS-49	448	446	-	448	0	3	
50	TS-50	433	436	-	432	0	3.9	
51	TS-51	434	390	-	434	0	23.1	
52	TS-52	426	423	-	426	0	1.9	
53	TS-53	454	466	-	454	0	11.2	
54	TS-54	557	555	1566	557	0	1	
55	TS-55	502	293	-	250	0	34.7	
56	TS-56	518	432	-	348	0	76	
57	TS-57	517	482	-	394	0	24.6	
58	TS-58	628	514	1534	628	0	55.5	
59	TS-59	422	381	-	300	0	35.1	
60	TS-60	613	607	-	613	0	5.7	
61	TS-61	510	528	-	510	0	18	
62	TS-62	442	418	-	442	0	23.6	
63	TS-63	522	541	-	522	0	18.3	
64	TS-64	396	421	-	297	0	25.8	
65	TS-65	384	401	1552	384	0	23	
66	TS-66	387	186	-	387	0	200	

For Corrpro

Signature- 
Name- Ahmed Jawaid
Date- 23/11/2021

For ENPPI

Signature- 
Name- Mohamed Hishon
Date- 23/11/2021

For PPC

Signature- 
Name- Mohamed Z. Ibrahim
Date-


PLANT PIPING CATHODIC PROTECTION SYSTEM PRE-COMMISSIONING JUNCTION BOXES AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC

corrpro
an AEGION company

S.No.	Junction Box ID	Visual inspection of all installed equipment for any physical flaws/damage	Ensure all variable resistors within the junction box are set to minimum	Continuity of main header cable to recipient box	Check cables terminated correctly and internal components continuous	Remarks
1	AG030-AJB-001	Pass	Pass	0.1 ohms	Yes	
2	AG030-AJB-002	Pass	Pass	0.1 ohms	Yes	
3	AG030-AJB-003	Pass	Pass	0.1 ohms	Yes	
4	AG030-AJB-004	Pass	Pass	0.1 ohms	Yes	
5	AG030-AJB-005	Pass	Pass	0.1 ohms	Yes	
6	AG030-AJB-006	Pass	Pass	0.1 ohms	Yes	
7	AG030-NJB-001	Pass	Pass	0.1 ohms	Yes	
8	AG030-NJB-002	Pass	Pass	0.1 ohms	Yes	
9	AG030-NJB-003	Pass	Pass	0.1 ohms	Yes	
10	AG030-NJB-004	Pass	Pass	0.1 ohms	Yes	
11	AG030-NJB-005	Pass	Pass	0.1 ohms	Yes	
12	AG030-NJB-006	Pass	Pass	0.1 ohms	Yes	
13	AG030-SJB-001	Pass	Pass	Not Verified	Yes	
14	AG030-SJB-002	Pass	Pass	Not Verified	Yes	
15	AG030-SJB-003	Pass	Pass	Not Verified	Yes	
16	AG030-SJB-004	Pass	Pass	Not Verified	Yes	
17	AG030-SJB-005	Pass	Pass	Not Verified	Yes	
18	AG030-SJB-006	Pass	Pass	Not Verified	Yes	
19	AG030-SJB-007	Pass	Pass	Not Verified	Yes	
20	AG030-SJB-008	Pass	Pass	Not Verified	Yes	
21	AG030-SJB-009	Pass	Pass	Not Verified	Yes	
22	AG030-SJB-010	Pass	Pass	Not Verified	Yes	
23	AG030-SJB-011	Pass	Pass	Not Verified	Yes	
24	AG030-SJB-012	Pass	Pass	Not Verified	Yes	
25	AG030-SJB-013	Pass	Pass	Not Verified	Yes	
26	AG030-SJB-014	Pass	Pass	Not Verified	Yes	
27	AG030-SJB-015	Pass	Pass	Not Verified	Yes	
28	AG030-SJB-016	Pass	Pass	Not Verified	Yes	
29	AG030-SJB-017	Pass	Pass	Not Verified	Yes	
30	AG030-SJB-018	Pass	Pass	Not Verified	Yes	
31	AG030-SJB-019	Pass	Pass	Not Verified	Yes	
32	AG030-SJB-020	Pass	Pass	Not Verified	Yes	
33	AG030-SJB-021	Pass	Pass	Not Verified	Yes	
34	AG030-SJB-022	Pass	Pass	Not Verified	Yes	
35	AG030-SJB-023	Pass	Pass	Not Verified	Yes	
36	AG030-SJB-024	Pass	Pass	Not Verified	Yes	

For Corrpro

Signature- 
Name- Ahmed Jassid
Date- 23/11/2021

For ENPPI

Signature- 
Name- Mohamed Hassen
Date- 23/11/2021

For PPC

Signature- 
Name-
Date-


PLANT PIPING CATHODIC PROTECTION SYSTEM PRE-COMMISSIONING TRANSFORMER RECTIFIER AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC



S.No.	Description	TR Unit	TR Unit	TR Unit	TR Unit	TR Unit	TR Unit	Remarks
PRIOR TO START-UP								
1	Transformer Rectifier ID	AG030-TR-001	AG030-TR-002	AG030-TR-003	AG030-TR-004	AG030-TR-005	AG030-TR-006	
2	Serial Number	H0375A1-4	H0375A1-11	H0375A1-12	H0375A1-13	H0375A1-14	H0375A1-15	
3	Correct Label Plate	Yes	Yes	Yes	Yes	Yes	Yes	
4	Correct Cable Terminations	Yes	Yes	Yes	Yes	Yes	Yes	
5	Correct Cable Tagging	Yes	Yes	Yes	Yes	Yes	Yes	
6	Correct AC Supply	Yes	Yes	Yes	Yes	Yes	Yes	
7	Sunshade	Yes	Yes	Yes	Yes	Yes	Yes	
8	Silica Gel	Yes	Yes	Yes	Yes	Yes	Yes	
9	Dial Type Thermometer	Yes	Yes	Yes	Yes	Yes	Yes	
10	Oil Level Check	Yes	Yes	Yes	Yes	Yes	Yes	
11	Earthing	Yes	Yes	Yes	Yes	Yes	Yes	
12	O&M Manual	Yes	Yes	Yes	Yes	Yes	Yes	
13	Isolator Switch Mismatch	No	No	No	No	No	No	
14	All Electrical Fuses Check	Yes	Yes	Yes	Yes	Yes	Yes	

START-UP / ENERGISE								
1	Energise - Correct AC Supply	Yes	Yes	Yes	Yes	Yes	Yes	
2	Energise - Signs of Distress - Small Output	No	No	No	No	No	No	
3	Energise - Signs of Distress - 10% Output	No	No	No	No	No	No	
4	Energise - Signs of Distress - 100% Output	No	No	No	No	No	No	
5	Accuracy of Panel Meter = Analogue Meter	Yes	Yes	Yes	Yes	Yes	Yes	
6	Accuracy of Panel Meter = Multimeter	Yes	Yes	Yes	Yes	Yes	Yes	

For Corrpro Signature- Name- Amr Jowaid Date- 23/11/2021	For ENPPI Signature- Name- Mohamed Heksen Date- 23/11/2021	For PPC Signature- Name- Mohamed Ibrahim Date-
--	--	--

PLANT PIPING CATHODIC PROTECTION SYSTEM COMMISSIONING POTENTIALS AFTER ENERGISATION AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC

corrpro[®]
an AEGION company

S.No.	Test Station ID	Piping Polarized Potential with Permanent RE (-mV)			Piping Polarized Potential with Portable RE (-mV)			Coupon (-mV)						Remarks
		After 24 hours	After 48 hours	After 72 hours	After 24 hours	After 48 hours	After 72 hours	ON			OFF			
								After 24 hours	After 48 hours	After 72 hours	After 24 hours	After 48 hours	After 72 hours	
1	TS-1	2308	2308	2295	2306	2300	2282	2307	2307	2294	1003	1030	1089	
2	TS-2	2263	2257	2242	2251	2246	2223	2261	2257	2241	1333	1523	1530	
3	TS-3	453	462	473	454	455	462	452	462	472	396	408	418	
4	TS-4	401	417	400	429	429	414	400	416	400	516	538	537	
5	TS-5	479	474	509	481	483	480	478	471	509	548	522	574	
6	TS-6	2247	2263	2235	2247	2239	2210	2245	2261	2234	1126	1219	1268	
7	TS-7	2247	2234	2227	2146	2139	2114	2244	2234	2226	1092	1070	1039	
8	TS-8	386	396	387	368	369	369	386	396	387	668	673	665	
9	TS-9	2239	2221	2208	2192	2181	2169	2235	2219	2207	1203	1217	1249	
10	TS-10	1842	1414	1234	1788	1360	1194	1842	1412	1231	905	908	809	
11	TS-11	2330	2363	2310	2341	2341	2317	2326	2321	2311	1072	-	1059	
12	TS-12	2335	2330	2315	2355	2350	2334	2334	2330	2311	1122	1129	1168	
13	TS-13	1735	1474	1341	1493	1247	1131	1732	1473	1341	883	863	848	
14	TS-14	2280	2191	2122	2265	2052	1990	2280	2189	2121	1150	1257	1299	Reed Switch removed
15	TS-15	2265	2210	2135	2205	2132	2062	2263	2210	2132	1151	1290	1273	
16	TS-16	2548	2520	2495	2563	2543	2513	2547	2520	2492	1207	1194	1161	
17	TS-17	2432	2406	2382	2483	2258	2238	2431	2405	2381	1179	1158	1176	
18	TS-18	2405	2377	2358	2409	2377	2363	2402	2374	2356	1066	1082	1079	
19	TS-19	2695	2611	2575	2712	2624	2584	691	2610	2574	-	1152	1285	
20	TS-20	2425	2385	2354	2406	2354	2326	2424	2380	2350	1077	1057	1055	
21	TS-21	2453	2440	2417	2467	2444	2420	2452	2438	2417	1107	1077	1066	
22	TS-22	2430	2418	2403	2072	2046	2032	2428	2417	2402	1177	1240	1263	
23	TS-23	2501	2478	2467	2473	2452	2431	2499	2477	2463	1000	1015	1061	
24	TS-24	2666	2656	2630	2578	2546	2524	2665	2652	2629	1192	1193	1195	
25	TS-25	2446	2433	2401	2442	2415	2395	2445	2432	2400	1204	1131	1228	
26	TS-26	2477	2457	2448	2479	2458	2434	2470	2454	2445	1027	1070	1080	
27	TS-27	2402	2384	2367	2238	2214	2187	2402	2384	2366	1429	1526	1564	Reed Switch removed
28	TS-28	2413	2384	2373	1989	1964	1940	2412	2382	2373	1293	1268	1353	
29	TS-29	2416	2373	2355	2033	1931	1913	2413	2366	2352	1088	1078	1077	
30	TS-30	2425	2420	2408	2425	2424	2402	2419	2419	2405	1334	1195	1027	
31	TS-31	2499	2495	2467	2498	2489	2468	2497	2492	2466	1036	1035	931	
32	TS-32	2394	2355	2353	2250	2231	2219	2388	2355	2350	1014	966	932	
33	TS-33	2295	2294	2286	2268	2266	2257	2292	2293	2284	1620	1488	1372	
34	TS-34	2371	2381	2360	2382	2395	2375	2371	2379	2361	1035	1054	1075	
35	TS-35	2171	2154	2129	1786	1778	1755	2169	2153	2129	1012	967	960	
36	TS-36	665	680	683	896	906	900	660	680	682	225	231	246	
37	TS-37	2457	2463	2440	2441	2440	2423	2453	2462	2434	1215	1791	1771	
38	TS-38	2414	2411	2401	2419	2414	2398	2413	2411	2399	876	795	818	
39	TS-39	2388	2391	2374	2378	2377	2368	2383	2388	2372	1011	1043	993	
40	TS-40	2489	2481	2462	2444	2451	2436	957	2480	2460	-	915	891	Reed Switch removed

Note: Blank OFF readings for coupon are due to reed switch not functioning.

<p>For Corrpro</p> <p>Signature: </p> <p>Name- Ahmed Jawaid</p> <p>Date- 23/11/2021</p>	<p>For ENPPI</p> <p>Signature: </p> <p>Name- Mohamed Hekson</p> <p>Date- 23/11/2021</p>	<p>For PPC</p> <p>Signature: </p> <p>Name- Mohamed Z. Ibrahim</p> <p>Date- </p>
---	---	--

PLANT PIPING CATHODIC PROTECTION SYSTEM COMMISSIONING POTENTIALS AFTER ENERGISATION AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC

corrpro[®]
an AEGION company

S.No.	Test Station ID	Piping Polarized Potential with Permanent RE (-mV)			Piping Polarized Potential with Portable RE (-mV)			Coupon (-mV)						Remarks
		After 24 hours	After 48 hours	After 72 hours	After 24 hours	After 48 hours	After 72 hours	ON			OFF			
								After 24 hours	After 48 hours	After 72 hours	After 24 hours	After 48 hours	After 72 hours	
41	TS-41	2431	2425	2422	2250	2357	2323	2429	2425	2421	915	921	899	
42	TS-42	2432	2415	2364	2445	2446	2424	2429	2413	2363	791	787	741	TP cap broken
43	TS-43	486	481	495	469	469	469	486	481	495	434	432	448	
44	TS-44	2433	2431	2410	2442	2438	2415	325	2431	2400	-	620	506	
45	TS-45	2452	2463	2449	2474	2477	2452	2452	2463	2449	735	766	764	
46	TS-46	2535	2536	2505	2552	2557	2532	2533	2533	2503	1026	985	919	
47	TS-47	2431	2430	2408	2349	2430	2411	2431	2430	2407	1101	1144	1190	
48	TS-48	2388	2374	2362	2254	2243	2215	620	2372	2362	-	769	908	Reed Switch removed
49	TS-49	2344	2341	2315	2349	2347	2317	2344	2341	2314	767	786	798	
50	TS-50	2254	2242	2222	2255	2339	2214	2252	2242	2214	830	855	861	
51	TS-51	2306	2316	2296	2163	2157	2134	2305	2313	2295	1314	1331	1336	
52	TS-52	2254	2252	2232	2219	2216	2189	2253	2252	2231	914	966	843	
53	TS-53	2090	2096	2064	2056	2052	2035	2090	2095	2063	1102	1093	1055	
54	TS-54	2162	2096	2050	2134	2063	2013	2162	2095	2050	1303	1393	1444	
55	TS-55	2392	2352	2316	1683	1682	1636	2391	2354	2313	1135	1320	1243	
56	TS-56	2519	2480	2444	2366	2310	2272	445	2479	2444	-	532	567	
57	TS-57	2516	2491	2455	2425	2387	2345	2516	2491	2455	779	858	840	
58	TS-58	1697	1664	1647	1676	1651	1625	1696	1664	1641	744	543	426	
59	TS-59	2232	2204	2187	2290	2261	2240	2232	2204	2183	1004	1049	1081	Reed Switch removed
60	TS-60	2092	2052	2028	1637	1622	1608	2091	2051	2028	1466	960	928	Reed Switch removed
61	TS-61	2171	2166	2133	2024	2021	1980	2168	2166	2132	1138	1121	1129	
62	TS-62	2347	2303	2352	2321	2311	2319	2347	2332	-	1071	1120	724	
63	TS-63	2166	2158	2149	2238	2208	2202	2167	2157	2146	1688	1630	880	
64	TS-64	2476	2444	2425	2447	2416	2399	2468	2443	2423	813	705	658	
65	TS-65	831	815	820	877	1041	878	-	815	820	580	451	672	Reed Switch removed
66	TS-66	825	817	815	618	610	610	825	817	815	663	719	695	

Note: Blank OFF readings for coupon are due to reed switch not functioning.

For Corrpro Signature-  Name- Amer Jassid Date- 23/11/2021	For ENPPI Signature-  Name- Mohamed Mohsen Date- 23/11/2021	For PPC Signature-  Name- Mohamed Z. Ibrahim Date-
---	--	---

PLANT PIPING CATHODIC PROTECTION SYSTEM COMMISSIONING ON/OFF POTENTIALS AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC



S.No.	Test Station ID	Piping Polarized Potential with Permanent RE (-mV)		Piping Polarized Potential with Portable RE (-mV)		Acceptable Criteria (Between -950mV and 1200mV)	Coupon (-mV)		AC Potential (V)	Remarks
		ON	OFF	ON	OFF		ON	OFF		
1	TS-1	1636	1070	1701	1081	Yes	1698	939	0.105	
2	TS-2	1640	1080	1624	1073	Yes	1610	730	0.148	
3	TS-3	872	613	841	610	No	841	580	0.09	
4	TS-4	831	605	781	530	No	779	524	0.082	
5	TS-5	888	655	816	600	No	811	655	0.072	
6	TS-6	1603	1066	1627	1070	Yes	1622	1079	0.121	
7	TS-7	1546	1056	1665	1099	Yes	1659	936	0.132	
8	TS-8	802	543	827	559	No	824	725	0.072	
9	TS-9	1583	1051	1604	1053	Yes	1601	932	0.152	
10	TS-10	1064	626	1065	667	No	1058	705	0.168	
11	TS-11	1748	1124	1738	1121	Yes	1732	938	0.181	
12	TS-12	1750	1144	1706	1113	Yes	1703	943	0.155	
13	TS-13	1004	695	1158	794	No	1149	698	0.174	
14	TS-14	1182	816	1216	799	No	1215	969	0.191	
15	TS-15	1106	626	1137	672	No	1130	838	0.199	
16	TS-16	1762	1217	1710	1216	No	1710	1169	0.143	
17	TS-17	1555	1063	1715	1194	Yes	1701	1052	0.137	
18	TS-18	1593	1196	1598	1193	Yes	1585	990	0.118	
19	TS-19	1689	1283	1690	1273	No	1687	937	0.124	
20	TS-20	1709	1220	1687	1201	No	1686	1065	0.125	
21	TS-21	1757	1201	1718	1184	Yes	1716	770	0.135	
22	TS-22	1433	880	1726	1099	Yes	1725	1043	0.161	
23	TS-23	1699	1167	1692	1177	Yes	1686	858	0.122	
24	TS-24	1735	1260	1768	1278	No	1760	1062	0.181	
25	TS-25	1688	1158	1682	1172	Yes	1680	1180	0.144	
26	TS-26	1707	1179	1690	1160	Yes	1689	821	0.13	
27	TS-27	1577	1024	1671	1105	Yes	1663	889	0.135	
28	TS-28	1382	858	1705	1104	Yes	1703	705	0.148	
29	TS-29	1409	899	1725	1086	Yes	1720	961	0.127	
30	TS-30	1755	1130	1752	1114	Yes	1752	939	0.144	
31	TS-31	1822	1115	1808	1115	Yes	1802	631	0.173	
32	TS-32	1602	1005	1693	1078	Yes	1688	618	0.132	
33	TS-33	1633	1058	1648	1089	Yes	1639	922	0.16	
34	TS-34	1744	1102	1746	1095	Yes	1742	1036	0.135	
35	TS-35	1274	898	1529	1065	Yes	1527	762	0.105	
36	TS-36	1229	724	1053	721	No	1053	336	0.13	
37	TS-37	1783	1114	1794	1095	Yes	1793	1154	0.156	
38	TS-38	1771	1103	1763	1115	Yes	1748	730	0.144	
39	TS-39	1751	1103	1744	1109	Yes	1744	942	0.157	
40	TS-40	1780	1116	1797	1117	Yes	1788	762	0.105	

For Corrpro

Signature- 
Name- Amr Joudi
Date- 23/11/2021

For ENPPI

Signature- 
Name- Mohamed Mohamed
Date- 23/11/2021

For PPC

Signature- 
Name-
Date-

PLANT PIPING CATHODIC PROTECTION SYSTEM COMMISSIONING ON/OFF POTENTIALS AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC

corrpro
an AEGION company

S.No.	Test Station ID	Piping Polarized Potential with Permanent RE (-mV)		Piping Polarized Potential with Portable RE (-mV)		Acceptable Criteria (Between -950mV and 1200mV)	Coupon (-mV)		AC Potential (V)	Remarks
		ON	OFF	ON	OFF		ON	OFF		
41	TS-41	1696	1045	1747	1105	Yes	1741	815	0.12	
42	TS-42	1721	1077	1717	1070	Yes	1710	806	0.131	
43	TS-43	894	627	953	708	No	962	706	0.129	
44	TS-44	1735	1087	1710	1088	Yes	1709	890	0.159	
45	TS-45	1746	1103	1749	1107	Yes	1743	996	0.169	
46	TS-46	1788	1096	1788	1101	Yes	1770	748	0.217	
47	TS-47	1727	1099	1730	1079	Yes	1729	915	0.182	
48	TS-48	1569	1000	1673	1060	Yes	1671	990	0.089	
49	TS-49	1688	1101	1710	1091	Yes	1699	874	0.088	
50	TS-50	1636	1072	1635	1068	Yes	1632	867	0.148	
51	TS-51	1595	1009	1691	1085	Yes	1690	987	0.146	
52	TS-52	1582	1049	1623	1035	Yes	1614	737	0.135	
53	TS-53	1532	1084	1560	1087	Yes	1559	909	0.077	
54	TS-54	1124	900	1126	896	No	1124	1030	0.105	
55	TS-55	811	547	1201	851	No	1200	771	0.142	
56	TS-56	1220	796	1353	899	No	1349	800	0.186	
57	TS-57	1296	844	1360	899	No	1353	744	0.176	
58	TS-58	980	830	1006	894	No	1002	542	0.042	
59	TS-59	1543	1071	1579	1081	Yes	1568	988	0.103	
60	TS-60	1126	1043	1164	1017	Yes	1163	923	0.069	
61	TS-61	1452	1036	1527	1050	Yes	1521	1167	0.113	
62	TS-62	1640	1002	1729	1116	Yes	1721	614	0.167	
63	TS-63	1601	1085	1532	1067	Yes	1529	1112	0.11	
64	TS-64	1698	1136	1693	1120	Yes	1689	450	0.149	
65	TS-65	1786	1383	1914	1411	No	1914	1320	0.22	
66	TS-66	1740	1169	1963	1449	No	1954	1323	0.227	

For Corrpro

Signature- 
Name- Ahmed Jawaid
Date- 23/11/2021

For ENPPI

Signature- 
Name- Mohamed Hishon
Date- 23/11/2021

For PPC

Signature- 
Name-
Date-
Mohamed Z. Ibrahim

PLANT PIPING CATHODIC PROTECTION SYSTEM COMMISSIONING FINAL ON/OFF POTENTIALS AFTER ADJUSTMENTS AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC


corrpro
an AEGION company

S.No.	Test Station ID	Piping Polarized Potential with Portable RE (-mV)		Acceptable Criteria (Between -950mV and -1200mV)	Remarks
		ON	OFF		
1	TS-1	3590	962	Yes	
2	TS-2	3332	961	Yes	
3	TS-3	2580	870	No	
4	TS-4	2537	796	No	
5	TS-5	2326	895	No	
6	TS-6	3370	956	Yes	
7	TS-7	3443	1038	Yes	
8	TS-8	2680	839	No	
9	TS-9	3303	962	Yes	
10	TS-10	2640	922	No	
11	TS-11	3513	1023	Yes	
12	TS-12	3383	1002	Yes	
13	TS-13	2373	1048	Yes	
14	TS-14	2560	1093	Yes	
15	TS-15	2866	974	Yes	
16	TS-16	3417	1010	Yes	
17	TS-17	3266	1013	Yes	
18	TS-18	3265	1060	Yes	
19	TS-19	3767	1161	Yes	
20	TS-20	3355	1028	Yes	
21	TS-21	3445	1019	Yes	
22	TS-22	3310	969	Yes	
23	TS-23	3560	976	Yes	
24	TS-24	3772	1048	Yes	
25	TS-25	3510	996	Yes	
26	TS-26	3501	969	Yes	
27	TS-27	3475	973	Yes	
28	TS-28	3350	980	Yes	
29	TS-29	3479	972	Yes	
30	TS-30	3366	990	Yes	
31	TS-31	3359	998	Yes	
32	TS-32	3338	959	Yes	
33	TS-33	3062	978	Yes	
34	TS-34	3328	980	Yes	
35	TS-35	2552	1034	Yes	
36	TS-36	2687	950	Yes	
37	TS-37	3362	987	Yes	
38	TS-38	3469	988	Yes	
39	TS-39	3396	999	Yes	
40	TS-40	3493	1008	Yes	

For Corrpro

Signature- 
Name- Amr Jassid
Date- 23/11/2021

For ENPPI

Signature- 
Name- Mohamed Hishon
Date- 23/11/2021

For PPC

Signature- 
Name- Mohamed Z. Ibrahim
Date-


PLANT PIPING CATHODIC PROTECTION SYSTEM COMMISSIONING FINAL ON/OFF POTENTIALS AFTER ADJUSTMENTS AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC


corrpro
an AEGION company

S.No.	Test Station ID	Piping Polarized Potential with Portable RE (-mV)		Acceptable Criteria (Between -950mV and -1200mV)	Remarks
		ON	OFF		
41	TS-41	3338	991	Yes	
42	TS-42	3141	966	Yes	
43	TS-43	2666	900	No	
44	TS-44	3301	969	Yes	
45	TS-45	3302	983	Yes	
46	TS-46	3269	999	Yes	
47	TS-47	3331	963	Yes	
48	TS-48	3239	950	Yes	
49	TS-49	3296	990	Yes	
50	TS-50	3392	974	Yes	
51	TS-51	3570	972	Yes	
52	TS-52	3263	956	Yes	
53	TS-53	2990	1001	Yes	
54	TS-54	2116	1089	Yes	
55	TS-55	2696	965	Yes	
56	TS-56	2708	971	Yes	
57	TS-57	2734	984	Yes	
58	TS-58	2088	1121	Yes	
59	TS-59	3235	960	Yes	
60	TS-60	2568	1132	Yes	
61	TS-61	2563	1040	Yes	
62	TS-62	3411	970	Yes	
63	TS-63	2541	1052	Yes	
64	TS-64	3613	952	Yes	
65	TS-65	3313	1008	Yes	
66	TS-66	3526	999	Yes	

For Corrpro

Signature- 
Name- Amr Jawsaid
Date- 23/11/2021

For ENPPI

Signature- 
Name- Mohamed Hishon
Date- 23/11/2021

For PPC

Signature- 
Name- Mohamed Z. Ibrahim
Date-

PLANT PIPING CATHODIC PROTECTION SYSTEM COMMISSIONING INSULATING FLANGE JOINTS AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC



S.No.	Assigned Insulating Flange Joint ID	Protected Side Potential with Portable RE (-mV)		Unprotected Side Potential with Portable RE (-mV)		Acceptable Criteria: Pass/Fail*	Electrical Continuity across the flange	Acceptable Criteria: Over Limit	Remarks
		ON	OFF	ON	OFF				
Pumps Area									
1	1	2401	960	293	309	Pass	OL	Yes	
2	2	1315	360	850	930	Pass*	OL	Yes	
3	3	2602	940	390	387	Pass	OL	Yes	
4	4	2654	890	416	422	Pass	OL	Yes	
5	5	2699	892	461	435	Pass	OL	Yes	
6	6	2650	931	467	470	Pass	OL	Yes	
7	7	2080	652	180	202	Pass	OL	Yes	
8	8	2376	802	142	136	Pass	OL	Yes	
9	9	2350	803	147	188	Pass	OL	Yes	
10	10	2170	852	413	430	Pass	OL	Yes	
11	11	-	-	-	-	Pass	OL	Yes	No Soil Access
12	12	990	490	165	170	Pass	OL	Yes	
13	13	-	-	-	-	Pass	OL	Yes	No Soil Access
14	14	2620	890	405	420	Pass	OL	Yes	
15	15	2703	961	501	496	Pass	X	-	
16	16	2553	820	335	410	Pass	OL	Yes	
17	17	2557	806	380	385	Pass	OL	Yes	
18	18	1466	300	186	44	Pass*	OL	Yes	
19	19	2630	775	430	352	Pass*	OL	Yes	
20	20	1580	385	128	140	Pass	OL	Yes	
21	21	2689	870	461	447	Pass	OL	Yes	
22	22	-	-	-	-	Pass	OL	Yes	No Soil Access
23	23	-	-	-	-	Pass	OL	Yes	No Soil Access
24	24	2560	874	460	450	Pass	OL	Yes	
25	25	-	-	-	-	Pass	OL	Yes	No Soil Access
26	26	2715	960	549	535	Pass	OL	Yes	
27	27	2360	705	350	330	Pass	OL	Yes	
28	28	2625	835	430	427	Pass	OL	Yes	
29	29	2444	800	409	395	Pass	OL	Yes	
30	30	-	-	-	-	Pass	OL	Yes	No Soil Access
31	31	2550	855	470	450	Pass	OL	Yes	
32	32	2046	850	-	-	Pass	OL	Yes	No Soil Access
33	33	-	-	-	-	Pass	OL	Yes	No Soil Access
34	34	2574	870	450	435	Pass	OL	Yes	
35	35	2695	860	510	398	Pass	OL	Yes	
36	36	2596	800	474	374	Pass	X	-	
37	37	2580	820	450	400	Pass	OL	Yes	
38	38	-	-	-	-	Pass	OL	Yes	No Soil Access
39	39	-	-	-	-	Pass	OL	Yes	No Soil Access
40	40	-	-	-	-	Pass	OL	Yes	No Soil Access
41	41	-	-	-	-	Pass	OL	Yes	No Soil Access
42	42	2635	860	485	454	Pass	OL	Yes	
43	43	-	-	-	-	Pass	OL	Yes	No Soil Access
44	44	2561	790	378	368	Pass	OL	Yes	
45	45	2450	795	450	380	Pass*	OL	Yes	
46	46	-	-	-	-	Pass	OL	Yes	No Soil Access
47	47	-	-	-	-	Pass	OL	Yes	No Soil Access
48	48	-	-	-	-	Pass	OL	Yes	No Soil Access

Pass/Fail Criterion:

ON potentials on both sides of the piping (underground or protected side and aboveground or unprotected side) are different by more than 100mV DC and the potential shift between ON and OFF potentials on the aboveground side is less than 25mV; the isolator is considered effective.

Note:

Poor soil access at insulating flange joint locations

* Swing on unprotected side needs to be further investigated.

X = Disconnected Flange

For Corrpro

Signature-
Name-
Date- 23/11/2021

For ENPPI

Signature-
Name-
Date- 23/11/2021

For PPC

Signature-
Name-
Date-

PLANT PIPING CATHODIC PROTECTION SYSTEM COMMISSIONING INSULATING FLANGE JOINTS AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC



S.No.	Assigned Insulating Flange Joint ID	Protected Side Potential with Portable RE (-mV)		Unprotected Side Potential with Portable RE (-mV)		Acceptable Criteria: Pass/Fail*	Electrical Continuity across the flange	Acceptable Criteria: Over Limit	Remarks
		ON	OFF	ON	OFF				
49	49	-	-	-	-	Pass	OL	Yes	No Soil Access
50	50	-	-	-	-	Pass	OL	Yes	No Soil Access
51	51	-	-	-	-	Pass	OL	Yes	No Soil Access
52	52	-	-	-	-	Pass	OL	Yes	No Soil Access
53	53	-	-	-	-	Pass	OL	Yes	No Soil Access
54	54	-	-	-	-	Pass	OL	Yes	No Soil Access
55	55	-	-	-	-	Pass	OL	Yes	No Soil Access
56	56	2480	879	494	401	Pass*	OL	Yes	
57	57	-	-	-	-	Pass	OL	Yes	No Soil Access
58	58	-	-	-	-	Pass	OL	Yes	No Soil Access
59	59	2511	890	410	400	Pass	OL	Yes	
60	60	2479	821	390	365	Pass	OL	Yes	
61	61	-	-	-	-	Pass	OL	Yes	No Soil Access
62	62	-	-	-	-	Pass	OL	Yes	No Soil Access
63	63	-	-	-	-	Pass	OL	Yes	No Soil Access
64	64	-	-	-	-	Pass	OL	Yes	No Soil Access
65	65	-	-	-	-	Pass	OL	Yes	No Soil Access
66	66	-	-	-	-	Pass	OL	Yes	No Soil Access
67	67	-	-	-	-	Pass	OL	Yes	No Soil Access
68	68	-	-	-	-	Pass	OL	Yes	No Soil Access
69	69	-	-	-	-	Pass	X	Yes	No Soil Access
70	70	2150	800	278	275	Pass	X	Yes	
71	71	2239	951	251	255	Pass	OL	Yes	
72	72	2294	882	192	170	Pass	OL	Yes	
73	73	2237	861	172	160	Pass	X	Yes	
74	74	2240	980	450	438	Pass	OL	Yes	
75	75	3316	651	599	605	Pass	OL	Yes	
Behind Tank Area (FW line)									
76	76	-	-	-	-	Pass	OL	Yes	No Soil Access
77	77	-	-	-	-	Pass	OL	Yes	No Soil Access
78	78	2385	970	271	265	Pass	OL	Yes	
79	79	2578	880	265	262	Pass	OL	Yes	
80	80	2650	889	296	280	Pass	OL	Yes	
81	81	-	-	-	-	Pass	OL	Yes	No Soil Access
Foam Lines									
82	82	2133	908	285	281	Pass	OL	Yes	
83	83	970	980	290	283	Pass	OL	Yes	
84	84	2780	924	262	248	Pass	OL	Yes	
85	85	1828	934	315	325	Pass	OL	Yes	

Pass/Fail Criterion:

ON potentials on both sides of the piping (underground or protected side and aboveground or unprotected side) are different by more than 100mV DC and the potential shift between ON and OFF potentials on the aboveground side is less than 25mV; the isolator is considered effective.


Note:

Poor soil access at insulating flange joint locations


* Swing on unprotected side needs to be further investigated.

X = Disconnected Flange

For Corrpro

Signature: 
Name: Amr Jassal
Date: 23/11/2021

For ENPPI

Signature: 
Name: Mohamed Hosen
Date: 23/11/2021

For PPC

Signature: 
Name: Mohamed Z. Ibrahim
Date: 

PLANT PIPING CATHODIC PROTECTION SYSTEM COMMISSIONING TRANSFORMER RECTIFIER AND JUNCTION BOX READINGS AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC


corrpro
an AEGION company

TRANSFORMER RECTIFIER								
S.No.	Description	TR-001 Readings	TR-002 Readings	TR-003 Readings	TR-004 Readings	TR-005 Readings	TR-006 Readings	Remarks
1	DC Voltage Output (V) - Display	10.0	4.4	3.8	5.4	8.1	7	
2	DC Voltage Output (V) - Measured	10.03	4.397	3.79	5.426	8.11	7.05	
3	DC Current Output at 60A/75mV Shunt (mV) - Display	16.4	2.0	1.5	2.9	8.3	7	
4	DC Current Output at 60A/75mV Shunt (mV) - Measured	16.5	2.1	1.6	3	8.3	7	
5	DC Current Output (A) - Converted from Shunt	13.2	1.68	1.28	2.4	6.64	5.6	
6	Back EMF (V)	1.9	2	1.6	2.3	2.2	1.8	
7	AC Input Voltage (V)	395.9	396.6	395.8	396.1	396.3	395.3	


ANODE JUNCTION BOX								
S.No.	Description	AJB-001 Readings	AJB-002 Readings	AJB-003 Readings	AJB-004 Readings	AJB-005 Readings	AJB-006 Readings	Remarks
1	AJB Current in the Main cable (A) - Measured via Clamp Meter	16.7	2.05	1.48	2.94	8.48	7.14	
2	Shunt reading for Circuit 1 - AJB to ASB (mV) (Shunt = 12A/100mV)	21.6	4.2	3.6	6.3	24.3	18.4	
3	Shunt reading for Circuit 2 - AJB to ASB (mV) (Shunt = 12A/100mV)	29.1	4.1	2.3	6.1	11.1	13.1	
4	Shunt reading for Circuit 3 - AJB to ASB (mV) (Shunt = 12A/100mV)	41.3	4.5	2.9	5.9	17.1	16.4	
5	Shunt reading for Circuit 4 - AJB to ASB (mV) (Shunt = 12A/100mV)	56.8	4	3.5	7	13	11.7	
6	Shunt reading for Circuit 5 - AJB to ASB (mV) (Shunt = 12A/100mV)	-	-	-	-	-	-	
7	Total shunt reading (mV)	148.8	16.8	12.3	25.3	65.5	59.6	
8	Shunt reading converted to Amperes (A)	17.856	2.016	1.476	3.036	7.86	7.152	

NEGATIVE JUNCTION BOX								
S.No.	Description	NJB-001 Readings	NJB-002 Readings	NJB-003 Readings	NJB-004 Readings	NJB-005 Readings	NJB-006 Readings	Remarks
1	NJB Current in the Main cable (A) - Measured via Clamp Meter	17.18	2.1	1.55	3.1	8.62	7.3	
2	Shunt reading for Circuit 1 (mV) (Shunt = 15A/100mV)	6.4	2.5	0.6	6.5	25.6	1 is bonded with 3	
3	Shunt reading for Circuit 2 (mV) (Shunt = 15A/100mV)	2 is bonded with 1	2 is bonded with 3	2 is bonded with 1	5.9	14.1	20.3	
4	Shunt reading for Circuit 3 (mV) (Shunt = 15A/100mV)	105	5.7	4.9	3 is bonded with 1	20.7	14.6	
5	Shunt reading for Circuit 4 (mV) (Shunt = 15A/100mV)	4 is bonded with 3	5.4	4.7	8	25.7	13.7	
6	Total shunt reading (mV)	111.4	13.6	10.2	20.4	86.1	48.6	
7	Shunt reading converted to Amperes (A)	16.71	2.04	1.53	3.06	12.915	7.29	

For Corrpro

Signature- 
Name- Ahmed Jawaid
Date- 23/11/2021

For ENPPI

Signature- 
Name- Mohamed Haddon
Date- 23/11/2021

For PPC

Signature- 
Name- Mohamed Z. Ibrahim
Date- 

PLANT PIPING CATHODIC PROTECTION SYSTEM COMMISSIONING ANODE SPLITTER JUNCTION BOXES READINGS AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC



ANODE SPLITTER BOX														
S.No.	Description	SJB-001		SJB-002		SJB-003		SJB-004		SJB-005		SJB-006		Remarks
		Anode	Result	Anode	Result	Anode	Result	Anode	Result	Anode	Result	Anode	Result	
1	ASB Current in the Main cable (A) - Measured via Clamp Meter	-	2.5	-	3.47	-	3.8	-	6.88	-	0.38	-	0.48	
2	Shunt	5A/100mV												
3	Shunt reading for Circuit 1 - ASB to Anode (mV)	A1	3.6	A11	7.8	A21	6.5	A31	8.7	A41	0.5	A51	2.8	
4	Shunt reading for Circuit 2 - ASB to Anode (mV)	A2	5.8	A12	5.2	A22	6.8	A32	9.6	A42	0.7	A52	3.8	
5	Shunt reading for Circuit 3 - ASB to Anode (mV)	A3	6.4	A13	1.6	A23	5.6	A33	15.8	A43	0.8	A53	0.9	
6	Shunt reading for Circuit 4 - ASB to Anode (mV)	A4	5.2	A14	8.4	A24	9	A34	11.6	A44	0.9	A54	0.5	
7	Shunt reading for Circuit 5 - ASB to Anode (mV)	A5	3.3	A15	1.2	A25	14.6	A35	16.8	A45	0.6	A55	0.8	
8	Shunt reading for Circuit 6 - ASB to Anode (mV)	A6	4.3	A16	25.2	A26	4.3	A36	18.6	A46	1.1	A56	0.4	
9	Shunt reading for Circuit 7 - ASB to Anode (mV)	A7	4.6	A17	3.4	A27	3.8	A37	9.1	A47	0.8	A57	0.0	
10	Shunt reading for Circuit 8 - ASB to Anode (mV)	A8	7.6	A18	0	A28	4.6	A38	16.8	A48	1.6	A58	0	
11	Shunt reading for Circuit 9 - ASB to Anode (mV)	A9	3.6	A19	7.5	A29	7.5	A39	19.8	A49	1.4	A59	0.0	
12	Shunt reading for Circuit 10 - ASB to Anode (mV)	A10	6.1	A20	10	A30	13	A40	8	A50	1.8	A60	0.6	
13	Total shunt reading (mV)	-	50.5	-	70.3	-	75.7	-	134.8	-	10.2	-	9.8	
14	Shunt reading converted to Amperes (A)	-	2.525	-	3.515	-	3.785	-	6.740	-	0.510	-	0.490	

S.No.	Description	SJB-007		SJB-008		SJB-009		SJB-010		SJB-011		SJB-012		Remarks
		Anode	Result	Anode	Result	Anode	Result	Anode	Result	Anode	Result	Anode	Result	
1	ASB Current in the Main cable (A) - Measured via Clamp Meter	-	0.51	-	0.46	-	0.37	-	0.19	-	0.32	-	0.41	
2	Shunt	5A/100mV												
3	Shunt reading for Circuit 1 - ASB to Anode (mV)	A61	0.0	A71	1.1	A81	0.5	A91	0.7	A101	0.1	A111	0.3	
4	Shunt reading for Circuit 2 - ASB to Anode (mV)	A62	1.2	A72	0.6	A82	0.5	A92	0.3	A102	0.9	A112	0.6	
5	Shunt reading for Circuit 3 - ASB to Anode (mV)	A63	3.5	A73	0.9	A83	0.4	A93	0.8	A103	0.7	A113	0.8	
6	Shunt reading for Circuit 4 - ASB to Anode (mV)	A64	1.6	A74	0.7	A84	0.6	A94	0.4	A104	2	A114	1.1	
7	Shunt reading for Circuit 5 - ASB to Anode (mV)	A65	0.0	A75	0.8	A85	1.5	A95	0.2	A105	0.6	A115	0.7	
8	Shunt reading for Circuit 6 - ASB to Anode (mV)	A66	0	A76	1.1	A86	1.7	A96	0.3	A106	0.9	A116	0.6	
9	Shunt reading for Circuit 7 - ASB to Anode (mV)	A67	0.0	A77	1.2	A87	1.6	A97	0.7	A107	1.9	A117	2.6	
10	Shunt reading for Circuit 8 - ASB to Anode (mV)	A68	2.7	A78	1.1	A88	1.3	A98	0.6	A108	0.1	A118	1.2	
11	Shunt reading for Circuit 9 - ASB to Anode (mV)	A69	2.2	A79	1.0	A89	0.2	A99	0.6	A109	0.6	A119	0.6	
12	Shunt reading for Circuit 10 - ASB to Anode (mV)	A70	0	A80	1.2	A90	0.3	A100	0.9	A110	0.1	A120	0	
13	Total shunt reading (mV)	-	11.2	-	9.7	-	8.6	-	5.5	-	7.9	-	8.5	
14	Shunt reading converted to Amperes (A)	-	0.560	-	0.485	-	0.430	-	0.275	-	0.395	-	0.425	

For Corrpro

Signature:
Name: Ahmed Jawaid
Date: 23/11/2021

For ENPPI

Signature:
Name: Mohamed Hekson
Date: 23/11/2021

For PPC

Signature:
Name: Mohamed Z. Ibrahim
Date:

PLANT PIPING CATHODIC PROTECTION SYSTEM COMMISSIONING ANODE SPLITTER JUNCTION BOXES READINGS AT AGROOD 30

Client: ENPPI
Project: New Crude Oil Tank Farm Project
Owner: EGPC

corrpro[®]
an AEGION company


ANODE SPLITTER BOX														
S.No.	Description	SJB-013		SJB-014		SJB-015		SJB-016		SJB-017		SJB-018		Remarks
		Anode	Result	Anode	Result	Anode	Result	Anode	Result	Anode	Result	Anode	Result	
1	ASB Current in the Main cable (A) - Measured via Clamp Meter	-	0.77	-	0.71	-	0.65	-	0.86	-	1.16	-	1.65	
2	Shunt	5A/100mV												
3	Shunt reading for Circuit 1 - ASB to Anode (mV)	A121	1.0	A131	1.4	A141	4.2	A151	2.2	A161	0.0	A171	2.0	
4	Shunt reading for Circuit 2 - ASB to Anode (mV)	A122	0.4	A132	1.3	A142	2.7	A152	0.4	A162	2.4	A172	1.6	
5	Shunt reading for Circuit 3 - ASB to Anode (mV)	A123	0.6	A133	1.2	A143	1.4	A153	4.0	A163	2.0	A173	2.9	
6	Shunt reading for Circuit 4 - ASB to Anode (mV)	A124	2.5	A134	1.2	A144	1	A154	1	A164	3.2	A174	2.8	
7	Shunt reading for Circuit 5 - ASB to Anode (mV)	A125	3.1	A135	1.9	A145	1.1	A155	2.1	A165	1.3	A175	0.0	
8	Shunt reading for Circuit 6 - ASB to Anode (mV)	A126	1.6	A136	1.6	A146	0.9	A156	1.9	A166	1.2	A176	1.9	
9	Shunt reading for Circuit 7 - ASB to Anode (mV)	A127	0.8	A137	1.9	A147	0.5	A157	1.8	A167	2.2	A177	8.9	
10	Shunt reading for Circuit 8 - ASB to Anode (mV)	A128	1.1	A138	0.8	A148	0.8	A158	0.9	A168	2.5	A178	6.4	
11	Shunt reading for Circuit 9 - ASB to Anode (mV)	A129	1.9	A139	2.1	A149	0.4	A159	1.0	A169	3.1	A179	5.8	
12	Shunt reading for Circuit 10 - ASB to Anode (mV)	A130	1.8	A140	1.1	A150	0.8	A160	1.9	A170	2.8	A180	2	
13	Total shunt reading (mV)	-	14.8	-	14.5	-	13.8	-	17.2	-	20.7	-	34.3	
14	Shunt reading converted to Amperes (A)	-	0.740	-	0.725	-	0.690	-	0.860	-	1.035	-	1.715	

S.No.	Description	SJB-019		SJB-020		SJB-021		SJB-022		SJB-023		SJB-024		Remarks
		Anode	Result	Anode	Result	Anode	Result	Anode	Result	Anode	Result	Anode	Result	
1	ASB Current in the Main cable (A) - Measured via Clamp Meter	-	2.59	-	3.17	-	2.13	-	1.51	-	1.98	-	1.4	
2	Shunt	5A/100mV												
3	Shunt reading for Circuit 1 - ASB to Anode (mV)	A181	8.1	A191	3.9	A201	3.1	A211	8.8	A221	2.6	A231	4.3	
4	Shunt reading for Circuit 2 - ASB to Anode (mV)	A182	3	A192	3.3	A202	1.4	A212	2.3	A222	5.4	A232	2.9	
5	Shunt reading for Circuit 3 - ASB to Anode (mV)	A183	3.1	A193	1.1	A203	7.4	A213	8.9	A223	4.7	A233	0.0	
6	Shunt reading for Circuit 4 - ASB to Anode (mV)	A184	6.8	A194	8.3	A204	5.6	A214	0	A224	3.9	A234	2	
7	Shunt reading for Circuit 5 - ASB to Anode (mV)	A185	3.2	A195	2.6	A205	6.9	A215	1.0	A225	3.5	A235	5.2	
8	Shunt reading for Circuit 6 - ASB to Anode (mV)	A186	12.5	A196	6.8	A206	0.1	A216	4.3	A226	6.2	A236	1.7	
9	Shunt reading for Circuit 7 - ASB to Anode (mV)	A187	3.2	A197	9.8	A207	7.2	A217	2.3	A227	1.1	A237	1.1	
10	Shunt reading for Circuit 8 - ASB to Anode (mV)	A188	4.9	A198	7	A208	4.3	A218	1	A228	2.4	A238	4.5	
11	Shunt reading for Circuit 9 - ASB to Anode (mV)	A189	2.2	A199	8.7	A209	4.1	A219	1.2	A229	3.8	A239	4.1	
12	Shunt reading for Circuit 10 - ASB to Anode (mV)	A190	2.9	A200	10.3	A210	4.1	A220	1.7	A230	6.1	A240	1.3	
13	Total shunt reading (mV)	-	49.9	-	61.8	-	44.2	-	31.5	-	39.7	-	27.1	
14	Shunt reading converted to Amperes (A)	-	2.495	-	3.090	-	2.210	-	1.575	-	1.985	-	1.355	

For Corrpro

Signature- 
Name- Amr Jassid
Date- 23/11/2021

For ENPPI

Signature- 
Name- Mohamed Hassan
Date- 23/11/2021

For PPC

Signature- 
Name- Mohamed Zaid
Date- 



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

12.10- Electrical Pre-Commissioning Check Lists

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-030-T01-CPTR




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	Construction punch list to be checked.	✓	
2	Check cables are correctly fixed to trays and supports.	✓	
3	Check cables through walls or ceilings are correctly sealed.	✓	
4	Check that all cables are installed in accordance with cable lists and approved documents.	✓	
5	Check identification tags of all conductors and wires.	✓	
6	Check connection, termination and joints of cables are correctly executed.	✓	
7	Inspect cables for jacket damage.	✓	
8	Ensure that the correct size and type of crimping lugs have been used.	✓	
9	Check that the bending radius of cables is not less than the minimum established.	✓	
10	Cable markers to be installed before covering buried cables or cables in cable trays.	✓	
11	Tie wraps to be used for cable and wires fixation.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-030-T01-CPTR




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
12	Trench markers to be checked w.r.t approved documents.	✓	
13	Check cable glands for tightness and check the correct type of gland has been used for the size and type of installed cables.	✓	
14	Inspect cable laid in trenches, segregation and protection.	✓	
15	Cables to be tested (continuity/insulation resistance).(*)	✓	
16	Equipment test report and inspection certificate to be-checked.	✓	
17	Check availability of vendor documents, including commissioning and start-up instructions. (If Any)	N/A	
18	Calibration test certificate of testing equipment to be checked.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

**PRE-COMMISSIONING CHECK LIST
MEDIUM VOLTAGE CABLES
EL-31 A**

INSULATION TEST

EL-31 A

CABLE VOLTAGE LEVEL	D.C TEST VOLTAGE	MINIMUM INSULATION RESISTANCE (M.OHMS).
3.3kV	2500V	200
6.6kV & Above	5000V	200

TABLE [I]

NOTES:

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-030-T02-CPTR




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	Construction punch list to be checked.	✓	
2	Check cables are correctly fixed to trays and supports.	✓	
3	Check cables through walls or ceilings are correctly sealed.	✓	
4	Check that all cables are installed in accordance with cable lists and approved documents.	✓	
5	Check identification tags of all conductors and wires.	✓	
6	Check connection, termination and joints of cables are correctly executed.	✓	
7	Inspect cables for jacket damage.	✓	
8	Ensure that the correct size and type of crimping lugs have been used.	✓	
9	Check that the bending radius of cables is not less than the minimum established.	✓	
10	Cable markers to be installed before covering buried cables or cables in cable trays.	✓	
11	Tie wraps to be used for cable and wires fixation.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-030-T02-CPTR




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
12	Trench markers to be checked w.r.t approved documents.	✓	
13	Check cable glands for tightness and check the correct type of gland has been used for the size and type of installed cables.	✓	
14	Inspect cable laid in trenches, segregation and protection.	✓	
15	Cables to be tested (continuity/insulation resistance).(*)	✓	
16	Equipment test report and inspection certificate to be-checked.	✓	
17	Check availability of vendor documents, including commissioning and start-up instructions. (If Any)	N/A	
18	Calibration test certificate of testing equipment to be checked.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

INSULATION TEST

EL-31 A

CABLE VOLTAGE LEVEL	D.C TEST VOLTAGE	MINIMUM INSULATION RESISTANCE (M.OHMS).
3.3kV	2500V	200
6.6kV & Above	5000V	200

TABLE [I]

NOTES:

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-030-T03-CPTR




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	Construction punch list to be checked.	✓	
2	Check cables are correctly fixed to trays and supports.	✓	
3	Check cables through walls or ceilings are correctly sealed.	✓	
4	Check that all cables are installed in accordance with cable lists and approved documents.	✓	
5	Check identification tags of all conductors and wires.	✓	
6	Check connection, termination and joints of cables are correctly executed.	✓	
7	Inspect cables for jacket damage.	✓	
8	Ensure that the correct size and type of crimping lugs have been used.	✓	
9	Check that the bending radius of cables is not less than the minimum established.	✓	
10	Cable markers to be installed before covering buried cables or cables in cable trays.	✓	
11	Tie wraps to be used for cable and wires fixation.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-030-T03-CPTR




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
12	Trench markers to be checked w.r.t approved documents.	✓	
13	Check cable glands for tightness and check the correct type of gland has been used for the size and type of installed cables.	✓	
14	Inspect cable laid in trenches, segregation and protection.	✓	
15	Cables to be tested (continuity/insulation resistance).(*)	✓	
16	Equipment test report and inspection certificate to be-checked.	✓	
17	Check availability of vendor documents, including commissioning and start-up instructions. (If Any)	N/A	
18	Calibration test certificate of testing equipment to be checked.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

INSULATION TEST




EL-31 A

CABLE VOLTAGE LEVEL	D.C TEST VOLTAGE	MINIMUM INSULATION RESISTANCE (M.OHMS).
3.3kV	2500V	200
6.6kV & Above	5000V	200

TABLE [I]

NOTES:

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)			
PROJECT NUMBER : 1251-100		DISCIPLINE : Electrical	
SYSTEM NAME : Piping Cathodic Protection System		SYSTEM ID : 030-CP-001	
SUB-SYSTEM NAME : Piping Cathodic Protection System		SUB-SYSTEM ID : 030-CP-001	
ITEM TAG No. : P-030-T04-CPTR		AREA : 30	
REF. DWGs/DOCs :			
No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	Construction punch list to be checked.	✓	
2	Check cables are correctly fixed to trays and supports.	✓	
3	Check cables through walls or ceilings are correctly sealed.	✓	
4	Check that all cables are installed in accordance with cable lists and approved documents.	✓	
5	Check identification tags of all conductors and wires.	✓	
6	Check connection, termination and joints of cables are correctly executed.	✓	
7	Inspect cables for jacket damage.	✓	
8	Ensure that the correct size and type of crimping lugs have been used.	✓	
9	Check that the bending radius of cables is not less than the minimum established.	✓	
10	Cable markers to be installed before covering buried cables or cables in cable trays.	✓	
11	Tie wraps to be used for cable and wires fixation.	✓	
REMARKS AND OBSERVATIONS :			
OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.			
COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-030-T04-CPTR




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
12	Trench markers to be checked w.r.t approved documents.	✓	
13	Check cable glands for tightness and check the correct type of gland has been used for the size and type of installed cables.	✓	
14	Inspect cable laid in trenches, segregation and protection.	✓	
15	Cables to be tested (continuity/insulation resistance).(*)	✓	
16	Equipment test report and inspection certificate to be-checked.	✓	
17	Check availability of vendor documents, including commissioning and start-up instructions. (If Any)	N/A	
18	Calibration test certificate of testing equipment to be checked.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

**PRE-COMMISSIONING CHECK LIST
MEDIUM VOLTAGE CABLES
EL-31 A**

INSULATION TEST

EL-31 A

CABLE VOLTAGE LEVEL	D.C TEST VOLTAGE	MINIMUM INSULATION RESISTANCE (M.OHMS).
3.3kV	2500V	200
6.6kV & Above	5000V	200

TABLE [I]

NOTES:




PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)	
PROJECT NUMBER : 1251-100	DISCIPLINE : Electrical
SYSTEM NAME : Piping Cathodic Protection System	SYSTEM ID : 030-CP-001
SUB-SYSTEM NAME : Piping Cathodic Protection System	SUB-SYSTEM ID : 030-CP-001
ITEM TAG No. : P-030-T10-CPTR	AREA : 30
REF. DWGs/DOCs :	

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	Construction punch list to be checked.	✓	
2	Check cables are correctly fixed to trays and supports.	✓	
3	Check cables through walls or ceilings are correctly sealed.	✓	
4	Check that all cables are installed in accordance with cable lists and approved documents.	✓	
5	Check identification tags of all conductors and wires.	✓	
6	Check connection, termination and joints of cables are correctly executed.	✓	
7	Inspect cables for jacket damage.	✓	
8	Ensure that the correct size and type of crimping lugs have been used.	✓	
9	Check that the bending radius of cables is not less than the minimum established.	✓	
10	Cable markers to be installed before covering buried cables or cables in cable trays.	✓	
11	Tie wraps to be used for cable and wires fixation.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-030-T10-CPTR




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
12	Trench markers to be checked w.r.t approved documents.	✓	
13	Check cable glands for tightness and check the correct type of gland has been used for the size and type of installed cables.	✓	
14	Inspect cable laid in trenches, segregation and protection.	✓	
15	Cables to be tested (continuity/insulation resistance).(*)	✓	
16	Equipment test report and inspection certificate to be-checked.	✓	
17	Check availability of vendor documents, including commissioning and start-up instructions. (If Any)	N/A	
18	Calibration test certificate of testing equipment to be checked.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

INSULATION TEST

EL-31 A

CABLE VOLTAGE LEVEL	D.C TEST VOLTAGE	MINIMUM INSULATION RESISTANCE (M.OHMS).
3.3kV	2500V	200
6.6kV & Above	5000V	200

TABLE [I]

NOTES:

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-AG030-TR-001




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	Construction punch list to be checked.	✓	
2	Check cables are correctly fixed to trays and supports.	✓	
3	Check cables through walls or ceilings are correctly sealed.	✓	
4	Check that all cables are installed in accordance with cable lists and approved documents.	✓	
5	Check identification tags of all conductors and wires.	✓	
6	Check connection, termination and joints of cables are correctly executed.	✓	
7	Inspect cables for jacket damage.	✓	
8	Ensure that the correct size and type of crimping lugs have been used.	✓	
9	Check that the bending radius of cables is not less than the minimum established.	✓	
10	Cable markers to be installed before covering buried cables or cables in cable trays.	✓	
11	Tie wraps to be used for cable and wires fixation.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-AG030-TR-001




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
12	Trench markers to be checked w.r.t approved documents.	✓	
13	Check cable glands for tightness and check the correct type of gland has been used for the size and type of installed cables.	✓	
14	Inspect cable laid in trenches, segregation and protection.	✓	
15	Cables to be tested (continuity/insulation resistance).(*)	✓	
16	Equipment test report and inspection certificate to be-checked.	✓	
17	Check availability of vendor documents, including commissioning and start-up instructions. (If Any)	N/A	
18	Calibration test certificate of testing equipment to be checked.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

INSULATION TEST

EL-31 A

CABLE VOLTAGE LEVEL	D.C TEST VOLTAGE	MINIMUM INSULATION RESISTANCE (M.OHMS).
3.3kV	2500V	200
6.6kV & Above	5000V	200

TABLE [I]

NOTES:

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-AG030-TR-002




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	Construction punch list to be checked.	✓	
2	Check cables are correctly fixed to trays and supports.	✓	
3	Check cables through walls or ceilings are correctly sealed.	✓	
4	Check that all cables are installed in accordance with cable lists and approved documents.	✓	
5	Check identification tags of all conductors and wires.	✓	
6	Check connection, termination and joints of cables are correctly executed.	✓	
7	Inspect cables for jacket damage.	✓	
8	Ensure that the correct size and type of crimping lugs have been used.	✓	
9	Check that the bending radius of cables is not less than the minimum established.	✓	
10	Cable markers to be installed before covering buried cables or cables in cable trays.	✓	
11	Tie wraps to be used for cable and wires fixation.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-AG030-TR-002




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
12	Trench markers to be checked w.r.t approved documents.	✓	
13	Check cable glands for tightness and check the correct type of gland has been used for the size and type of installed cables.	✓	
14	Inspect cable laid in trenches, segregation and protection.	✓	
15	Cables to be tested (continuity/insulation resistance).(*)	✓	
16	Equipment test report and inspection certificate to be-checked.	✓	
17	Check availability of vendor documents, including commissioning and start-up instructions. (If Any)	N/A	
18	Calibration test certificate of testing equipment to be checked.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

INSULATION TEST

EL-31 A

CABLE VOLTAGE LEVEL	D.C TEST VOLTAGE	MINIMUM INSULATION RESISTANCE (M.OHMS).
3.3kV	2500V	200
6.6kV & Above	5000V	200

TABLE [I]

NOTES:

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-AG030-TR-003




AREA : 30

REF. DWGs/DOCs :




No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	Construction punch list to be checked.	✓	
2	Check cables are correctly fixed to trays and supports.	✓	
3	Check cables through walls or ceilings are correctly sealed.	✓	
4	Check that all cables are installed in accordance with cable lists and approved documents.	✓	
5	Check identification tags of all conductors and wires.	✓	
6	Check connection, termination and joints of cables are correctly executed.	✓	
7	Inspect cables for jacket damage.	✓	
8	Ensure that the correct size and type of crimping lugs have been used.	✓	
9	Check that the bending radius of cables is not less than the minimum established.	✓	
10	Cable markers to be installed before covering buried cables or cables in cable trays.	✓	
11	Tie wraps to be used for cable and wires fixation.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)			
PROJECT NUMBER : 1251-100		DISCIPLINE : Electrical	
SYSTEM NAME : Piping Cathodic Protection System		SYSTEM ID : 030-CP-001	
SUB-SYSTEM NAME : Piping Cathodic Protection System		SUB-SYSTEM ID : 030-CP-001	
ITEM TAG No. : P-AG030-TR-003		AREA : 30	
REF. DWGs/DOCs :			
No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
12	Trench markers to be checked w.r.t approved documents.	✓	
13	Check cable glands for tightness and check the correct type of gland has been used for the size and type of installed cables.	✓	
14	Inspect cable laid in trenches, segregation and protection.	✓	
15	Cables to be tested (continuity/insulation resistance).(*)	✓	
16	Equipment test report and inspection certificate to be-checked.	✓	
17	Check availability of vendor documents, including commissioning and start-up instructions. (If Any)	N/A	
18	Calibration test certificate of testing equipment to be checked.	✓	
REMARKS AND OBSERVATIONS :			
OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.			
COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

INSULATION TEST

EL-31 A

CABLE VOLTAGE LEVEL	D.C TEST VOLTAGE	MINIMUM INSULATION RESISTANCE (M.OHMS).
3.3kV	2500V	200
6.6kV & Above	5000V	200

TABLE [I]

NOTES:

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-AG030-TR-004




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	Construction punch list to be checked.	✓	
2	Check cables are correctly fixed to trays and supports.	✓	
3	Check cables through walls or ceilings are correctly sealed.	✓	
4	Check that all cables are installed in accordance with cable lists and approved documents.	✓	
5	Check identification tags of all conductors and wires.	✓	
6	Check connection, termination and joints of cables are correctly executed.	✓	
7	Inspect cables for jacket damage.	✓	
8	Ensure that the correct size and type of crimping lugs have been used.	✓	
9	Check that the bending radius of cables is not less than the minimum established.	✓	
10	Cable markers to be installed before covering buried cables or cables in cable trays.	✓	
11	Tie wraps to be used for cable and wires fixation.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-AG030-TR-004




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
12	Trench markers to be checked w.r.t approved documents.	✓	
13	Check cable glands for tightness and check the correct type of gland has been used for the size and type of installed cables.	✓	
14	Inspect cable laid in trenches, segregation and protection.	✓	
15	Cables to be tested (continuity/insulation resistance).(*)	✓	
16	Equipment test report and inspection certificate to be-checked.	✓	
17	Check availability of vendor documents, including commissioning and start-up instructions. (If Any)	N/A	
18	Calibration test certificate of testing equipment to be checked.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

**PRE-COMMISSIONING CHECK LIST
MEDIUM VOLTAGE CABLES
EL-31 A**

INSULATION TEST

EL-31 A

CABLE VOLTAGE LEVEL	D.C TEST VOLTAGE	MINIMUM INSULATION RESISTANCE (M.OHMS).
3.3kV	2500V	200
6.6kV & Above	5000V	200

TABLE [I]

NOTES:




PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)	
PROJECT NUMBER : 1251-100	DISCIPLINE : Electrical
SYSTEM NAME : Piping Cathodic Protection System	SYSTEM ID : 030-CP-001
SUB-SYSTEM NAME : Piping Cathodic Protection System	SUB-SYSTEM ID : 030-CP-001
ITEM TAG No. : P-AG030-TR-005	AREA : 30
REF. DWGs/DOCs :	




No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	Construction punch list to be checked.	✓	
2	Check cables are correctly fixed to trays and supports.	✓	
3	Check cables through walls or ceilings are correctly sealed.	✓	
4	Check that all cables are installed in accordance with cable lists and approved documents.	✓	
5	Check identification tags of all conductors and wires.	✓	
6	Check connection, termination and joints of cables are correctly executed.	✓	
7	Inspect cables for jacket damage.	✓	
8	Ensure that the correct size and type of crimping lugs have been used.	✓	
9	Check that the bending radius of cables is not less than the minimum established.	✓	
10	Cable markers to be installed before covering buried cables or cables in cable trays.	✓	
11	Tie wraps to be used for cable and wires fixation.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)			
PROJECT NUMBER : 1251-100		DISCIPLINE : Electrical	
SYSTEM NAME : Piping Cathodic Protection System		SYSTEM ID : 030-CP-001	
SUB-SYSTEM NAME : Piping Cathodic Protection System		SUB-SYSTEM ID : 030-CP-001	
ITEM TAG No. : P-AG030-TR-005		AREA : 30	
REF. DWGs/DOCs :			
No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
12	Trench markers to be checked w.r.t approved documents.	✓	
13	Check cable glands for tightness and check the correct type of gland has been used for the size and type of installed cables.	✓	
14	Inspect cable laid in trenches, segregation and protection.	✓	
15	Cables to be tested (continuity/insulation resistance).(*)	✓	
16	Equipment test report and inspection certificate to be-checked.	✓	
17	Check availability of vendor documents, including commissioning and start-up instructions. (If Any)	N/A	
18	Calibration test certificate of testing equipment to be checked.	✓	
REMARKS AND OBSERVATIONS :			
OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.			
COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

**PRE-COMMISSIONING CHECK LIST
MEDIUM VOLTAGE CABLES
EL-31 A**

INSULATION TEST

EL-31 A

CABLE VOLTAGE LEVEL	D.C TEST VOLTAGE	MINIMUM INSULATION RESISTANCE (M.OHMS).
3.3kV	2500V	200
6.6kV & Above	5000V	200

TABLE [I]

NOTES:




PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)	
PROJECT NUMBER : 1251-100	DISCIPLINE : Electrical
SYSTEM NAME : Piping Cathodic Protection System	SYSTEM ID : 030-CP-001
SUB-SYSTEM NAME : Piping Cathodic Protection System	SUB-SYSTEM ID : 030-CP-001
ITEM TAG No. : P-AG030-TR-006	AREA : 30
REF. DWGs/DOCs :	

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	Construction punch list to be checked.	✓	
2	Check cables are correctly fixed to trays and supports.	✓	
3	Check cables through walls or ceilings are correctly sealed.	✓	
4	Check that all cables are installed in accordance with cable lists and approved documents.	✓	
5	Check identification tags of all conductors and wires.	✓	
6	Check connection, termination and joints of cables are correctly executed.	✓	
7	Inspect cables for jacket damage.	✓	
8	Ensure that the correct size and type of crimping lugs have been used.	✓	
9	Check that the bending radius of cables is not less than the minimum established.	✓	
10	Cable markers to be installed before covering buried cables or cables in cable trays.	✓	
11	Tie wraps to be used for cable and wires fixation.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST MEDIUM VOLTAGE CABLES EL-31 A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Electrical

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : P-AG030-TR-006




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
12	Trench markers to be checked w.r.t approved documents.	✓	
13	Check cable glands for tightness and check the correct type of gland has been used for the size and type of installed cables.	✓	
14	Inspect cable laid in trenches, segregation and protection.	✓	
15	Cables to be tested (continuity/insulation resistance).(*)	✓	
16	Equipment test report and inspection certificate to be-checked.	✓	
17	Check availability of vendor documents, including commissioning and start-up instructions. (If Any)	N/A	
18	Calibration test certificate of testing equipment to be checked.	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

**PRE-COMMISSIONING CHECK LIST
MEDIUM VOLTAGE CABLES
EL-31 A**

INSULATION TEST

EL-31 A

CABLE VOLTAGE LEVEL	D.C TEST VOLTAGE	MINIMUM INSULATION RESISTANCE (M.OHMS).
3.3kV	2500V	200
6.6kV & Above	5000V	200

TABLE [I]

NOTES:

PRE-COMMISSIONING CHECK LIST IMPRESSED CURRENT / SACRIFICIAL ANODES CP-01A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Cathodic Protection

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : Cathodic Protection




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
1	INSTALLATION AS PER RELEVANT AFC DRAWINGS		
1.1	T/R's, panels and boxes location as per drawings	✓	
1.2	T/R's, panels, boxes and test posts fixation:(concrete foundation dimensions,cables entry in foundation, leveling and tightness)	✓	
2	EXTERNAL CABLES		
2.1	Cables are properly buried	✓	
2.2	Cables are in protective conduits (if required)	✓	
2.3	Cables are marked by cables markers (if required)	✓	
3	T/R (TRANSFORMER RECTIFIER)		
3.1	Oil level in the T/R	✓	
3.2	Filter is fitted with dry silica gel	✓	
3.3	Earthing cable is tightly connected	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST IMPRESSED CURRENT / SACRIFICIAL ANODES CP-01A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Cathodic Protection

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : Cathodic Protection




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
3.4	T/R and its sealing is in clean condition and dust free	✓	
3.5	T/R potentiometer is set at minimum setting or adjusted to minimum before energizing	✓	
3.6	INTERNAL CABLES:(Proper termination,Correct polarity,Tagging,Tight fixation and Cable glands and shrouds-if required)	✓	
3.7	Spare fuses and circuit cards are available-if required	✓	
4	JUNCTION BOXES (NEGATIVE AND POSITIVE JUNCTION BOXES)		
4.1	Earthing cables are tightly connected	✓	
4.2	Junction boxes and its sealing are in clean condition and dust free	✓	
4.3	Variable resistances (if any) are set at minimum setting before energizing	✓	
4.4	INTERNAL CABLES:(Proper termination,Correct polarity,Tagging,Tight fixation and Cable glands and shrouds-if required)	✓	
5	ANODES		
5.1	Type (horizontal ground bed, distributed anodes, etc.) as per the AFC drawing	✓	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST IMPRESSED CURRENT / SACRIFICIAL ANODES CP-01A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Cathodic Protection

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : Cathodic Protection




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
5.2	Anodes locations are as per the AFC drawings	✓	
6	TEST POSTS AND BOND BOXES		
6.1	Co-ordinate with the vendor to carry out checks and tests on junction boxes, test posts, bond boxes, etc. as per vendor approved procedures	N/A	
6.2	Junction boxes and its sealing are in clean condition and dust free	✓	
6.3	Check continuity between test lead cables and metallic structure	✓	
7	PHOTOVOLTAIC POWER CELLS		
7.1	Correct polarity of battery cables	N/A	
7.2	Correct level of battery electrolyte	N/A	
7.3	Spare fuses and circuit cards available	N/A	
7.4	INTERNAL CABLES:(Proper termination,Correct polarity,Tagging,Tight fixation and Cable glands and shrouds-if required)	N/A	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST IMPRESSED CURRENT / SACRIFICIAL ANODES CP-01A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)

PROJECT NUMBER : 1251-100

DISCIPLINE : Cathodic Protection

SYSTEM NAME : Piping Cathodic Protection System

SYSTEM ID : 030-CP-001

SUB-SYSTEM NAME : Piping Cathodic Protection System

SUB-SYSTEM ID : 030-CP-001

ITEM TAG No. : Cathodic Protection




AREA : 30

REF. DWGs/DOCs :

No.	DESCRIPTION	RESULT	PL
		OK/NA/PL	ITEM No.
8	TEMPORARY CATHODIC PROTECTION (if required)		
8.1	Disconnect all the temporary cathodic protection anodes before energizing	N/A	
9	INSULATING FLANGE KITS, JOINTS AND SPOOLS (if required)		
9.1	All are installed as per P&IDs; in good condition and free of sand and water	N/A	
9.2	Check continuity before and after the two sides	N/A	

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			

PRE-COMMISSIONING CHECK LIST IMPRESSED CURRENT / SACRIFICIAL ANODES CP-01A

PROJECT TITLE : EGPC Crude Oil Tank Farms Project, Agrood Area 30 (Module-01)	
PROJECT NUMBER : 1251-100	DISCIPLINE : Cathodic Protection
SYSTEM NAME : Piping Cathodic Protection System	SYSTEM ID : 030-CP-001
SUB-SYSTEM NAME : Piping Cathodic Protection System	SUB-SYSTEM ID : 030-CP-001
ITEM TAG No. : Cathodic Protection	AREA : 30

REF. DWGs/DOCs :

NATURAL POTENTIAL SURVEY :

REFERENCE TO : **CU/CUSO4** ☐ **AG/AGCI** ☐ **ZINC** ☐

ID No.	NAT. POT. (MV)	REMARKS

REMARKS AND OBSERVATIONS :

OK: NO OBJECTION, NA: NOT APPLICABLE, PL: PUNCH LIST.

COMPANY	CONST. CONTRACTOR	ENPPI	CUSTOMER
NAME			
SIGNATURE			
DATE			



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

12.11- Electrical Supplier Check Lists & Reports



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

13- Electrical Commissioning



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

13.01- Electrical -Commissioning Check Lists



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

13.02- Electrical Supplier Check Lists & Reports



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

14- Red Marked-up Drawings



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

14.01- P&ID



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

14.02- Instrumentation Drawings



Project: 01251-100
CRUDE OIL TANK FARM PROJECT (AGROOD AREA)



System ID	030-CP-001
System Description	Piping Cathodic Protection System

14.03- Electrical Drawings
